

PM MITRA TAMIL NADU

VIRUDHUNAGAR

Monthly Progress - July 2026

➤ **Core Infrastructure:**

Name of Work	Contract award Date	Name of Contractor	Status
Widening Internal Road – Forming Four Lane Road starting from NH-44 to E.Kumaralingapuram	26.10.2023	(Deposit work through State Highways Department)	100% Completed
Administrative Building for PM MITRA Park	01.03.2024	M/s. Aram Construction, Madurai	100% Completed
	23.01.2025	M/s. Shri Prakash Infra, Theni	100% Completed
	30.09.2025	M/s. Shri Prakash Infra, Theni	100% Completed
External water supply - 2.5 MLD Water from River Thamirabharani	19.06.2023	(Deposit work through Tamil Nadu Water supply and Drainage Board)	100% Completed

PM MITRA TAMIL NADU

VIRUDHUNAGAR

Monthly Progress - July 2026

Name of Work	Contract award Date	Name of Contractor	Physical completion %	Probable date of Completion
Package I – Trunk Infrastructure works, such as	27.11.2025	M/s. Ramalingam Construction Company Pvt. Ltd.,	5% Completed	April 2027
Roads, Storm water drain, canal drainage and Street light (20 Km)				
Water Supply system for all the plots				
5 MLD - Sewerage Treatment System for all the plots				
Electrical (RCC Duct) Distribution				
Streetlights and building Electrical Distribution				
Effluent collection system				
Truck Parking facility				
Amenities Buildings (health centre, crèche, etc.,)				

PM MITRA TAMIL NADU

VIRUDHUNAGAR

Monthly Progress - July 2026

➤ Supporting Infrastructure (Phase I) :

Name of Work (Phase I)	Contract award Date
Package II A - Common Effluent Treatment Plant (5 MLD) Phase I	5 MLD CETP with ZLD (on EPC mode) - Estimated Cost – Rs. 119.74 Cr - Construction period - 18 Months (Eighteen Months) - O&M - 60 Months - Bid published on - 16.03.2026 - Work orders will be issued by September 2026
Package II B Boilers (50 Ton/hr) and Solar plant (5 MW)	Tender will be published by September 2026 <i>(In discussion with key stakeholders for finalization of design and project components)</i>
Package III Workers' accommodation -3000 Beds,	Tender will be published by August 2026 <i>(In discussion with key stakeholders for finalization of design and project components)</i>
Plug and play – 4 Lakh Sq.ft, (Phase I) Warehouse – 60k Sq.ft (Phase I)	Tender will be published by August 2026 <i>(In discussion with key stakeholders for finalization of design and project components)</i>
Amenities building, Social Infrastructure buildings	Tender will be published by September 2026 <i>(In discussion with key stakeholders for finalization of design and project components)</i>
Package IV ICT works/ Integrated Command and Control centre	Tender will be published by December 2026

PM MITRA TAMIL NADU VIRUDHUNAGAR

Monthly Progress - July 2026


➤ **Proposed Buildings:**

Proposed Iconic Building Elevation:



Proposed Plug and Play Building Elevation:





PM MITRA PARK TAMIL NADU

at E. Kumaralingapuram,
Virudhunagar District, Tamil Nadu

Site Photographs
July-2026

Date:01&02-07-2026



Road NO-1,CNG Work

Road NO-1,CNG Work



Road NO-1,Outer line marking

Road NO-1,Outer line marking

Date:04-07-2026



Inspection at EE AM-6 D-ELSR-1



Road NO-1,CNG Work



Road NO-1,CNG Work

Road NO-1,CNG Work

Date:06-07-2026



R-18 C35 0+153 -Culvert Excavation work



Road NO-1,CNG Work



Road NO-1,CNG Work



R1- C7-1+745 Culvert Excavation

Date:07-07-2026



R-18 C35 0+153 -Culvert Excavation work

R-18 C35 0+153 -Culvert Excavation work



Road NO-1,CNG Work

Road NO-1,CNG Work

Date:08-07-2026

 8 Jul 2026 4:53:53 pm 9.4309N 77.9149E 269° W Maniparaipatti Kumaralingapuram Tamil Nadu Altitude:-11.2msnm Speed:0.6km/h Index number: 428	 8 Jul 2026 5:07:45 pm 9.4308N 77.9145E 287° W Chennai - Villupuram - Trichy - Kanyakumari Road Maniparaipatti Kumaralingapuram Tamil Nadu Altitude:- 13.5msnm Speed:0.1km/h Index number: 430
R-16 CNG Work	R-16 CNG Work & Grading
 8 Jul 2026 4:53:56 pm 9.4309N 77.9149E 270° W Maniparaipatti Kumaralingapuram Tamil Nadu Altitude:-8.5msnm Speed:0.6km/h Index number: 429	 8 Jul 2026 5:07:47 pm 9.4308N 77.9145E 289° W Chennai - Villupuram - Trichy - Kanyakumari Road Maniparaipatti Kumaralingapuram Tamil Nadu Altitude:-13.5msnm Speed:0.6km/h Index number: 431
R-16 CNG Work	R-16 CNG Work

Date:09-07-2026



R-16 CNG Work

R-16 CNG Work



R-16 CNG Work

R-16 CNG Work

Date:10-07-2026



R-16 CNG Work

R-16 CNG Work



R-16 CNG Work

R-16 CNG Work

Date:11-07-2026



AM-6 D-ELSR-1 Steel Cutting work



AM-6 D-ELSR-1 Steel Cutting work



AM-6 D-ELSR-1 Steel Cutting work



AM-6 D-ELSR-1 Steel Cutting work

Date:12-07-2026



AM-6 D-ELSR-1 PCC Pouring work

AM-6 D-ELSR-1 PCC Pouring work



AM-6 D-ELSR-1 PCC batching plant

M-6 D-ELSR-1 PCC Bed Preparation & Compaction work

Date:13-07-2026



R-16 CNG Work

R-16 CNG Line Marking



R-16 CNG Work

AM-6 F-ELSR-1 PCC Bed Sand Filling Work

Date:14.07.2026 – PD Visit



PD Inspection at R-1 Road CNG Work





PD Inspection at D-ELSR black soil depth checking



PD Inspection at steel Checking


R-16 OSR Land Inspection

Date:14.07.2026 – PD Visit

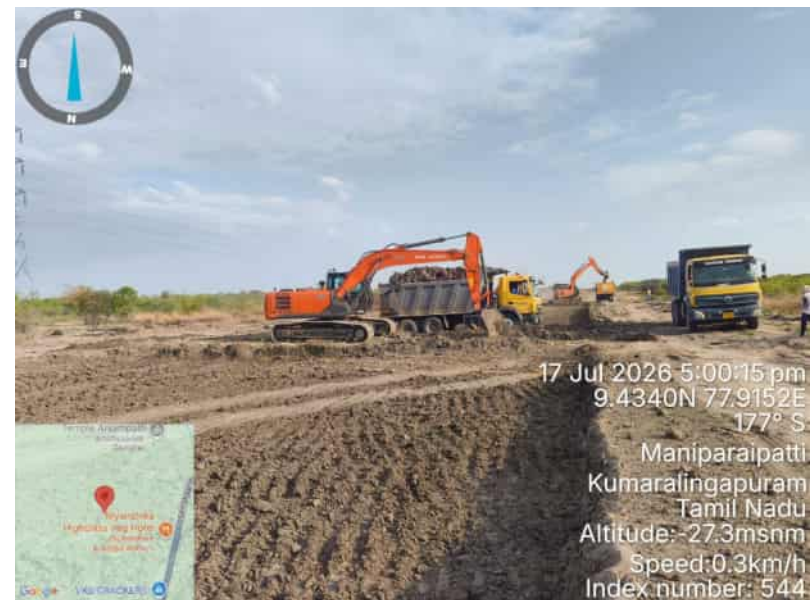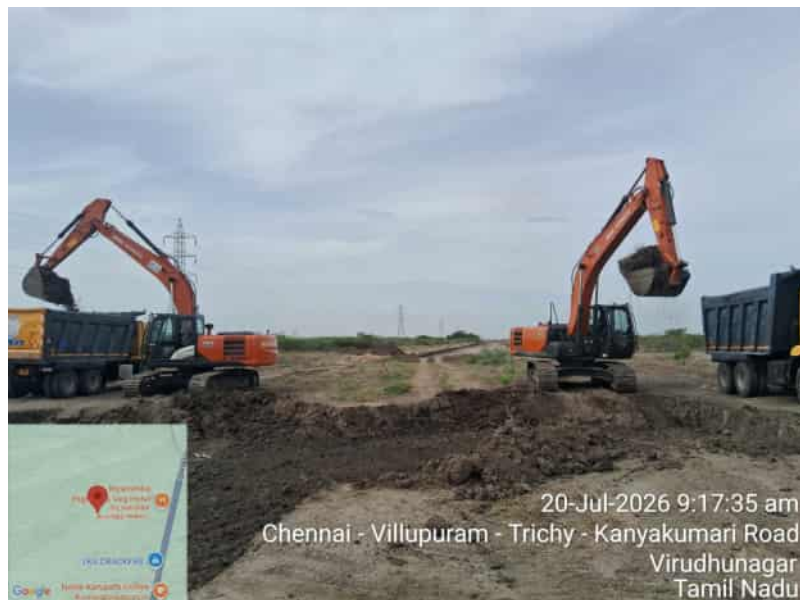

R-1 CNG Work

R-1 CNG Work

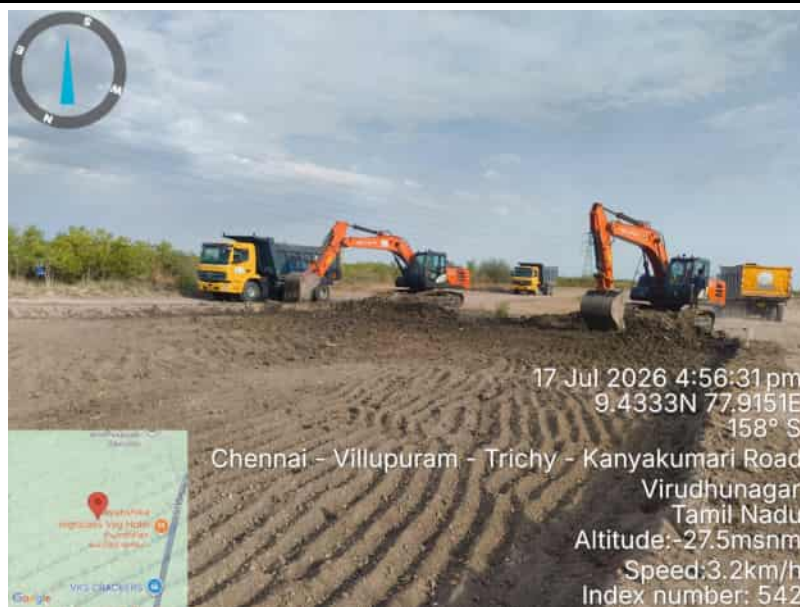


R-1 CNG Work

AM-6 F-ELSR-1 PCC Bed Sand Filling Work

Date:15.07.2026

 15 Jul 2026 6:47:29 pm 9.4151N 77.8983E 259° W Etturvattam Tamil Nadu	 15 Jul 2026 6:47:38 pm 9.4151N 77.8983E 233° SW Etturvattam Tamil Nadu
AM-6 F-ELSR PCC Pouring work	AM-6 F-ELSR PCC Pouring work
 15 Jul 2026 6:47:57 pm 9.4150N 77.8983E 190° S Unnamed Road Virudhunagar Tamil Nadu	 Virudhunagar, Tamil Nadu, India Tamil Nadu 626203, India, Virudhunagar, Tamil Nadu 626203, India Lat 9.415952° Long 77.899284° Wednesday, 15/07/2026 10:20 AM GMT +05:30
AM-6 F-ELSR PCC Pouring work	AM-6 D-ELSR PCC curing work

Date:16-07-2026

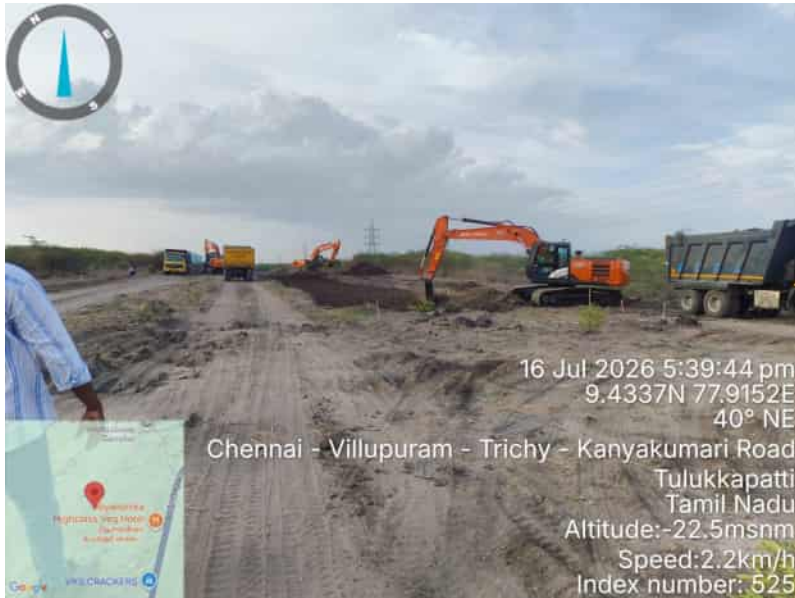

R-1 CNG work

R-1 C2 0+430 Culvert marking



R-1 CNG work

R-1 CNG work

Date:17-07-2026



R-16 C31 0+054 Culvert EW completed


R-16 C31 0+054 Culvert EW completed



R-1 CNG WORK

R-1 CNG WORK

Date:18-07-2026

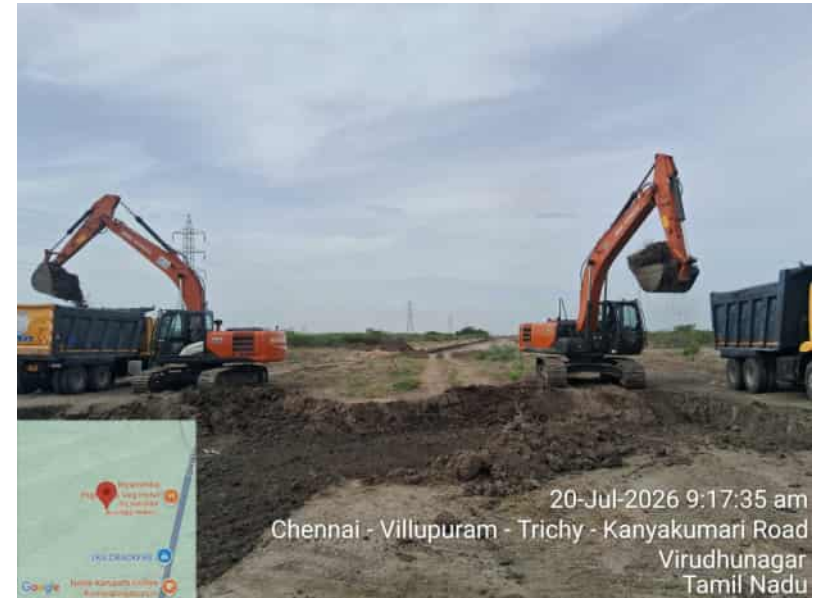

AM-6 D_ELSR Footing Reinforcement tying work

R-1 CNG Work



R-1 CNG Work

Ins[ection at F-ELSR-1 Sand filling Checking

Date:22-07-2026



AM-6 0.7 ML L-ELSR SPT Test



AM-5 0.5 ML D-ELSR SPT Test



AM-5 0.5 ML D-ELSR SPT Test Sample Collection



Road No-1 C-8 0+945 Culvert pcc Bottom Section work.

Date:22-07-2026

 22-Jul 2026 12:19:28 pm 9.428809080272913N 77.90371712297201E 106° E Kumaralingapuram Tamil Nadu Altitude:-12.0msnm Speed:0.0km/h Index number: 15	 22 Jul 2026 12:19:06 pm 9.428812600672245N 77.90371896699071E 130° SE Kumaralingapuram Tamil Nadu Altitude:-12.0msnm Speed:0.3km/h Index number: 14
AM-6 D-ELSR PCC Cube Compression test	AM-6 D-ELSR PCC Cube weight test
 22 Jul 2026 10:46:49 am 9.4211N 77.9149E 181° S Maniparaipatti, Naduvaipatti Post National Highway 44 Maniparaipatti Kumaralingapuram Tamil Nadu Altitude:-28.0msnm Speed:1.2km/h Index number: 554	 22 Jul 2026 10:57:26 am 9.4239N 77.9139E 288° W Maniparaipatti Kumaralingapuram Tamil Nadu Altitude:-14.0msnm Speed:0.3km/h Index number: 557
R-18 C35 0+153 PCC Bed Preparation work	R-1,C-6 1+563 PCC Bed Preparation work

Date:22-07-2026



PO MAAM inspection AM-6 D-ELSR-1

PO MAAM inspection AM-6 D-ELSR-1



PO MAAM inspection AM-6 D-ELSR-1

PO MAAM inspection AM-6 D-ELSR-1

Date:23-07-2026



R-1 C-7 1+745 PCC Laying work



Slump Cone Casted Work



R-1 C-7 1+745 PCC Laying work



AM-6 D-ELSR PCC Cube weight test

Date:24-07-2026



R-16 C-31 0+054 Culvert PCC Bed preparation



PO & EE Maam Inspection R-1 C-7 1+745 PCC



PO & EE Maam Inspection R-1 C-6 1+563 PCC
Laying



PO & EE Maam Inspection R-18 C35 0+153 PCC
Bed preparation

Date:25-07-2026



R-2 C-10 0+400 PCC Laying work



R-2 C-10 0+400 PCC Laying work



R-16 C-31 PCC Laying work



R-1 C7 1+745 Raft Reinforcement Tying

Date:27-07-2026



R-2 C10 0+400 PCC Curing work

R-10 CNG Work



AM-6 D-ELSR-1 Footing Tying work

OSR-25 Top black Soil Removal work

Date:27-07-2026



OSR-25 Top black Soil Removal work

OSR-25 Top black Soil Removal work



OSR-25 Top black Soil Removal work

AM-6 D-ELSR-1 Footing Tying & Shuttering work

Date:28-07-2026

 28 Jul 2026 11:10:45 am 9.416057104244828N 77.89939055219293E 159° S Unnamed Road Virudhunagar Tamil Nadu Altitude: 2.0msnm Speed: 0.2km/h Index number: 36	 28 Jul 2026 11:11:04 am 9.416013266891241N 77.89955575197041E 244° SW Unnamed Road Virudhunagar Tamil Nadu Altitude: 6.0msnm Speed: 0.7km/h Index number: 37
AM-6 D-ELSR-1 Footing Tying & Shuttering work	AM-6 D-ELSR-1 Footing Tying & Shuttering work
 28 Jul 2026 4:01:21 pm 9.4137N 77.9044E 56° NE Chennai - Villupuram - Trichy - Kanyakumari Road Muthulingapuram Tamil Nadu	 28 Jul 2026 4:10:26 pm 9.4274N 77.9028E 267° W Sattur Tamil Nadu Altitude: -18.0msnm Speed: 0.5km/h Index number: 573
OSR-25 Black Soil Removal work	R-20 C38 PCC Bottom Level Checking


Date:28-07-2026



R-20 C38 PCC Side Shuttering Work



R-20 C38 PCC Laying work

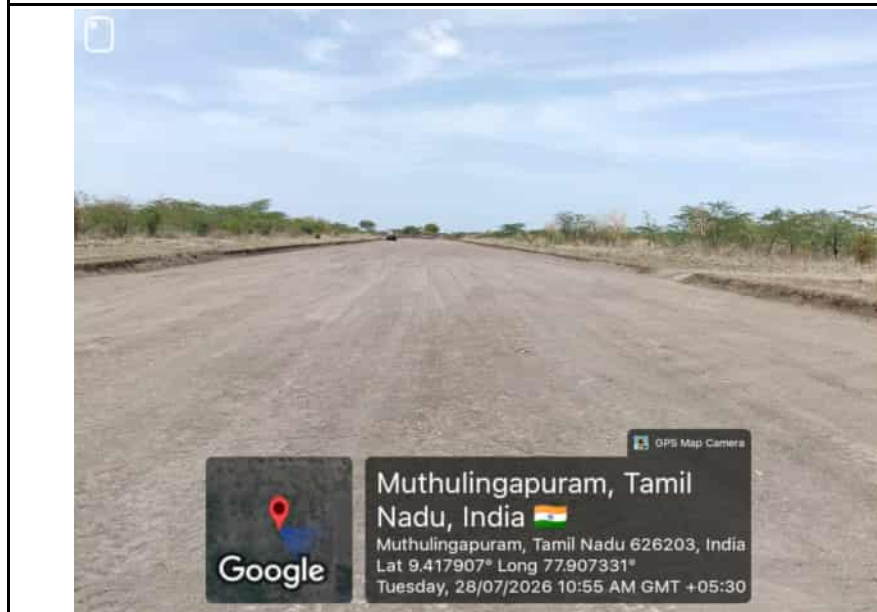

R-2 1240 Bed Compaction work



R-1 1+945 PCC Curing Work

Date:29-07-2026



R-2 CH-1220 FDT test Cheking

R-2 CH-1220 FDT test Cheking



R-2 CH-1220 Embankment Soil Filling work

R-2 CH-1220 Embankment Soil Filling work

Date:30-07-2026



R-1 1+745 C-7 Culvert Reinforcement Work

R-1 1+745 C-7 Culvert Reinforcement Work



AM-6 D-ELSR-1 Footing Shuttering work

AM-6 D-ELSR-1 Footing Shuttering work

Date:31-07-2026



R-1 1+745 C-7 PO MAAM Inspection

R-2 Embankment Soil Dumping



R-1 1+745 C6 Level Checking

R-8 CH-560 FDT Test Conducted



Thank you
