



EC/Vaipur_Mathur/HYC/June/2025

To,
The Member Secretary,
State Level Environment Impact Assessment Authority,
Chennai Metro Rail Limited (Head office),
No.327, Anna Salai, Nandanam,
Chennai - 600 035.

Sir/Madam,

Sub: SIPCOT Industrial Park at Vaipur Mathur – Submission of Half Yearly Compliance Report for June 2025 (i.e., for the period of October 2024 to March 2025) - Reg.

Ref: EC vide Letter No. SEIAA/TN/F-662/EC/8(b)/385/2012 dt.01.04.2015

We hereby submit the Half Yearly Compliance Report for the Development of Industrial Park at Vaipur, Mathur, Perinjambakkam Villages, Sriperumpudur Taluk, Kancheepuram District, Tamil Nadu for June 2025 (i.e., for the period of October 2024 to March 2025) along with the supporting documents for your perusal.

Thanking you

Yours faithfully,

(PROJECT MANAGEMENT)

Date: 30.05.2025

Encl: As above.

Copy to:

The Director,
 The Ministry of Environment and Forest & Climate Change,
 Integrated Regional Office,
 1st Floor, Additional Office Block for GPOA,
 Shastri Bhawan, Haddows Road,
 Nungambakkam, Chennai – 600 006

 The Director, CPCB Zonal Office, 77-A, South Avenue Road, Ambattur Industrial Estate, Ambattur Taluk, Thiruvallur District, Chennai - 600 058.

P.T.O.

State Industries Promotion Corporation of Tamil Nadu Limited

(A Government of Tamil Nadu Undertaking)





- 3. The Chairman, Tamil Nadu Pollution Control Board, No-76, Mount Road, Guindy, Chennai-600 032
- 4. The Project Officer SIPCOT Industrial Park, Oragadam.

State Industries Promotion Corporation of Tamil Nadu Limited

CIN I U74999TN1971SGC005967

Regd. Office: 19-A, Rukmani Lakshmipathy Road, Post Box No. 7223, Egmore, Chennai - 600 008.

Phone: 4526 1777, Fax: 4526 1796 Website: www.sipcot.tn.gov.in

HALF YEARLY ENVIRONMENTAL CLEARANCE COMPLIANCE REPORT

For the period of October 2024 to March 2025

for

"Development of Industrial Park"

at

Vaipur, Mathur, Perinjambakkam Villages, Sriperumpudur Taluk, Kancheepuram District, Tamil Nadu.

EC OBTAINED Vide Letter No. SEIAA/TN/F-662/EC/8(b)/385/2012 dt.01-04-2015

Submitted by



M/S. STATE INDUSTRIES PROMOTION CORPORATION OF TAMILNADU LTD

19/A, Rukmani Lakshmipathy Road, Egmore, Chennai- 600008.

Prepared by



ENVIRONMENTAL CONSULTANT
HUBERT ENVIRO CARE SYSTEMS (P) LTD CHENNAI

MAY 2025

TABLE OF CONTENTS

S.No	Table of Content	ts Page No
1.	Project details	4
2.	Location map	5
3.	Site photographs	6
4.	Six-month environmental clearance statement	8
	Environmental Monitoring Details	18
	5.1 Ambient air quality monitoring	18
5.	5.2 Ambient noise level monitoring	18
3.	5.3 Soil Quality monitoring	18
	5.4 Ground water quality monitoring	18
	5.5 Surface water quality monitoring	18
6.	Conclusion	19


LIST OF ANNEXURE

S. No	List of Annexure
Annexure 1	Copy of Environmental Clearance
Annexure 2	Consent To Establishment from TNPCB
Annexure 3	CMWSSB Approval letter
Annexure 4	Environmental Monitoring Reports
Annexure 5	Newspaper Advertisement
Annexure 6	Screenshot of EC copy uploaded in website
Annexure 7	Screenshot of compliance report uploaded in Website
Annexure 8	Environment Cell Roles and Responsibilities
Annexure 9	Acknowledgement from TNPCB on submission of Form V
Annexure 10	Environmental Monitoring Photos
Annexure 11	Storm water drain photograph
Annexure 12	Road photographs
Annexure 13	Solid waste management area photographs


1. PROJECT DETAILS


Name of the Project	Vaipur Mathur Industrial Park	
Name of the Proponent	State Industries Promotion Corporation of Tamil Nadu Ltd	
Location	Vaipur, Mathur and Perinjambakkam village, Sriperumpudur Taluk, Kancheepuram District, Tamil Nadu.	
EC. No	SEIAA/TN/F-662/EC/8(b)/385/2012 Dated: 01.04.2015 (Enclosed as Annexure-1)	
Total Plot Area	616 acres	
Water Requirements	Water requirement during Operation Phase - 4.5 MLD met from CMWSSB. CMWSSB letter is enclosed as Annexure 3 .	
Project Cost	Rs.126.50 Crores	


2. LOCATION MAP

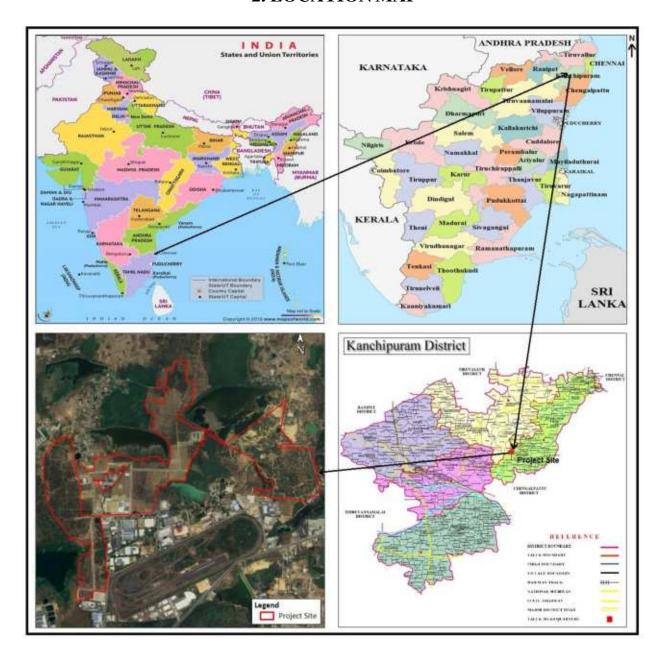

3. SITE PHOTOGRAPHS

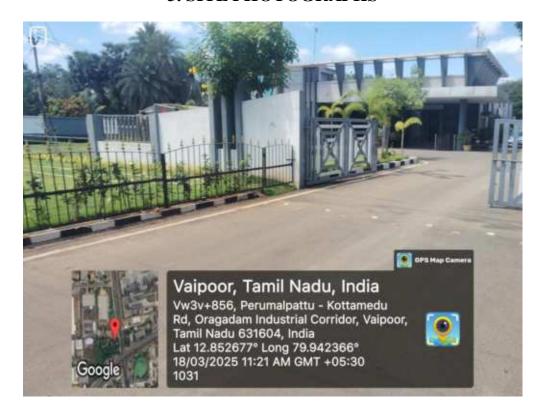

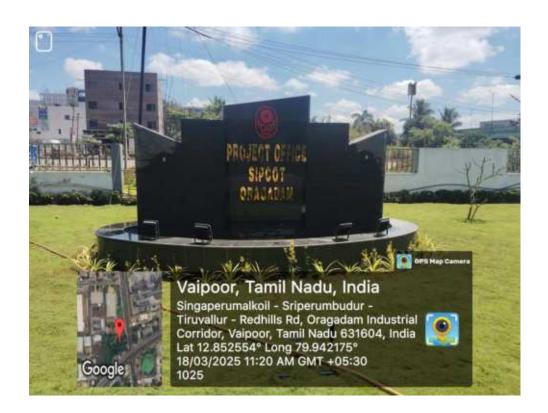

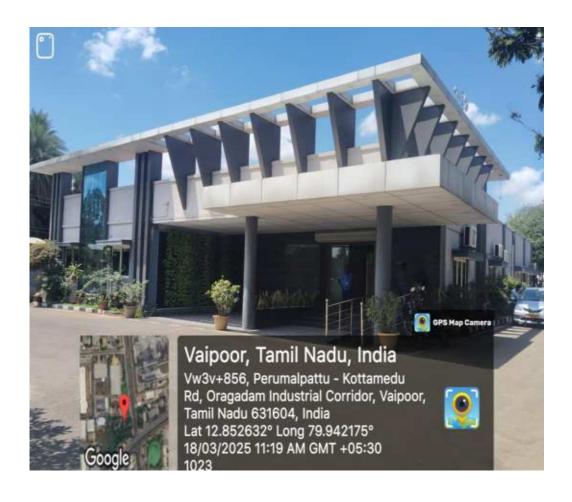



4. SIX MONTHLY ENVIRONMENTAL CLEARANCE COMPLIANCE STATEMENT

PART A- SPECIFIC CONDITIONS

I. Construction Phase

S.NO	EC CONDITIONS	STATUS OF COMPLIANCE
i.	"Consent for Establishment" shall be obtained	Condition complied.
	by SIPCOT as well as by all member industries	Consent for Establishment has been obtained
	from the Tamil Nadu Pollution Control Board	from TNPCB.
	and a copy shall be submitted to the SEIAA,	CTE copy is enclosed as Annexure -2.
	Tamil Nadu before taking up of any	
	construction activity at the site.	
ii.	SIPCOT shall not alter, change or reroute	Condition Noted.
	the natural course of the water bodies either	
	partly or wholly and shall ensure to take every	
	precautionary steps to keep the alignment,	
	direction of flow, size etc of the water bodies to	
	have its natural and smooth passage in	
	existence over year.	
iii.	SIPCOT shall ensure that any	Condition Noted.
	construction/development activity shall not	Storm water drainage photograph is
	change or alter the course of storm water	enclosed as Annexure- 11.
	flow either directly or indirectly and shall	
	ensure that every precautionary step shall be	
	taken to ensure the natural existence of	
	waterways with respect to the nearby lakes.	
iv.	SIPCOT shall mandated that all member units	Condition Noted. All the member industries
	provide complete closed pipeline system for the	will be mandated to adopt Zero Liquid
	collection, storage and Reuse systems for the	Discharge system and to handle the
	treated sewage/trade effluent generated from	domestic wastewater as per the TNPCB /
	the individual industry with provisions to	CPCB Norms.
	ensure regular treated sewage effluent sample	
	collection periodically from all the individual	
	industries to ensure the degree of treatment	
	and also to ensure complete compliance of the	
	standards prescribed by the TNPCB.	

v.	SIPCOT shall mandated that the member units	Condition complied.
	should be commissioned only after securing	Water supply letter from CMWSSB is
	water supply connection from the CMWSSB by	enclosed as Annexure- 3.
	SIPCOT.	

SIPCOT shall adhere the following conditions and also mandated to all its member units to adhere the conditions

S.NO	EC CONDITIONS	STATUS OF COMPLIANCE
1.	The excavated earth / construction debris must	Condition is being complied.
	be used within the premises only.	Excavated soil/ construction debris are used
		for greenbelt development within the project
		premises.
2.	The solid waste in the form of excavated earth	Condition noted.
	excluding the topsoil scientifically utilized for	Road photograph is enclosed as annexure -
	approach road and peripheral roads	12
	constructions.	
3.	All the topsoil excavated during construction	Condition is being complied.
	activities should be stored for use in	Top soil excavated during construction phase
	horticulture/landscape development within the	is reused for greenbelt development within
	project site.	the project premises.
4.	Disposal of other construction debris during	Condition is being complied.
	construction phase should not create any adverse	
	effect on the neighboring communities and be	
	disposed of only in approved sites with the	
	approval of competent authority with necessary	
	precautions for general safety and health aspects	
	of people.	
5.	Adequate potable drinking water and sanitary	
	facilities should be provided for construction	Drinking water and sanitary facilities are
	workers at the site. The safe disposal of	provided for the construction workers at the
	wastewater and solid wastes generated during	site
	the construction phase should be ensured.	
6.	All required sanitary and hygienic, measures	Condition noted.
	should be in place before starting construction	
	activities arid they have to be maintained	
	throughout the construction phase.	

7.	For disinfection of waste-water, system using	Condition noted.
	ultra violet radiation shall be adopted.	
8.	For Solid-waste management, composting	Condition noted. All the member units will
	arrangements shall be provided for	be instructed to follow applicable rules and
	biodegradable waste at site.	guidelines.
		Solid waste management is enclosed as
		annexure -13
9	The e - waste generated shall be handed over to	Condition noted. All the member units will
	the authorized recyclers.	be instructed to follow applicable rules and
		guidelines.
10.	All the labourers to be engaged for construction	Condition will be complied.
	should be screened for health and adequately	
	treated before and during their employment on	
	the work at the site.	
11.	A First Aid Room shall be provided with	Condition Noted.
	qualified personnel during operation of the	
	project.	
12.	Disposal of muck, generated during the	Not applicable. This is an infrastructure
	construction phase should be so managed as not	development project involving activities such
	to create any adverse effect on the neighboring	as road construction, storm water drains,
	areas and communities and be disposed of only	street lighting, and greenbelt development.
	in approved sites with the approval of the	No significant muck generation is involved
	concerned local body with necessary	that would require disposal at approved sites.
	precautions for general safety and health	
	aspects of people.	
13.	Soil and ground water samples shall be tested to	Condition is being complied.
	ascertain that there is no threat to ground water	Soil and ground water quality report and
	quality by leaching heavy metals and other	monitoring photograph are enclosed as
	toxic contaminants.	Annexure – 4 & annexure 10
14.	Construction spoils and spills including	Condition Noted.
	bituminous materials and other hazardous	
	materials must not be allowed to contaminate	
	water courses. The dump sites for such	
	materials must be impervious so that they do	
	not leach into the ground water.	
15.	No ground water shall be drawn with in	Condition is being complied.
	SIPCOT area for construction period.	
16.	Vehicles hired for bringing construction	Condition is being complied.

	materials to the site should be in good operable	
	condition and should conform to air and noise	
	emission standards, prescribed by	
	TNPCB/CPCB. The vehicles should be	
	operated only during non-peak hours.	
17.	Ambient air and noise level should conform to	Condition is being complied.
17.	residential standards prescribed by the TNPCB	Air and Noise monitoring report and
	•	
	both during day and night Incremental pollution	
	loads on the ambient air and noise quality	Annexure- 4 & annexure-10
	should be closely monitored during	
	construction phase and results of monitoring	
	shall be furnished to the Tamil Nadu Pollution	
	Control Board by recording base-lined date of	
	recent origin. Adequate. measures to reduce air	
	and noise pollution during construction shall be	
	adopted, conforming to the norms prescribed by	
	the TNPCB on noise limits.	
18.	Building materials composed wholly or partly	Condition Noted.
	of fly Ash should be used in the construction	Individual industries shall comply with.
	activities as per the provision of Fly ash	
	Notification of September, 1999 as amended in	
	August, 2003.	
19.	Ready mixed concrete must be used in building	Condition Noted.
	construction.	
20.	Storm water control and its reuse shall be as	Condition Noted.
	per CGWB and BIS standards for various	
	applications.	
21.	Water demand during construction should be	Condition Noted.
	reduced by use of premixed concrete, curing	
	agents and other best practices prevalent.	
22.	Fixtures for showers, toilet flushing and	Condition noted.
	drinking water should be of low flow type by	Individual industries shall comply with.
	adopting the use of aerators / pressure reducing	
	devices / sensor based control.	
23.	Use of glass may be reduced by up to 40% to	Condition noted.
	reduce the electricity consumption load on air	Individual industries shall comply with.
	conditioning. If necessary, high quality double	
	glass with special reflecting outside coating	

	shall be used for windows.	
24.	Roof should be designed to meet prescriptive	Condition noted.
	requirement of Energy Conservation Building	Individual industries shall comply with.
	Code (ECBC) by the use of appropriate thermal	
	insulation material.	
25.	Opaque wall should be made to meet	Condition will be complied.
	prescriptive requirement as per Energy	Individual industries shall comply with.
	Conservation Building Code which is	
	mandatory for all air conditioned spaces by	
	use of appropriate thermal insulation material.	
26.	Proper approach road for fire fighting vehicles	Condition complied.
	and for rescue operations in the event of	
	emergency shall be provided.	
27.	Adequate fire protection equipments and rescue	Condition Noted.
	arrangements should be made.	All the member units shall comply with.
28.	A separate cell shall be formed and kept in	Condition noted.
	readiness with suitable trained personnel for	
	handling of fire fighting equipments/	
	operations.	
29.	Design of buildings should be in conformity	Condition noted.
	with the Seismic Zone Classification.	
30.	All Energy Conservation Building Code	Condition noted.
	(ECBC) norms shall be adopted.	
31.	Rubber padding to absorb noise while loading	Condition noted. All member units will be
	& unloading operation should be provided.	advised to comply with.
32.	The probable date of commissioning of the	Condition Noted.
	project supported with necessary bar charts	
	shall be furnished to the SEIAA. Tamil Nadu	
33.	SIPCOT shall conduct EIA study for one	Condition complied.
	season excluding rainy season for all	Water, air, noise, wastewater etc are
	parameters such as Water, air, noise, waste	monitored and being submitted to SEIAA.
	water etc and submit to SEIAA before	Environmental monitoring report and
	March2014.	monitoring photographs are enclosed as
		Annexure 4 & annexure 10

PART –B GENERAL CONDITIONS (Construction and Operation stage)

S.NO	EC CONDITIONS	STATUS OF COMPLIANCE

i.	It is mandatory for the Project proponent to	Condition is being complied.
	furnish to the SEIAA, Half yearly compliance	Half Yearly compliance report is being
	report in Hard and Soft copies on 1st June and	submitted to the SEIAA periodically.
	1st December of each calendar year in respect	Screenshot of the previous Half Yearly
	of the conditions stipulated in the prior	compliance report is uploaded in the portal
	Environmental Clearance.	is enclosed as Annexure 7.
ii.	In the case of any change(s) in the scope of	Condition noted.
	the project or in the product mix, a fresh	There is no change in scope of the project.
	appraisal by the SEAC/SEIAA shall be	
	obtained	
iii.	The SEIAA reserves the right to add	Condition noted.
	additional safeguard measures/ subsequently,	
	if found non compliance of EC conditions	
	and to take action including revoking of this	
	Environmental Clearance as the case may be.	
iv.	All other statutory clearances such as the	Condition is being complied.
	approvals for storage of diesel from Chief	All the member industries are
	Controller of Explosives, Fire and Rescue	mandated to obtain all necessary statutory
	Services Department, Civil Aviation	clearances and approvals from the competent
	Department, Forest Conservation Act, 1980	authority.
	and Wild Life (protection) Act, 1972, State /	
	CMW SSB, Coastal Regulatory Zone	
	Authority, other statutory and other authorities	
	as applicable to the project shall be obtained	
	by project proponent from the competent	
	authorities	
v.	The project authorities should advertise with	Condition complied.
	basic details at least in two local newspaper	We, SIPCOT have advertised in two local
	widely circulated, one of which shall be in the	newspapers in Tamil and English that we
	vernacular language of the locality concerned,	have obtained Environmental clearance
	within 7 days of issue of clearance and a copy	from SEIAA /TN along with the details of
	of the clearance letter is available with the	SEIAA website where it is displayed.
	State Pollution Control Board and also at	Newspaper advertisement is enclosed as
	website of SEIAA, TN and a copy of the	
	same should be forwarded to the Regional	Annexure – 5.
	Office of the MoEF located at Chennai.	

vi.	Under the provisions of Environment	Condition noted.
, , , , , , , , , , , , , , , , , , , 	(Protection) Act, 1986, legal action shall be	Condition noted.
	initiated against the project proponent, if it	
	was found that Construction of the project has	
	been started without obtaining Environmental	
	Clearance, and for action for any violation of	
	any condition stipulated in the Environmental	
	Clearance.	
vii.	The proponent shall upload the status of	Condition is being complied.
	compliance of the stipulated EC conditions,	We uploaded the status of compliance of
	including results of monitored data on their	the stipulated EC conditions, including
	website and shall update the same	results of monitored data on our website and
	periodically. It shall simultaneously be sent to	updated the same periodically. It is
	the Regional Office of MoEF, Bengaluru, the	simultaneously sent to the concerned
	respective Zonal Office of CPCB, Bengaluru	authority. Screenshot of compliance report
	and the TNPCB. The criteria pollutant levels	including monitoring results uploaded in the
	namely SPM, RSPM, S02, NOx (ambient	website is enclosed as Annexure -7 .
	levels as well as stack emissions) or critical	
	sectoral parameters, indicated for the project	
	shall be monitored and displayed at a	
	convenient location near the main gate of the	
	company in the public domain.	
viii.	A copy of the clearance letter shall be sent by	Condition complied.
	the proponent to the Block Development	A copy of the Environmental clearance
	Officer and the Local NGO, if any, from	letter has been submitted to the block
	whom suggestions /representations, if any,	development officer by the SIPCOT and
	have been received while processing the	Environmental clearance letter has been
	proposal. The clearance letter shall also be	uploaded on website . Same is enclosed as
	put on the website of the proponent.	Annexure -6.
ix.	Personnel working in dusty areas should	Condition Noted. All the member units
	wear protective respiratory devices and they	shall comply with.
	should also be provided with adequate training	
	and information on safety and health aspects.	
	Occupational health surveillance program of	
	the workers should be undertaken periodically	
1		
	to observe any contractions due to exposure	
	to observe any contractions due to exposure to dust and take corrective measures, if	

needed

X.	Periodical medical examination of the workers	Condition Noted.
	engaged in the project shall be carried out and	
	records maintained. For the purpose, schedule	
	of health examination of the workers should	
	be drawn and followed accordingly. The	
	workers shall be provided with personnel	
	protective measures such as masks, gloves,	
	boots etc.	
xi.	A separate environmental management cell	Condition complied.
	with suitable qualified personnel should be	A separate environmental management cell
	set-up under the control of a Senior Executive,	has been assigned and will report to the
	who will report directly to the Head of the	General Manager, SIPCOT who will report
	Organization.	directly to the Head of the Organization for
		implementation monitoring and compliance
		of the environmental safeguards.
		Details of Environment cell with Roles and
		responsibilities are enclosed as Annexure –
		8.
xii.	The funds earmarked for environmental	Condition Noted.
	protection measures should be kept in	
	separate account and should not be diverted	
	for other purpose. Year wise expenditure	
	should be reported to the Ministry of	
	Environment and Forests and its Regional	
	Office located at Chennai.	
xiii.	The Regional Office of the Ministry located	Condition Noted.
	at Chennai shall monitor compliance of the	
	stipulated conditions. The project authorities	
	should extend full cooperation to the officer	
	(s) of the Regional Office by furnishing the	
	requisite data / information / monitoring	
	reports.	
xiv.	The project proponent shall submit six	Condition is being complied.
A1 V .	monthly reports on the status of compliance of	Six monthly reports on the status of
		compliance of the stipulated environmental
	•	
	conditions including results of monitored data	clearance conditions including results of
	(both in hard copies as well as by e-mail) to	monitored data is submitted to the
	the Ministry of Environment and Forests, its	concerned authority and upload copy is

	Regional Office Chennai, the respective Zonal	enclosed as Annexure 7
	Office of Central Pollution Control Board,	cherosed as rame are r
	SEIAA, TN and the State Pollution Control	
	Board.	
VV	The environmental statement for each	Condition is being complied
XV.		Condition is being complied.
	financial year ending 31st March in Form-V	
	as is mandated to be submitted by the project	The environmental statement for each
	proponent to the concerned State Pollution	financial year ending 31st March in Form-
	Control Board as prescribed under the	V as is mandated to be submitted to
	Environment (Protection) Rules, 1986, as	TNPCB and Acknowledgement for
	amended subsequently, shall also be put on	submission of Form – V to TNPCB is
	the website of the company along with the	enclosed as Annexure – 9 .
	status of compliance of environmental	
	clearance conditions and shall also be sent to	
	the Regional Office of the Ministry of	
	Environment and Forests, Chennai by e-mail.	
xvi.	The Environmental Clearance does not	Condition Noted.
	absolve the applicant/proponent of his	
	obligation/requirement to obtain other	
	statutory and administrative clearances from	
	other statutory and administrative authorities.	
kvii.	This Environmental Clearance does not imply	Condition noted.
	that the other statutory / administrative	
	clearances shall be granted to the project by	
	the concerned authorities. Such authorities	
	would be considering the project on merits	
	and be taking decisions independently of the	
	Environmental Clearance.	
viii.	The SEIAA, TN may alter/modify the above	Condition noted.
	conditions or stipulate any further condition	
	in the interest of environment protection.	
xix.	The SEIAA, TN may cancel the	Condition noted.
	environmental clearance granted to this	
	project under the provisions of EIA	
	Notification, 2006, if, at any stage of the	
	validity of this environmental clearance, if it	
	is found or if it comes to the knowledge of	
	this SEIAA, TN that the project proponent has	
	and other, 11, that the project proponent has	

	deliberately concealed and/or submitted false	
	or misleading information or inadequate data	
	for obtaining the environmental clearance.	
xx.	Failure to comply with any of the conditions	Condition Noted.
	mentioned above may result in withdrawal	
	of this clearance and attract action under	
	the provisions of the Environment	
	(Protection) Act, 1986.	
xxi.	The above conditions will be enforced inter-	Condition complied.
	alia, under the provisions of the Water	CTE is obtained from TNPCB.
	(Prevention & Control of Pollution) Act,	CTE copy is enclosed as Annexure -2.
	1974, the Air (Prevention & Control of	
	Pollution) Act, 1981, the Environment	
	(Protection) Act, 1986, the Public Liability	
	Insurance Act, 1991, along with their	
	amendments ,draft Minor Mineral	
	Conservation & Development Rules, 2010	
	framed under MMDR Act 1957, National	
	Commission for protection of Child Right	
	Rules ,2006 and rules made there under	
	and also any other orders passed by the	
	Hon'ble Supreme Court of India / Hon'ble	
	High Court of Madras and any other Courts of	
	Law relating to the subject matter.	
xxii.	Any appeal against this environmental	Condition noted.
	clearance shall lie with the National Green	No appeal lies against this Environmental
	Tribunal, if preferred, within a period of 30	Clearance, till date.
	days as prescribed under section 16 of the	
	National Green Tribunal Act, 2010.	

5. ENVIRONMENTAL MONITORING DETAILS

It is mandatory to submit six- monthly EC compliance report (Half yearly Compliance) to MoEF & CC Regional Office by the proponent. For the purpose of submitting Six-Monthly EC Compliance report, environmental monitoring was carried out at site by M/s. Hubert Enviro Care Systems Pvt. Ltd, an NABL Accredited Consultant during the period of October 2024 to March 2025

5.1 Ambient Air Quality monitoring

During the construction phase, particulate matter and gaseous emissions are likely to arise from the site movement of vehicles, operation of DG sets etc., the ambient air quality parameters such as suspended Particulate matter (PM10), Respirable Particulate matter (PM 2.5), Sulphur dioxide, Oxides of Nitrogen (NOx), Ammonia, Ozone and Carbon monoxide were monitored. The test report of ambient air quality for the period of October 2024 to March 2025 is enclosed as **Annexure - 4.**

5.2 Ambient Noise level monitoring

Ambient noise levels were monitored and the test report of ambient noise recorded during the period of October 2024 to March 2025, is enclosed as **Annexure - 4.**

5.3 Soil quality monitoring

Soil samples were collected and analyzed for nutrients and heavy metals. The test report of soil samples collected and analyzed during the period of October 2024 to March 2025 is enclosed as **Annexure - 4.**

5.4 Ground water quality monitoring

The Ground water was collected and tested for various water quality parameters during the period of October 2024 to March 2025. The test report of Ground water collected and analyzed is enclosed as **Annexure- 4.**

5.5 Surface water quality monitoring

The surface water was collected and tested for various water quality parameters during the period of October 2024 to March 2025. The test report of surface water collected and analyzed is enclosed as **Annexure- 4.**

Environmental monitoring photographs are enclosed in Annexure-10

6. CONCLUSION

- 1. Environmental monitoring was carried out at site during the period of October 2024 to March 2025
- 2. All the conditions stipulated in Environmental Clearance are being complied/ will be complied.

Dr. RAJKUMAR SAMUEL Director Technical

Name: Dr. Rajkumar Samuel Designation: Director Technical

Company Name: Hubert Enviro Care

Systems Private Limited

STATE LEVEL ENVIRONMENT IMPACT ASSESSMENT AUTHORITY, TAMILNADU



3rd Floor, Panagal Maaligai, No.1 Jeenis Road, Saidapet, Chennai-15.

Thiru, V. Thangavelu, I.A.S. (Reto.) Chairman Tieru V. Haridass Member Dr. H. Mallechappa, I.F.S. Member Secretary

Letter No. SEIAA/TN/F-662/EC/ 8(b)/385/2012 dt .01.04.2015

To

The Principal Secretary/Chairman and Managing Director, SIPCOT,

19/A, Rukmani Lakshmipathy Road, Egmore, Chennai-600 008.

Sir,

Sub:

SEIAA, TN - Environmental Clearance - Proposed project of VAIPUR MATHUR Industrial Park over an extent of 249.28.63 Ha (616.00 ACRES) in S.F.nos.15,16,17,18,56pt, 61pt, 63, 155pt, 166, 167 pt, 168, 159, 170, 171 pt, 172, 173, 174pt, 181, 222, 227, 228–229–230, 231, 233, 234, 236, 237, 238, 239, 240, 241, 242, 243, 244, 245, 246, 247, 248, 249, 250, 251, 252, 253, 254, 255, 256, 257, 258, 259, 260., of Vaipur village, S.F.nos. 44, 46, 47, 48, 49, 50, 51, 52, 53–54, 55, 56, 57, 58, 59, 60, 61, 62, 63, 64, 65, 66, 67, 68, 69, 21, 72, 73, 74, 75, 76, 77, 305, 306, 307, 309, 310, 311, 312, 313, 314, 315, 316, 317, 318, 319, 320, 321, 322, 323, 324, 325, 326, 327, 328, 329, 330, 331, of Mathur village and in S.F.nos. 201/2,202,204, 205, 206, 207, 208bt of Perinjambakkam village, Sriperumpedur taluk, Kancheepuram district under Category [B1] and Schedule S.No. 8(b) by The Principal Secretary/Chairman and Managing Director. M/s. SIPCOT - Issued - Regarding

This has reference to your application dated 7.12.2012 submitted to the State Level Environment Impact Assessment Authority, Tamil Nadu socking Environmental Clearance under the Environment Impact Assessment Notification, 2006.

It is noted, interalia, that the project proposal is for the infrastructural development of an industrial Park at S.F.nos.15,16,47,18,56pt, 61pt, 63, 165pt 166, 167 pt, 168, 169, 170, 171 pt, 172, 173, 174pt, 181, 222, 227, 228, 229, 230, 231, 233, 234, 236, 237, 238, 239, 240, 241, 242, 243, 244, 245, 246, 247, 248, 259, 250, 251, 252, 253, 254, 255, 256, 257, 258, 259, 260., of Vaipur village, S.F.nos. 44, 46, 47, 48, 49, 50, 51, 52, 53, 54, 55, 56, 57, 58, 59, 60, 61, 62, 63, 64, 65, 66, 67, 68, 69, 21, 72, 73, 74, 75, 78, 77, 305, 306, 307, 309, 310, 311, 312, 313, 314, 315, 316, 317, 318, 319, 320, 321, 322, 323, 324, 325,

Page 1 o∫ 15

Member Secretary

مئتاراجويز ک

326, 327, 328, 329, 330, 331., of Mathur village and lin S.F.nos, 201/2,202,204, 205, 206, 207, 208pt of Perinjambakkam village, Sciperumpudur taluk, Kancheepuram district as per the application submitted. The total area of development is 249.28.63 Ha (616.00 ACRES) and is exclusively for industries that do not attract the provisions of EIA notification 2006. The member units will be required to take consent from the TNPCB, individually.

As a developer, the SIPCOT has proposed to provide infrastructure facilities like road, water and other amenities. SIPCOT proposes to allot only developed plots to the potential industries based on the comprehensive assessment of investment, technology, employment, expert, compliance to environmental regulations, etc and to insist them to maintain ZLD in accordance with the TNPCB norms. The cost of the project is Rs. 126 50 Crores. The breakup of the total area is tabulated as below:

S,No.	Area Breakup	Area in acres
1	C Serious industries	393.28
2	D Serious industries	123.18
3	Roads	32.40
4	Panchayath temple	3.36
5	OSR/ Green belt development	1 6 3. 7 817.61
	Total	6160.00 acres

Water requirement of the project during construction phase is 5,00,000 litres which shall be met by SIPCOT from the existing pipeline leading to Oragadam Industrial Growth Centre; Total Water requirement for the operation onase is 4.5 MLD which will be met from CMWSSB.

The member industries will be mandated to have their own STP for treating sewage. SIPCOT will have septic tank and soak pit to treat sewage from the project office and security establishments. The allotted units will be mandated by the SIPCOT to put up ZLD based Effluent Treatment Plants for treating trade effluents and will completely recycle or rouse the treated effluent In the utilities and for green belt development. The member industries will be mandated by SIPCOT to commit for pollution control measures in respect of water/waste water, air/emission, solid waste and noise as per the standards. prescribed by the TNPCB. The member industries will be mandated to take authorization for storage of hazardous solid waste, if any, from TNPCB and the solid waste will be sent to CPCB approved recyclers or to TSDF.

The initial requirement of power is 20 MW reported as, No DG ets will be used during construction period, as per the proposals

The proponent also furnished affidavit in a Non judicial stamp paper stated that,

- We commit to the SEIAA that the fresh water requirement(4.5 MLD) for the proposed project will be met from Chennal Metropolitan. Water Supply and Sewarage Board.
- The allottee industries will be mandated to ensure Zero liquid discharge as per INPCB norms and the same will be monitored by concern Project Officer of SIPCOT.

The project activity is covered in 8(b) of the Schedule and falls under 'B1' category. As per the amendment ct. 1.12.2009 to the EIA notification, 2006, the industrial estate of area less than 500 ha but contain building and construction projects > 20,000 sq.m and or development area more than 50 ha will be treated as activity listed at serial no. 8 (a) or 8 (b) in the schedule as the case may be.

In this proposal, no 'A' or 'B' category industry has been proposed to be housed and also the development area (249.28.63 ha) is more than 50 ha and hence, this project is considered as 8 (b) category which requires EIA report and does not require Public Consultation. Therefore the project does not require Public Consultation as per Para 7(i) III Stage (3) (d) 'Public Consultation' of EIA Notification, 2006.

The SEAC, after due consideration of the relevant documents submitted by the project proponent, and additional clarifications furnished in response to its observations has recommended—in its 60th SEAC meeting held on 25,09,2014 to the SEIAA, Tamil Nadu to grant Environmental Clearance to this project.

The project was considered by the SEIAA-TN in its 124th meeting held on 27.03.2015 in detail and decided to grant EC. Accordingly, SEIAA hereby accords Environmental Clearance to the above project under the provisions of EIA Notification dated 14th September, 2006, as amended <u>with validity for five</u>

Member Secretary SEIAA-TN

المنكاح والمتحود

years from the date of issue of EC, subject to the strict compliance of the terms and conditions stipulated below:

PART A- SPECIFIC CONDITIONS

Construction Phase

- "Consent for Establishment" shall be obtained by SIPCOT as well as Ď. by all member industries from the Tamil Nadu Pollution Control Board and a copy shall be submitted to the SEIAA, Tami: Nadu before taking up of any construction activity at the site
- SIPCOT shall not alter, change or reroute the natural course of the ii) water bodies either partly or wholly and shall ensure to take every precautionary steps to keep the alignment, direction of flow, size etc. of the water bodies to have its natural and smooth passage in existence over Year.
- SIPCOT shall ensure that any construction/ development activity shall iii) not change or after the course of storm water flow either directly or indirectly and shall ensure that every precautionary step shall be taken to ensure the natural existence of waterways with respect to the nearby lakes.
- SIPCOT shall mandated that all member units provide complete iv) closed pipeline system for the collection, storage and Reuse systems for the treated sewage/ trade effluent generated from the individual industry with provisions to ensure regular treated sowage/ effluent sample collection periodically from all the individual industries to ensure the degree of treatment and also to ensure complete compliance of the standards prescribed by the TNPCB.
- SIPCOT shall mandated that the member units should be ٧ì commissioned only after securing water supply connection from the CMWSSB by SIPCOT.

SIPCOT shall adhere the following conditions and also mandated to all its member units to adhere the conditions.

- The excavated earth / construction debris must be used within the premises only.
- 2. The solid waste in the form of excavated earth excluding the top soil scientifically utilized for approach road and peripheral roads constructions.



- 3. All the top soil excavated during construction activities should be stored for use in horticulture/landscape development within the project site.
- 4. Disposal of other construction debris during construction phase should not create any adverse effect on the neighboring communities and be disposed of only in approved sites with the approval of competent authority with necessary precautions for general safety and health aspects of people.
- 5. Adequate potable drinking water and sanitary facilities should be provided for construction workers at the site. The safe disposal of waste water and solid wastes generated during the construction phase should be ensured.
- 6. All required sanitary and hygienic measures should be in place before starting construction activities and they have to be maintained throughout the construction phase.
- 7. For disinfection of waste-water, system using ultra violet radiation shall be adopted.
- 8. For Solid-waste management, composting arrangements shall be provided for biodegradable waste at site.
- 9. The e waste generated shall be handed over to the authorized recyclers.
- 10. All the labourers to be engaged for construction should be screened for health and adequately treated before and during their employment on the work at the site.
- 11.A First Aid Room shall be provided with qualified personnel during operation of the project.
- 12. Disposal of muck, generated during the construction phase should be so managed as not to create any adverse effect on the neighboring areas and communities and be disposed of only in approved sites with the approval of the concerned local body with necessary precautions for general safety and health aspects of people.
- 13. Soil and ground water samples shall be tested to ascertain that there is no threat to ground water quality by leaching of heavy metals and other toxic contaminants.
- 14 Construction spoils and spills including bituminous materials and other hazardous materials must not be allowed to contaminate water courses.

SEIAA-TN

The dump sites for such materials must be impervious so that they do not leach into the ground water.

- 15. No ground water shall be drawn with in SIPCOT area for construction period. .
- 16. Vehicles hired for bringing construction materials to the site should be in good operable condition and should conform to air and noise emission standards, prescribed by TNPCB/CPCB. The vehicles should be operated only during non-peak hours.
- 17. Ambient air and noise level should conform to residential standards prescribed by the TNPCB both during day and night, incremental pollution loads on the ambient air and noise quality should be closely monitored during construction phase and results of monitoring shall be furnished to the Tamilnadu Poliution Control Board by recording base-line date of recent origin. Adequate measures to reduce air and noise pollution during construction shall be adopted, conforming to the norms prescribed by the TNPCB on noise limits.
- 18. Building materials composed wholly or partly of fly Ash should be used in the construction activities as per the provision of Fly ash Notification of September, 1999 as amended in August, 2003.
- 19 Ready mixed concrete must be used in building construction.
- 20. Storm water control and its re-use shall be as per COWB and BIS standaros for various applications.
- 21. Water demand during construction should be reduced by use of premixed concrete, curing agents and other best practices prevalent.
- 22. Fixtures for showers, toilet flushing and drinking water should be of low flow type by adopting the use of aerators / pressure reducing devices / sensor based control.
- 23. Use of glass may be reduced by up to 40% to reduce the electricity consumption load on air conditioning, if necessary, high quality double glass with special reflecting outside coating shall be used for windows.
- 24. Roof should be designed to meet prescriptive requirement of Energy Conservation Building Code (ECBC) by the use of appropriate thermal insulation material.
- 25. Opaque wall should be made to meet prescriptive requirement as per Energy Conservation Building Code which is mandatory for all air conditioned spaces by use of appropriate thermal insulation material.

- Proper approach road for fire fighting vehicles and for rescue operations. in the event of emergency shall be provided.
- Adequate fire protection equipments and rescue arrangements should. be made
- 26. A separate cell shall be formed and kept in readiness with suitable trained personnel for handling of fire fighting equipments / operations.
- 29. Design of buildings should be in conformity with the Seismic Zono. Classification.
- 30. All Energy Conservation Building Code (ECRC) norms shall be adopted.
- 31. Rubber padding to absorb noise while loading & unloading operation. should be provided.
- 32. The probable date of commissioning of the project supported with necessary bar charts shall be furnished to the SEI/AA, Tamil Nadu.
- 33. SIPCO1 shall conduct EIA study for one season excluding rainy season for all parameters such as water lair, noise, waste water etc and submit to SEIAA before March 2014.

<u>Operation Phase</u>

- i) SIPCOT shall ensure that the water podies shall be kept in their natural course without any change in its alignment, direction, capacity eto during entire operation phase of the project
- įη SIPCOT shall also ensure that the catchment area of the adjacent lakes shall not be disturbed or realigned or redistributed or restricted etc during the entire operation phase of the project.
- Ϊij No bunc shall be formed around the premises of SIPCOT which obstruct the rain water flow to the lakes located abetting the Industrial Park
- SIPCOT shall mandated all member units i cosure that the treated iv) sewage/ trade effluent collection, storage and Reuse system shall not have any access at any cost, to the water bodies. All precautionary steps shall be effectively taken and shall be continuously monitored. by the Developer so as to prevent the teachate or discharge of the treated sewage/ trade effluent into canal/ Lakes.
- The irrigational rights of the lands / land owners whose lands are not V) yet acquired should not be either disturbed or denied for any reasons; it should be ensured that they get not only required and eligible water.

SEIAA-TN

Page 7 of 15

- supply to their patta lands, but also should have free access to their respective lands.
- vi) SIPCOT shall ensure that only after Rehabilitation & Resettlement ie., after making payment to all the land owners as per law, the land can be allotted to the member industries.
- vii) The lands under litigation shouldn't be sold/handed over to any industry till the judgement is finalised and delivered in favour of SIPCOT by the concerned court.
- viii) SIPCOT shall ensure that the Green Belt Development as committed including the premises owned by the individual industries and a saving clause in the allotment/sale deed executed with every industry shall be provided.
- SIPCOT shall ensure that no CETP/ CMSWTSF shall be provided for the sewage, trade effluent, municipal solid waste generated from the individual industries except the facilities for the collection, storage and Reuse of the treated sewage/ trade effluent by member units.
- x) SIPCOT shall ensure that no allotment letter/ sale deed in any form shall be made to house category A or category B industry as prescribed in the schedule of EIA notification 2006. However, it is liberty to the Developer to make fresh application for EC before the concerned authority if the Developer so desires to allot / sale the industrial plot for the individual industry to house category A or category B type of industry as prescribed in the schedule of EIA notification 2006 for fresh Environment Clearance (EC).
- xi) SIPCOT shall house in the Industrial park only industries that do not attract the provision of EIA Notification 2006 as committed.
- xii) The water requirement shall be met from the CMWSSB as committed, by SIPCOT.
- xiii) The measures contemplated in the EIA report shall be adhered to by the SIPCOT.
- xiv) Treated sewage shall conform to the norms & standards prescribed by the Tamil Nadu Pollution Control Board.
- xv) There shall be no discharge of treated sewage / trade effluent outside the Pre Industrial Park at any time.
- xvi) No drawal of ground water is permitted within the SIPCOT Industrial Park premises during construction/ operation phase.
- xviii) SIPCOT shall mandate the member units of the Industrial Park to discharge emissions within permissible limits only and to install



adequate APC measures and to allot 30% of the plot area for green belt development and to install rain water harvesting structures.

- SIPCOT shall mandate that all its unit shall furnish separate plan of xviii) action for disposal of treated sewage during monsoon months such as optimal / minimized usage of water, regulate the application of treated sewage to avoid stagnation etc.
- The SIPCOT shall énsure that storm water drain provided at project xix) site shall be maintained without chocking for stagnation and should also ensure that the storm water shall be properly disposed in the natural drainage course.

SIPCOT as well as its member units shall mandated to comply the following conditions:

- Organic converter shall be installed for treating the organic waste and 1. sludge from septic tank and the treated mass shall be used as manure.
- The SIPCOT shall ensure that rain water collected from the covered 2. roof of the buildings; etc shall be scientifically harvested so as to ensure the maximum beneficiation of rain water harvesting.
- SIPCOT shall mandate all its member units that Rain water harvesting 3. for surface run-off, should be filtered before recharging the surface run off, pre-treatment with screens, settlers etc. must be done to remove suspended matter, oil and grease.
- The proponent should also ensure to keep necessary road width as 4. per O.M. dated 7.2.12 of MOEF, GOI, New Delhi with respect to high rise buildings.
- The Plastic wastes shall be segregated and disposed through 5. authorized recyclers.
- A First Aid Room shall be provided with qualified personnel during 6. operation of the project.
- Adequate fire protection equipments and rescue arrangements should 7. be made.
- 8. A separate cell shall be formed and kept in readiness with suitable trained personnel for handling of fire fighting equipments / operations.

- 9. The acoustic enclosures shall be installed at all noise generating equipments such as DG sets, air conditioning systems, etc. and the noise level shall be maintained as per MoEF / CPCB / TNPCB guidelines / norms both during day and night time.
- 10. The green belt design along the periphery of the plot shall achieve attenuation factor conforming to the day and night noise standards prescribed for residential land use. The open spaces inside the plot shall be suitably landscaped and covered with vegetation of suitable variety.
- 11. Application of solar energy should be incorporated for illumination of common areas, lighting for gardens and street lighting in addition to provision for solar water heating. A hybrid system or fully solar system for a portion of the buildings shall be provided.
- 12. Traffic congestion near the entry and exit points from the roads adjoining the proposed project site shall be avoided. Parking shall be fully internalized and no public space should be utilized.
- A report on the energy conservation measures conforming to energy conservation norms prescribed by the Bureau of Energy Efficiency shall be prepared incorporating details about building materials & technology, R & U factors etc and submitted to the SEIAA in three month's time.
- 14. Incremental pollution loads on the ambient air quality, noise and water quality shall be periodically monitored after commissioning of the project.
- 15. SIPCOT shall collect periodical water samples in the adjacent lakes and sufficient well water samples atleast once in 3 months for physiochemical and biological analysis and shall keep the baseline data for record. The compiled annual Report of Analysis shall be forwarded to TNPCB to ascertain the changes in the quality of the lake water, if any followed by remediation / action
- 16. NOC from Forest Department / Chief Wildlife Warden should be obtained for reserve forests or Wild Life Sanctuaries located within 10 Km radius from the boundary of SIPCOT area before allotting land to member industries.

PART-B. GENERAL CONDITIONS (Construction and Operation stage)



- It is mandatory for the Project proponent to furnish to the SEIAA, Half yearly compliance report in Hard and Soft copies on 1st June and 1st December of each calendar year in respect of the conditions stipulated in the prior Environmental Clearance.
 - ii) In the case of any change(s) in the scope of the project or in the product mix, a fresh appraisal by the SEAC/SEIAA shall be obtained.
 - iii) The SEIAA reserves the right to add additional safeguard measures subsequently, if found non compliance of EC conditions and to take action including revoking of this Environmental Clearance as the case may be.
 - iv) All other statutory clearances such as the approvals for storage of diesel from Chief Controller of Explosives, Fire and Rescue Services Department, Civil Aviation Department, Forest Conservation Act, 1980 and Wild Life (Protection) Act, 1972, State / CMWSSB, Coastal Regulatory Zone Authority, other statutory and other authorities as applicable to the project shall be obtained by project proponent from the competent authorities.
 - v) The project authorities should advertise with basic details at least in two local newspaper widely circulated, one of which shall be in the vernacular language of the locality concerned, within 7 days of issue of clearance and a copy of the clearance letter is available with the State Pollution Control Board and also at website of SEIAA, TN and a copy of the same should be forwarded to the Regional Office of the MoEF located at Chennal.
 - vi) Under the provisions of Environment (Protection) Act, 1986, legal action shall be initiated against the project proponent, if it was found that Construction of the project has been started without obtaining Environmental Clearance, and for action for any violation of any condition stipulated in the Environmental Clearance.
 - vii) The proponent shall upload the status of compliance of the stipulated EC conditions, including results of monitored data on their website and shall update the same periodically. It shall simultaneously be sent



to the Regional Office of MoEF, Bengaluru, the respective Zonal Office of CPCB, Bengaluru and the TNPCB. The criteria pollutant levels namely; SPM, RSPM, SO2, NOx (ambient levels as well as stack emissions) or critical sectoral parameters, indicated for the project shall be monitored and displayed at a convenient location near the main gate of the company in the public domain.

- viii)A copy of the clearance letter shall be sent by the proponent to the Block Development Officer and the Local NGO, if any, from whom suggestions /representations, if any, have been received while processing the proposal. The clearance letter shall also be put on the website of the proponent.
- ix) Personnel working in dusty areas should wear protective respiratory devices and they should also be provided with adequate training and information on safety and health aspects. Occupational health surveillance program of the workers should be undertaken periodically to observe any contractions due to exposure to dust and take corrective measures, if needed.
- x) Periodical medical examination of the workers engaged in the project shall be carried out and records maintained. For the purpose, schedule of health examination of the workers should be drawn and followed accordingly. The workers shall be provided with personnel protective measures such as masks, gloves, boots etc.
- xi) A separate environmental management cell with suitable qualified personnel should be set-up under the control of a Senior Executive, who will report directly to the Head of the Organization.
- xii) The funds earmarked for environmental protection measures should be kept in separate account and should not be diverted for other purpose. Year wise expenditure should be reported to the Ministry of Environment and Forests and its Regional Office located at Chennai.
- xiii)The Regional Office of the Ministry located at Chennai shall monitor compliance of the stipulated conditions. The project authorities should extend full cooperation to the officer (s) of the Regional Office by furnishing the requisite data / information / monitoring reports.
- The project proponent shall submit six monthly reports on the



status of compliance of the stipulated environmental clearance conditions including results of monitored data (both in hard copies as well as by e-mail) to the Ministry of Environment and Forests, its Regional Office Chennai, the respective Zonal Office of Central Pollution Control Board, SEIAA, TN and the State Pollution Control Board.

- xv) The environmental statement for each financial year ending 31st March in Form-V as is mandated to be submitted by the project proponent to the concerned State Pollution Control Board as prescribed under the Environment (Protection) Rules, 1986, as amended subsequently, shall also be put on the website of the company along with the status of compliance of environmental clearance conditions and shall also be sent to the Regional Office of the Ministry of Environment and Forests, Chennal by e-mail.
- xvi) The Environmental Clearance does not absolve the applicant/proponent of his obligation/requirement to obtain other statutory and administrative clearances from other statutory and administrative authorities.
- This Environmental Clearance does not imply that the other statutory / administrative clearances shall be granted to the project by the concerned authorities. Such authorities would be considering the project on merits and be taking decisions independently of the Environmental Clearance.
- xviii) The SEIAA, TN may alter/modify the above conditions or stipulate any further condition in the interest of environment protection.
- The SEIAA, TN may cancel the environmental clearance granted xix) to this project under the provisions of EIA Notification, 2006, if, at any stage of the validity of this environmental clearance, if it is found or if it comes to the knowledge of this SEIAA, TN that the project proponent has deliberately concealed and/or submitted false or misleading

information or inadequate data for obtaining the environmental clearance.

- xx) Failure to comply with any of the conditions mentioned above may result in withdrawal of this clearance and attract action under the provisions of the Environment (Protection) Act, 1986.
- The above conditions will be enforced inter-alia, under the provisions of the Water (Prevention & Control of Pollution) Act, 1974. the Air (Prevention & Control of Pollution) Act, 1981, the Environment (Protection) Act, 1986, the Public Liability Insurance Act, 1991, along with their amendments ,draft Minor Mineral Conservation & Development Rules , 2010 framed under MMDR Act 1957, National Commission for protection of Child Right Rules ,2006 and rules made there under and also any other orders passed by the Hon'ble Supreme Court of India / Hon ble High Court of Madras and any other Courts of Law relating to the subject matter.
- xxii) Any appeal against this environmental clearance shall be with the National Green Tribunal, if preferred, within a period of 30 days as prescribed under Section 16 of the National Green Tribunal Act. 2010.

Member Secrétàr∜≫

Copy to:-

- The Secretary to Government, Environment & Forests Dept. Govt, of Tamil Nadu, Fort St. George, Chennai - 9.
- The Secretary to Government, Industries Dept. Govt, of Tamil Nadu, Fort St. George, Channai - 9. -
- 3 The Chairman, Central Pollution Control Board, Parivesh Bhavan. CBD Cum-Office Complex, East Arjun Nagar, New Delhi 110032.
- The Member Secretary, Tamil Nadu Pollution Control Board 76, Mount Salai, Guindy, Chennai-600 032.
- The Additional Principal Chief Conservator of Forests, Regional Office (SZ). 34, HEPC Building, 1st & 2nd Floor, Cathedral Carden Road,

Member Secreta SEIA & JAN

ţř.

Nungampakkam, Chennai – 34.

- 7. Monitoring Cell, I A Division, Ministry of Environment & Forests, Paryavaran Bhavan, CGO Complex, New Delhi 110003.
- 8. The District Collector, Dt. Collectorate, Kancheepuram District.
- 9. The Commissioner, Sriperumbudur Taluk, Kancheepuram District.
- 10. The Chief Engineer (Chennai Region), WRO, Taramani, Chennai.
- 11. Stock File.

Member Secretary **SEIAA-TN**



TAMIL NADU POLLUTION CONTROL BOARD

Category of the Industry:

RED

CONSENT ORDER NO. 210127977199 DATED: 10/08/2021.

PROCEEDINGS NO.T4/TNPCB/F.1366SPR/RL/SPR/A/2021 DATED: 10/08/2021

SUB: TNPC Board-Consent for Establishment-M/s. SIPCOT INDUSTRIAL PARK, VAIPUR MATHUR 71, 72, 73, 74, 75, 76, 77, 305, 306, 307, 309, 310,311, 312,313, 314, 315, 316, 317, 318, 319, 320,321,322, 323, 324, 325, 326, 327, 328, 329, 330, 331 of Mathur village and S.F.nos. 201/2, 202,204, 205, 206,207, 208pt of Perinjambakkam village., MATHUR village, Sriperumbudur Taluk and Kancheepuram District - for the establishment or take steps to establish the industry under Section 21 of the Air(Prevention and control of Pollution)Act,1981, as amended in 1987(Central Act. 14 of 1981)-Issued -Reg.

REF: 1. Unit's application no. 7977199 dated: 26.01.2017 2. IR.No: F.1366SPR/RL/AE/SPR/2020 dated 30/12/2020

- 3. Minutes of the 185th TSC meeting vide item no. 185-04 dated:20.01.2021.
- 4. Minutes of the 187th TSC meeting vide item no. 187-01 dated:29.07.2021.

Consent to establish or take steps to establish is hereby granted under Section 21 of the Air (Prevention and control of Pollution) Act, 1981, as amended in 1987 and the Rules and Orders made there under to

The Managing Director,

M/s . SIPCOT INDUSTRIAL PARK, VAIPUR MATHUR

S.F. No.S.F.nos.15,16, 17, 18, 56pt, 61pt, 63, 165pt, 166,167 pt, 168, 169,170, 171 pt, 172, 173, 174pt, 181, 222, 227, 228,229,230, 231, 233,234, 236, 237, 238, 239, 240,241, 242, 243, 244, 245,246, 247, 248, 249, 250, 251, 252, 253, 254, 255,256, 257, 258, 259, 260 of Vaipur village, S.F.nos. 44, 46, 47,48, 49, 50, 51, 52, 53, 54, 55, 56, 57, 58, 59, 60, 61, 62, 63, 64, 65, 66, 67, 326, 327, 328, 329, 330, 331 of Mathur village and S.F.nos. 201/2, 202,204, 205, 206,207, 208pt of Perinjambakkam village.,

MATHUR Village,

Sriperumbudur Taluk,

Kancheepuram District.

Authorizing occupier to establish or take steps to establish the industry in the site mentioned below:

S.F. No. S.F.nos.15,16, 17, 18, 56pt, 61pt, 63, 165pt, 166,167 pt, 168, 169,170, 171 pt, 172, 173, 174pt, 181, 222, 227, 228, 229, 230, 231, 233, 234, 236, 237, 238, 239, 240, 241, 242, 243, 244, 245, 246, 247, 248, 249, 250, 251, 252, 253, 254, 255,256, 257, 258, 259, 260 of Vaipur village, S.F.nos. 44, 46, 47,48, 49, 50, 51, 52, 53, 54, 55, 56, 57, 58, 59, 60, 61, 62, 63, 64, 65, 325, 326, 327, 328, 329, 330, 331 of Mathur village and S.F.nos. 201/2, 202,204, 205, 206,207, 208pt of Perinjambakkam village.,

MATHUR Village,

Sriperumbudur Taluk,

Kancheepuram District.

This Consent to establish is valid upto March 31, 2022, or till the industry obtains consent to operate under Section 21 of the Air (Prevention and control of Pollution) Act, 1981, as amended in 1987 whichever is earlier subject to special and general conditions enclosed.

For Member Secretary, Tamil Nadu Pollution Control Board, Chennai

To

The Managing Director,

M/s.SIPCOT INDUSTRIAL PARK, VAIPUR MATHUR,

State Industries Promotion Corporation of Tamilnadu Limited, 19-A, Rukmani Lakshmipathy Road, Post Box No. 7223, Egmore,

Chennai, Kancheepuram District

Pin: 600008

Copy to:

- 1. The Commissioner, SRIPERUMBUDUR-Panchayat Union, Sriperumbudur Taluk, Kancheepuram District .
- 2. The District Environmental Engineer, Tamil Nadu Pollution Control Board, SRIPERUMBUDUR.
- 3. The JCEE-Monitoring, Tamil Nadu Pollution Control Board, Chennai.
- 4. File

SPECIAL CONDITIONS

1. This consent to establish is valid for establishing the facility for the manufacture of products/byproducts (Col. 2) at the rate (Col 3) mentioned below. Any change in the product/byproduct and its quantity has to be brought to the notice of the Board and fresh consent has to be obtained.

Sl. No.	Description	Quantity	Unit
	Product Details		
1.	It is an Industrial Park for development and maintenance of infrastructure such as roads, storm water drains, water supply, power supply through TANGEDCO, etc., to accommodate industries, which does not fall under the purview of EIA Notification 2006 and its amendments.	249.2863	Hectares

2. This consent to establish is valid for establishing the facility with the below mentioned emission/noise sources along with the control measures and/or stack. Any change in the emission source/control measures/change in stack height has to be brought to the notice of the Board and fresh consent has to be obtained if necessary.

I	Point source emission with stack :					
Stack No.	Point Emission Source	Air pollution Control measures	Stack height from Ground Level in m	Gaseous Discharge in Nm3/hr		
II	Fugitive/Noise emission :					
Sl. No.	Fugitive or Noise Emission sources	Type of emission	Control measures			

3. Special Additional Conditions:

The unit shall install the approved retrofit emission control device/equipment with at least 70% Particulate matter reduction efficiency on all DG sets with capacity of 125 KVA and above or otherwise the unit shall be shift to gas based generators within the time frame prescribed in the notification No. TNPCB/Labs/DD(L)02151/2019 dated 10.06.2020 issued by TNPCB.

4. Additional Conditions:

- 1. The unit shall comply with the conditions as stipulated in the Environmental Clearance obtained from SEIAA, TN vide Lr.No.SEIAA/TN/ F.662/ 8(b)/385/ 2012 Dated 01.04.2015.
- 2. The unit shall conduct Ambient Noise level survey report and Ambient Air Quality survey report for base line data to assess the quality of Ambient Air and Ambient Noise level and submit the report within one month's time.
- 3. The unit shall remit consent fee in case of revision by the Government.

For Member Secretary, Tamil Nadu Pollution Control Board, Chennai

GENERAL CONDITIONS

- 1. This consent to establish cannot be construed as consent to operate and the unit shall not commence the operation without obtaining the Consent to operate.
- 2. The applicant shall make a request for grant of consent to operate at least thirty days, before the commissioning of trial production.
- 3. Any Change in the details furnished in the conditions has to be brought to the notice of the Board and got approved by the Board, before obtaining consent to operate under the said Act.
- 4. The unit has to comply with the provisions of Public Liability Insurance Act, 1991 to provide immediate relief in the event of any hazard to human beings, other living creatures/plants and properties while handling and storage of hazardous substances (wherever applicable).
- 5. Consent to operate will not be issued unless the unit complies with the conditions of consent to establish.
- 6. The unit shall provide adequate water sprinklers for the control of dust emission during the loading and unloading of construction material so as to minimize the dust emission.
- 7. The unit shall provide water sprinklers along the temporary roads inside the premises to avoid fugitive dust emission during the vehicle movements.
- 8. The unit shall develop green belt of adequate width around the premises.
- 9. In case there is any change in the management, the unit shall inform the change with relevant documents immediately.

For Member Secretary, Tamil Nadu Pollution Control Board, Chennai

** This consent order is computer generated by OCMMS of TNPCB and no signature is needed**



TAMIL NADU POLLUTION CONTROL BOARD

Category of the Industry:

RED

CONSENT ORDER NO. 210117977199 DATED: 10/08/2021.

PROCEEDINGS NO.T4/TNPCB/F.1366SPR/RL//SPR/W/2021 DATED: 10/08/2021

SUB: TNPC Board-Consent for Establishment-M/S SIPCOT INDUSTRIAL PARK, VAIPUR MATHUR S.F No. S.F.nos.15,16, 17, 18, 56pt, 61pt, 63, 165pt, 166,167 pt, 168, 169,170, 171 pt, 172, 173, 174pt, 181, 222, 227, 228,229,230, 231, 233,234, 236, 237, 238, 239, 240,241, 242, 243, 244, 245,246, 247, 248, 249, 250, 251, 252, 253, 254, 255,256, 257, 258, 259, 260 of Vaipur village, S.F.nos. 44, 46, 47,48, 49, 50, 51, 52, 53, 54, 55, 56, 57, 58, 59, 60, 61, 62, 63, 64, 65, 66, 67, 68, 69, 71, 72, 73, 74, 75, 76, 77, 305, 306, 307, 309, 310,311, 312,313, 314, 315, 316, 317, 318, 319, 320,321,322, 323, 324, 325, 326, 327, 328, 329, 330, 331 of Mathur village and S.F.nos. 201/2, 202,204, 205, 206,207, 208pt of Perinjambakkam village., MATHUR Village, Sriperumbudur Taluk, Kancheepuram District - for the establishment or take steps to establish the industry under Section 25 of the Water (Prevention and control of Pollution)Act,1974, as amended in 1988(Central Act 6 of 1974)- Issued- Reg.

REF: 1. Unit's application no. 7977199 dated: 26.01.2017

- 2. IR.No: F.1366SPR/RL/AE/SPR/2020 dated 30/12/2020
- 3. Minutes of the 185th TSC meeting vide item no. 185-04 dated:20.01.2021.
- 4. Minutes of the 187th TSC meeting vide item no. 187-01 dated:29.07.2021.

Consent to establish or take steps to establish is hereby granted under Section 25 of the Water (Prevention and control of Pollution) Act,1974, as amended in 1988(Central Act 6 of 1974) (hereinafter referred to as 'The Act') and the Rules and Orders made there under to

The Managing Director,

SIPCOT INDUSTRIAL PARK, VAIPUR MATHUR

Authorizing occupier to establish or take steps to establish the industry in the site mentioned below:

S.F. No.S.F.nos.15,16, 17, 18, 56pt, 61pt, 63, 165pt, 166,167 pt, 168, 169,170, 171 pt, 172, 173, 174pt, 181, 222, 227, 228,229,230, 231, 233,234, 236, 237, 238, 239, 240,241, 242, 243, 244, 245,246, 247, 248, 249, 250, 251, 252, 253, 254, 255,256, 257, 258, 259, 260 of Vaipur village, S.F.nos. 44, 46, 47,48, 49, 50, 51, 52, 53, 54, 55, 56, 57, 58, 59, 60, 61, 62, 63, 64, 65, 66, 67, 68, 69, 71, 72, 73, 74, 75, 76, 77, 305, 306, 307, 309, 310,311, 312,313, 314, 315, 316, 317, 318, 319, 320,321,322, 323, 324, 325, 326, 327, 328, 329, 330, 331 of Mathur village and S.F.nos. 201/2, 202,204, 205, 206,207, 208pt of Perinjambakkam village.,

MATHUR Village,

Sriperumbudur Taluk,

Kancheepuram District.

This Consent to establish is valid upto **March 31, 2022**, or till the industry obtains consent to operate under Section 25 of the Water (Prevention and control of Pollution) Act, 1974, as amended in 1988 whichever is earlier subject to special and general conditions enclosed.

For Member Secretary, Tamil Nadu Pollution Control Board, Chennai

То

The Managing Director,

M/s.SIPCOT INDUSTRIAL PARK, VAIPUR MATHUR,

State Industries Promotion Corporation of Tamilnadu Limited, 19-A, Rukmani Lakshmipathy Road, Post Box No. 7223, Egmore, Chennai,

Pin: 600008

Copy to:

- 1. The Commissioner, SRIPERUMBUDUR-Panchayat Union, Sriperumbudur Taluk, Kancheepuram District .
- $2.\ The\ District\ Environmental\ Engineer,\ Tamil\ Nadu\ Pollution\ Control\ Board,\ SRIPERUMBUDUR.$
- 3. The JCEE-Monitoring, Tamil Nadu Pollution Control Board, Chennai.

4. File

SPECIAL CONDITIONS

1. This consent to establish is valid for establishing the facility for the manufacture of products/byproducts (Col. 2) at the rate (Col 3) mentioned below. Any change in the product/byproduct and its quantity has to be brought to the notice of the Board and fresh consent has to be obtained.

Sl. No.	Description	Quantity	Unit
	Product Details		
1.	It is an Industrial Park for development and maintenance of infrastructure such as roads, storm water drains, water supply, power supply through TANGEDCO, etc., to accommodate industries, which does not fall under the purview of EIA Notification 2006 and its amendments.	249.2863	Hectares

2. The unit shall provide Sewage Treatment Plant and /or Effluent Treatment Plant as indicated below.

The unit sha	all provide Sewage Treatment Pla	int and /or Enruent Treatmen	it Flait as illuicated below.
a	Sewage Treatment Plant:		
	Treatment stat	us: Septic Tank and SP/DT	
SL. No. Name of the Treatment Unit		No. of Units	Dimensions in metres
1.	Septic Tank at SIPCOT project office	1	4.2*2.3*1.9
2.	Soak Pit	1	1.0m dia x 2.5 m Ht
	Treatment	status: Individual STP	
SL. No.	Name of the Treatment Unit	No. of Units	Dimensions in metres
1.	Member units will have their own STP	0	-
b	Effluent Treatment Plant:		
	Treatment	status: Individual ETP	
SL. No.	Name of the Treatment Unit	No. of Units	Dimensions in metres
1.	Member units will have their own ETP	0	-
	Treatment status: No tra	ade effluent and hence does i	not arise
SL. No.	Name of the Treatment Unit	No. of Units	Dimensions in metres
1.			
2.			

3. This consent to establish is valid for establishing the facility with the below mentioned outlets for the discharge of sewage/trade effluent. Any change in the outlets and the quantity has to be brought to the notice of the Board and fresh consent has to be obtained.

Outlet No.	Description of Outlet	Maximum daily discharge in KLD	Point of disposal				
Effluent Type : Sewage							
1.	1. Sewage 0.57 On Industrys own land						
Effluent Ty	pe : Trade Effluent						

4. Additional Conditions:

- 1. The unit shall comply with the conditions as stipulated in the Environmental Clearance obtained from SEIAA, TN vide Lr.No.SEIAA/TN/ F.662/ 8(b)/385/ 2012 Dated 01.04.2015.
- 2. The issue of CTE to the project shall not be construed as CTO and shall not commission the project without obtaining CTO from the Board.
- 3. The unit shall start its establishment activities only after getting the necessary project/building approvals from the competent authorities.
- 4. This consent order does not absolve from obtaining necessary permission / Clearance from other Authority or under other statutes as applicable.

 5. The stability of the entire building/ STP does not falls under the purview of the TNPC Board.
- 6. The unit shall obtain planning permission and building plan approval from the competent authority and furnish the same to the Board.
- 7. The unit shall earmark the buffer zone all around the periphery of the layout.
- 8. The unit shall allow only housing the industries that do not attract the provisions of EIA notification 2006 as amended in the industrial park as per the EC obtained.
- 9. The unit shall submit baseline data for ground water to assess the quality of ground water for 1 KM radius outside the boundary of the project and also inside available open wells within a month's time.
- 10. The unit shall monitor the ground water in and around the unit premises periodically, so as to assess its quality and submit the same to the Board.
- 11. The unit has to ensure that all the member Industries within the industrial Park shall make their own arrangements to achieve zero discharge of the trade effluents, solid waste & E waste management, gaseous emission and noise control measures to achieve the standards prescribed by the TNPCB.
- 12. The unit shall obtain the necessary permission / NOC of water supply from the TWAD Board / competent Authority.
- 13. The unit shall provide septic tank followed by soak pit to treat the sewage generated from SIPCOT administrative building, so as to achieve the standards prescribed by the Board.
- 14. The unit shall ensure that the allotted industrial units obtain consent from the TNPCB separately for their establishment & operation in this industrial estate.
- 15. The unit shall ensure that 33% of the total area of the project site should be covered with green belt.
- 16. The proponent shall provide Rain Water Harvesting pits so as to recharge the ground water table.
- 17. The bio degradable solid waste, non bio degradable solid waste, STP sludge, etc generated from the project activity shall be properly collected, segregated and disposed as per the provision of Solid
- waste(Management and Handling) Rules, 2016.

 18. The unit shall allot 5% (9.95 Hectares) of the total plot area (199.04 Hectares) for Solid Waste Management as reported in the unit's letter dated 27.02.2021.
- 19. The plastic wastes shall be segregated and disposed as per the provisions of Plastic Waste (Management and Handling) Rules, 2016.
- 20. The unit shall remit consent fee in case of revision by the Government.

For Member Secretary, Tamil Nadu Pollution Control Board,

GENERAL CONDITIONS

- 1. This consent to establish cannot be construed as consent to operate and the unit shall not commence the operation without obtaining the Consent to operate.
- 2. The applicant shall make a request for grant of consent to operate at least thirty days, before the commissioning of trial production.
- 3. Any Change in the details furnished in the conditions has to be brought to the notice of the Board and got approved by the Board, before obtaining consent to operate under the said Act.
- 4. The unit has to comply with the provisions of Public Liability Insurance Act, 1991 to provide immediate relief in the event of any hazard to human beings, other living creatures/plants and properties while handling and storage of hazardous substances (wherever applicable).
- 5. Consent to operate will not be issued unless the unit complies with the conditions of consent to establish.
- 6. The unit shall provide adequate water sprinklers for the control of dust emission during the loading and unloading of construction material so as to minimize the dust emission.
- 7. The unit shall provide water sprinklers along the temporary roads inside the premises to avoid fugitive dust emission during the vehicle movements.
- 8. The unit shall develop green belt of adequate width around the premises.
- 9. In case there is any change in the management, the unit shall inform the change with relevant documents immediately.

For Member Secretary, Tamil Nadu Pollution Control Board, Chennai

** This consent order is computer generated by OCMMS of TNPCB and no signature is needed**



CHIEF ENGINEER (08M-)

CHENNAL METROPOLITAN WATER SUPPLY AND SEWERAGE BOARD



Er No:CM/WSSB/C.E(O&M)II/S.E(WWT&R) / 45 TTRO-KOY / SIPCOT / 2020-21. Dated:13.04.2020

To The Managing Director, SIPCOT. 19-A, Rukmani Lakshmipathi Road, Egmore, Chennai - 600 008,

> CMWSSB \sim C.E(O&M- \aleph I) + S.E(W.W.T&R) + Design, Build and Operate for 15 years (DBO) a 45 MED capacity Tertlary Treatment Reverse Osmosis (TTRD) Plant at Koyambedu including supply, laying and maintenance of M.S. transmission main for conveying product water to various S(POO7 industries situated at frungaltukotta). Sriperumbudur and Oragadani' - Works Completed in all aspects - Inaugurated and Commissioned by the Hor/de Chief Minister of Tarrelloidu on 29.11.2019 - Supply of TTRO Water to the M/s. SIPCO: incustria. bub located at trungattukottei, Pilaipakkam, Vallamvadagal, Seperembudur and Oragadam --Commenced from 18.12.2019 - Security deposit to be remitted -Requested -

Reminder - Reg.

Lr.No: CMWSS8 / C.E(O&M)II / S E(WWT&R) / 45 TTRO-KOY / SIPCOT / Ref: 2019-20, Dated: 06.12.2019 16.12.2019 & 24.91.2020.

The work of "Design, Build and Operate for 15 years (DBO) a 45 MLD capacity. Tertiary Treatment Reverse Osmosis (TTRO) Plant at Koyambedia including supply, laying and maintenance of M.S. transmission main for conveying product water to various SIPCOT industries situated at Irungattukottai, Sriperumbudur and Oragadam" has been completed in all aspects and has been inaugurated & commissioned by the Hon'ble Chief Minister of Tamilhadu on 29.11.2019. The supply of TTRO product water to the M/s SIPCOT industries located at trungattuxottal, Piltaipakkam, Vallamvadagal, Sriperumbudar and Oragadam from Koyambedu TTRO plant, was commenced from 18,12,2019 onwards.

In this connection, it is submitted that, the request for remittance of security deposit for an amount of Rs.2.045 Grores towards the supply of TTRO product water to M/s SIPCOT industries from Koyambedu TTRO plant has been made since 96.12.2019 and further reminders were made vide under references ciled

In this contraction, it is submitted that the requisite security deposit amount has not been remitted till date, inspite of continuous follow up with officials of M/s StPCQT.

As CMWSSB is facing financial crunch for the past more than 5 years with the deficit of about Rs.300 Crores, it is very difficult to manage to remit the Electricity consumption charges of about Rs.1.5 Crores per month towards operation of TTRO plant & Intermediate storage Pumping Stations.

Hence it is requested to cause necessary instructions to the officials to expedite the remittance of security deposit of Rs.2.045 Crores immediately through RTGS/NEST.

This is submitted for favour of information and requested for early action in this regard.

பாசவம் – இன்னா மாவட்டம் – இருப்பெருப்புரு ர் வட்டம் – இருக்காட்டுக் கோட்டை கீராமம் – சிப்சாட் தொழுல் வளர்கத்தில் இன்மத்தின் தொழுற்சாகல குடுத்– செய்பரம்பாக்கம் ஏரியாகுந்த கொறிர் மற்பம் நிலங்குடுத்த நீர்ப்பாசகம் போக எட்சிய நிரால் 5 மில்கியம் தோது நீர் – வடும்புதெல் – ஆகை வெனியைடம் படுகிறது.

envering (crisbled)

456 tem (160) . . 134

gra: 31.3.1997

படிக்கவும்:

De le

1. நோள்ளம் இயக்றநர், சிப்காட் நோர்முக கடிதை என். 1026/96 நாள்: 2.9.1996.

2. தலைகையைப்பொறுயாளர். நூர்வள ததார அமைப்பு, சென்னை மோடியைம். கிருஉத்கா கூறநீர் வழங்கல்களை கடதை என். டபிரியை 1/5250/96, நாள்: 24.12.1996.

பார்வை 1ல் கட்ட கலதத்தில் சிப்காட், மேலாவிலைம் இயக்குநேர் இரும் கோட்டுக்கோட்டை சிப்சாட் தொழில் வளைகத்திற்கு, அந்த அடையைவுள்ள உறுருட்டால் கார் தொழிற்சாறலக்கு தேறையான 1.1.மில்ஸ்மைல் கன அடி தெண்ணிர் உட்பட மொத்தம் சமார் 10 மில்ஸ்மைல் கன அடி தெண்ணிர் தேறைய என்ற கோள்டுள்ளோர்

2. பார்கை 20 கூட கடித்தில் தலைகைப்பொறுமானர் நீர் வன தோர அடைப்பு செல்கும் மூட்லம் மூற்யம் கிருஉள்ள திரை வழக்கல் கிட்டம். கடந்த காலக்கால் செய்பரப்பாக்கும் ஏராயில் உள்ள நீர் நிலை ஒரே சீராக இந்ததில்லை எல்பும், நீரில் கொள்ளனரை 1980ம் ஆடிகு 711 மில்வூடி கோ அடியாக வும், 1992ம் நூட்டு 485 மில்வூடி கேன் நடியாகவும் 1996ம் ஐட்டு 2401 மில்வூடி கோஅடியாகவும் இந்நேததா, தொப்பிட்டுக்கார். மேஷாம் பிதிவு செல்யப் பட்டுக்கை 13,223 ஏக்கர் நயக்கட்டுகளில் தற்போத விவசாயம் செல்யப்பட்டு வரும் 9800 ஏக்கர் நிலக்குத்தை நீர்பாசகம் செலிதாக வேக்கும் என்ற நிலை உள்ளத என்றும் தறிப்பிட்டுக்கார். மேஷம் இத்தோடு செல்கன மாநகருக்கு திருதங்கிர் வசதியும் செம்பரம்பாக்கும் ஏரியிலிருந்த வழங்க வேண்டியிருப்பதால் நீர் இருப்பை கருத்தில் கொள்டு தான் தவ்கீர் வழக்க இடியம் என்ற குறிப்பிட்டுக்கார்.

3. தலைமைப்பொறியாளர் (இசக்குமை மூஃடலம் மறியும் கிருஉத்கா இந்நூர் வழக்கல் இட்டம்) க் கினக்கத்தை குருக்கிற்கொடுகு ஏப்காட் தொழுல் வளரத்தாளாக செயற்குறிப்பை ஐறம் பார்சீகித்தரு.

இது நிறைப்பெறவ்பாக்கம் ஏராயூக் நிர் இருப்பூற்கு நிக்க, பதிவு செலியப் பட்ட ஐயக்கட்டு பஞ்சிகளுக்காக தேவையாக தக்கிர் மற்பும் செல்லக் நகருக்கு தேவதிருக்குத் தேவையாக தூறக்கு பூர்த்த செயித பூர் செய்பெறவ்பாக்கம்



undoors a's tren' I'm L'an UC AM.

Bollows misidents.

Pl. Send a copy y living h

to SIPGIT. GM (The Rondy)

ter information

(1)

Street ...

SE HERE

21/4

Seen du

து நியியிலுத்த தான் ஒன். එது 5 தில்வியும் என திர சிப்சாட் இதாதிற் வளாகத்திற்கு வநல்துவதற்கு இதன் உடைவிடுகிறது. மேற்கும்ட 'சுகுமிறன திறைவேற்பதுள், சிப்சாட் தொழில் வளாகத்தியர் பொருப்புறத்துவறுவல் புதிய தியந்தவவகைகள் உட்பட்டு ஒப்பந்தத்தில் வகவொடுப்படுட்ட பிட்டைசே நிர் வழங்க வேளிடும் எஸ்ட தலைமைப்பொறுமாளர். கொள்ள மண்டலம். மூற்றம் கிருஉத்கார குஷநீர் வழங்கல் திட்டம் அறிவுலுத்தப்படுகிறார்.

(அத்தாக் தெரைப்பா)

ದರಿ.ಟಿ. ಫಲ್ಪಗ, 'ಸರ್ವಾಹಿ ದರಬರುಗೆ.

GULBA:

தவைவமைப்பொறுபோளர், நூர்வள ஆதார அமைப்பு, 'செக்கோன.5.'

தன்றையைப்பொழியானர். தீர்வன ஐதார அமைய்பு. இச்ச்சன மடிடைலம் மற்பேம் சிறுஉத்கா இருநீர் மேற்கம் வழங்கம் சலுற், தெயிற்நாடு தொழில் வளர்ச்சி. கழகம், 19 ஏ. ருக்முன் வட்சியும் தோரு, எழும்புர், செக்கோன்.8. இருவைட்ட ஐட்சியர், அக்காரை மானட்டம்.

நகல்:

தொழில்தறை இக்கான 5 நகராட்டு நிர்வாகம் முற்பம் ஞாநீர் வழங்கல் தலு. வெக்கான 5

/genung/gotubucans/

ार्ष वाच व्याप्त केवाली प्राप्ति महाद्याम व ५ पूर्

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) **BIS FSSAI Notified Laboratory** ISO 9001, 14001 & 45001 Certified.



Name of the Client

TEST REPORT

Page: 1 of 1

ULR

: TC1231025000016355F

Report No.

: HECS/AP/064/180325

Sample ID No

: 180325145

Sampling Date

Received Date

Completed On

Sample quantity : NA

Report Date

Commenced Date: 18/03/2025

: 18/03/2025

: 18/03/2025

: 04/04/2025

: 04/04/2025

Address of the Client

: Vaipur Mathur

: M/s. SIPCOT

Group

: Atmospheric Pollution

Sample Name

: Ambient Air

: NA

Sample Mark

Sample Reference

: NA

Sample Drawn By

; M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location

Project Area

Environmental Condition

: Temperature (°C): 30.8 | Humidity (%): 54.0

S.No.	Test Parameters	Units	Results	Test Method	NAAQ Stand	lards: 2009
Discip	oline : Chemical					
1	Arsenic	ng/m3	BLQ (LOQ: 2.0)	HECS-G/INS/SOP/ 041 Issue No.:01 Issue Date:01.03,2021	6 (Annual)	6 (Annual)
2	Nickel	ng/m3	BLQ (LOQ: 2.0)	HECS-G/INS/SOP/ 041 Issue No.:01 Issue Date:01.03.2021	20 (Annual)	20 (Annual)
9	Benzene-AAQ	µg/m3	BLQ (LOQ: 0.1)	1S 5182 Part 11: 2006	5 (Annual)	5 (Annual)
4	Benzo (a) pyrene-AAQ	ng/m³	BLQ (LOQ: 0.1)	IS: 5182 Part 12: 2004	1 (Annual)	1 (Annual)
5	Ammonia as NH3	μg/m³	7.36	1S 5182 (Part 25) 2018	400 (24 hours)	100 (Annual
6	Carbon Monoxide (CO)	mg/ m³	BLQ(LOQ 0.05)	IS 5182 (Part 10) Clause 4 1999	4 (1 hours)	2 (8 hours)
7	Nitrogen dioxides as NO2	μg/m³	21.91	IS 5182 (Part 6) 2006	80 (24 hours)	40 (Annual)
8	Ozone as O3	μg/m³	15.81	IS 5182 (Part 9) 1974	180 (1 hours)	100 (8 hours
9	Particulate matter (Size less than 10 µm)	μg/m³	87.14	IS 5182 (Part 23) 2006	100 (24 hours)	60 (Annual)
10	Particulate matter (Size less than 2.5 µm)	μg/m³	33.86	IS 5182 (Part 24) 2019	60 (24 hours)	40 (Annual)
11	Sulphur dioxide as SO2	μg/m³	13.24	IS 5182 (Part 2) 2001	80 (24 hours)	50 (Annual)
12	Lead	μg/m3	BLQ (LOQ: 0.002)	HECS-G/INS/SOP/ 041 Issue No.:01 Issue Date:01.03.2021	1 (24 hours)	0.5 (Annual

Note:- BLQ - Below the Limit of Quantification, LOQ- Limit of Quantification, µg/m3- Micrograms per cubic meter, mg/m3-Milligrams per cubic meter, ng/m3-Nanograms per cubic meter.

Remarks: The Tested Parameters as above are within the Limits of NAAQ Standards 2009. ""End of Report""



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization 2. Samples are not drawn by HECS unless or otherwise mentioned 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items.

HECS-C/O/FMT/049 HECS-G/Q/FMT/049

Hubert Enviro Care Systems (P) Ltd. A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in

Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) BIS, FSSAI Notified Laboratory ISO 9001, 14001 & 45001 Certified

TEST REPORT

Page: 1 of 1

Report No.

: HECS/AP/064/180325/N

Sample ID No

: 180325145

Sampling Date

: 18/03/2025

Address of the Client

Name of the Client

: Vaipur Mathur

: M/s. SIPCOT

: 18/03/2025

Sample Name

Group

: Atmospheric Pollution

Received Date

: Ambient Air

Commenced Date: 18/03/2025

: 04/04/2025

Sample Mark

: NA

Completed On

Sample Reference

: NA

Report Date

: 04/04/2025 Sample quantity : NA

Sample Drawn By Sample Location : M/s. Hubert Enviro care Systems (P) Ltd. : Project Area

Environmental Condition

: Temperature (°C): 30.8 | Humidity (%): 54.0

Sampling Method & Plan

: IS 5182 Part 5 & Part 14

S.No.	Test Parameters	Units	Results	Test Method
Discipline	: Chemical			
TVC	oc .	ppmv	BLQ(LOQ 0.1)	HECS-G/ENV/AAQ/SOP/005 Issue No.:01 Issue Date:02:07 2020

Note:- BLQ - Below the Limit of Quantification, LOQ-Limit of Quantification, ppmv- Parts per million by Volume. ***End of Report***



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization 2. Samples are not drawn by HECS unless or otherwise mentioned 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items. HECS-G/Q/FMT/49

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) **BIS FSSAI Notified Laboratory** ISO 9001, 14001 & 45001 Certified.



Name of the Client

TEST REPORT

Page: 1 of 1

ULR

: TC1231025000016356F

Report No.

: HECS/AP/065/180325

Sample ID No

: 180325146

Sampling Date

Received Date

Completed On

Sample quantity : NA

Report Date

Commenced Date: 18/03/2025

: 18/03/2025

: 18/03/2025

: 04/04/2025

: 04/04/2025

Address of the Client

: Vaipur Mathur

: M/s. SIPCOT

Group

: Atmospheric Pollution

Sample Name

: Ambient Air

Sample Mark

Sample Reference

: NA

Sample Drawn By

: M/s.Hubert Enviro care Systems (P) Ltd.

Sample Location Environmental Condition

: Temperature (°C): 30.8 | Humidity (%): 54.0

Sampling Method & Plan

: IS 5182 Part 5 & Part 14

S.No.	Test Parameters	Units	Results	Test Method	NAAQ Stand	lards : 2009
Discip	line : Chemical		101			
Ļ	Arsenic	ng/m3	BLQ (LOQ: 2.0)	HECS-G/INS/SOP/ 041 Issue No.:01 Issue Date:01.03.2021	6 (Annual)	6 (Annual)
2	Nickel	ng/m3	BLQ (LOQ: 2.0)	HECS-G/INS/SOP/ 041 Issue No.:01 Issue Date:01.03.2021	20 (Annual)	20 (Annual)
3	Benzene-AAQ	µg/m3	BLQ (LOQ: 0.1)	1S 5182 Part 11: 2006	5 (Annual)	5 (Annual)
	Benzo (a) pyrene-AAQ	ng/m³	BLQ (LOQ: 0.1)	IS: 5182 Part 12: 2004	l (Annual)	1 (Annual)
Š	Ammonia as NH3	μg/m³	6.88	1S 5182 (Part 25) 2018	400 (24 hours)	100 (Annual)
5	Carbon Monoxide (CO)	mg/ m³	BLQ(LOQ 0.05)	IS 5182 (Part 10) Clause 4 1999	4 (1 hours)	2 (8 hours)
7	Nitrogen dioxides as NO2	μg/m³	16.31	IS 5182 (Part 6) 2006	80 (24 hours)	40 (Annual)
3	Ozone as O3	μg/m³	13.63	IS 5182 (Part 9) 1974	180 (1 hours)	100 (8 hours
9	Particulate matter (Size less than 10 μm)	μg/m³	90.39	IS 5182 (Part 23) 2006	100 (24 hours)	60 (Annual)
10	Particulate matter (Size less than 2.5 μm)	μg/m³	30.71	IS 5182 (Part 24) 2019	60 (24 hours)	40 (Annual)
11	Sulphur dioxide as SO2	μg/m³	6.21	IS 5182 (Part 2) 2001	80 (24 hours)	50 (Annual)
12	Lead	μg/m3	BLQ (LOQ: 0.002)	HECS-G/INS/SOP/ 041 Issue No.:01 Issue Date:01.03.2021	1 (24 hours)	0.5 (Annual)

Note: BLQ - Below the Limit of Quantification, LOQ- Limit of Quantification, µg/m3- Micrograms per cubic meter, mg/m3-Milligrams per cubic meter, ng/m3-Nanograms per cubic meter.

Remarks: The Tested Parameters as above are within the Limits of NAAO Standards 2009. "End of Report"



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization 2. Samples are not drawn by HECS unless or otherwise mentioned 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items. HECS-G/Q/FMT/049

Hubert Enviro Care Systems (P) Ltd. A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in

Laboratory Services Division (Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) BIS, FSSAI Notified Laboratory ISO 9001, 14001 & 45001 Certified.

TEST REPORT

Page: 1 of 1

Report No.

HECS/AP/065/180325/N

Sample ID No

: 180325146

Sampling Date

: 18/03/2025

Address of the Client

Name of the Client

: Vaipur Mathur

: M/s. SIPCOT

Group

: Atmospheric Pollution

Received Date Commenced Date: 18/03/2025

: 18/03/2025

Sample Name Sample Mark

: Ambient Air

Completed On

: 04/04/2025

Sample Reference

: NA

: 04/04/2025

Sample Drawn By

: NA : M/s. Hubert Enviro care Systems (P) Ltd. Report Date

Sample quantity : NA

Sample Location

: Panruti

: Temperature (°C): 30.8 | Humidity (%): 54.0

Environmental Condition Sampling Method & Plan

: IS 5182 Part 5 & Part 14

S.No.	Test Parameters	Units	Results	Test Method
Discipline :	Chemical			
TVO	C	ppmv	BLQ(LOQ 0.1)	HECS-G/ENV/AAQ/SOP/005 Issue No.:01 Issue Date:02:07 2020

Note:- BLQ - Below the Limit of Quantification, LOQ- Limit of Quantification, ppmy- Parts per million by Volume. ***End of Report***



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization. 2. Samples are not drawn by HECS unless or otherwise mentioned. 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss? damage caused by use or misuse of test report after invoicing or issue of fest report. 5. The test results relate only to the test items.

IFCS.CO/EMT/40.* HECS-G/Q/FMT/49

A-21, III Phase, Thiru Vi Ka Industrial Estate.

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) **BIS FSSAI Notified Laboratory** ISO 9001, 14001 & 45001 Certified.



Name of the Client

TEST REPORT

Page: 1 of 1

ULR

: TC1231025000016357F

Report No.

: HECS/AP/066/180325

Sample ID No

: 180325147

Sampling Date

: 18/03/2025

Address of the Client

: Vaipur Mathur

: M/s. SIPCOT

: Atmospheric Pollution

Received Date

: 18/03/2025

Sample Name

Group

: Ambient Air

Commenced Date: 18/03/2025

Sample Mark

: NA

: 04/04/2025

Sample Reference

: NA

Completed On

: 04/04/2025

Sample Drawn By

: M/s.Hubert Enviro care Systems (P) Ltd.

Report Date Sample quantity : NA

Sample Location

: Kanchivakkam

Environmental Condition

: Temperature (°C): 30.8 | Humidity (%): 54.0

Sampling Method & Plan

: IS 5182 Part 5 & Part 14

S.No.	Test Parameters	Units	Results	Test Method	NAAQ Stand	dards: 2009
Discip	dine : Chemical		N			
1	Arsenic	ng/m3	BLQ (LOQ: 2.0)	HECS-G/INS/SOP/ 041 Issue No.:01 Issue Date:01.03.2021	6 (Annual)	6 (Annual)
2	Nickel	ng/m3	BLQ (LOQ: 2.0)	HECS-G/INS/SOP/ 041 Issue No.:01 Issue Date:01.03.2021	20 (Annual)	20 (Annual)
3	Benzene-AAQ	µg/m3	BLQ (LOQ: 0.1)	IS 5182 Part 11: 2006	5 (Annual)	5 (Annual)
4	Benzo (a) pyrene-AAQ	ng/m³	BLQ (LOQ: 0.1)	1S: 5182 Part 12: 2004	i (Annual)	i (Annual)
5	Ammonia as NH3	μg/m³	BLQ(LOQ 5)	IS 5182 (Part 25) 2018	400 (24 hours)	100 (Annual)
6	Carbon Monoxide (CO)	mg/ m³	BLQ(LOQ 0.05)	IS 5182 (Part 10) Clause 4 1999	4 (1 hours)	2 (8 hours)
7	Nitrogen dioxides as NO2	μg/m³	12.03	IS 5182 (Part 6) 2006	80 (24 hours)	40 (Annual)
8	Ozone as O3	μg/m³	BLQ(LOQ 10)	IS 5182 (Part 9) 1974	180 (1 hours)	100 (8 hours)
9	Particulate matter (Size less than 10 μm)	μg/m³	83.97	IS 5182 (Part 23) 2006	100 (24 hours)	60 (Annual)
10	Particulate matter (Size less than 2.5 μ m)	μg/m³	28.91	IS 5182 (Part 24) 2019	60 (24 hours)	40 (Annual)
11	Sulphur dioxide as SO2	μg/m³	7.43	IS 5182 (Part 2) 2001	80 (24 hours)	50 (Annual)
12	Lead	μg/m3	BLQ (LOQ: 0.002)	HECS-G/INS/SOP/ 041 Issue No.:01 Issue Date:01.03.2021	1 (24 hours)	0.5 (Annual)

Note:- BLQ - Below the Limit of Quantification, LOQ- Limit of Quantification, µg/m3- Micrograms per cubic meter, mg/m3-Milligrams per cubic meter, ng/m3-Nanograms per cubic meter.

Remarks: The Tested Parameters as above are within the Limits of NAAQ Standards 2009. "End of Report"



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization 2. Samples are not drawn by HECS unless or otherwise mentioned 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss/damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items.

HECS-C/O/FMT/049 HECS-G/Q/FMT/049

Hubert Enviro Care Systems (P) Ltd. A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in

Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) BIS, FSSAI Notified Laboratory ISO 9001, 14001 & 45001 Certified.

TEST REPORT

Page: 1 of 1

Report No.

: HECS/AP/066/180325/N

Sample ID No

: 180325147

Sampling Date

Received Date

Completed On

Report Date

: 18/03/2025

: 18/03/2025

: 04/04/2025

: 04/04/2025

Address of the Client

Name of the Client

: Vaipur Mathur

: M/s. SIPCOT

Group

: Atmospheric Pollution

Sample Name

: Ambient Air

: NA

Sample Mark Sample Reference

: NA

Sample Drawn By

: M/s. Hubert Enviro care Systems (P) Ltd. : Kanchivakkam

Sample Location Environmental Condition Sampling Method & Plan

: IS 5182 Part 5 & Part 14

: Temperature (°C): 30.8 | Humidity (%): 54.0

Sample quantity : NA

Commenced Date: 18/03/2025

S.No.	Test Parameters	Units	Results	Test Method
Disciplin	e : Chemical			
1 T	VOC	ppmv	BLQ(LOQ 0.1)	HECS-G/ENV/AAQ/SOP/005 Issue No.:01 Issue Date:02:07 2020

Note:- BLQ - Below the Limit of Quantification, LOQ- Limit of Quantification, ppmv- Parts per million by Volume. ***End of Report***



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization 2. Samples are not drawn by HECS unless or otherwise mentioned 2. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items. HECS-G/Q/FMT/49

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) **BIS FSSAI Notified Laboratory** ISO 9001, 14001 & 45001 Certified.



TEST REPORT

Page: 1 of 1

ULR

: TC1231025000016358F

Report No.

HECS/AP/067/180325

Sample ID No

: 180325148

Name of the Client

: M/s. SIPCOT

Sampling Date

: 18/03/2025

Address of the Client

: Vaipur Mathur

: Atmospheric Pollution

Received Date

: 18/03/2025

Sample Name

Group

: Ambient Air

Commenced Date: 18/03/2025

Sample Mark

: NA

Completed On

: 04/04/2025

Sample Reference

: NA

Report Date

: 04/04/2025

Sample Drawn By

: M/s. Hubert Enviro care Systems (P) Ltd. : Vattambakkam

Sample quantity : NA

Sample Location

| Humidity (%): 54.0

Environmental Condition Sampling Method & Plan

: Temperature (°C): 30.8 : 18 5187 Part 5 & Part 14

S.No.	Test Parameters	Units	Results	Test Method	NAAQ Stand	dards : 2009
Discip	line : Chemical					
1	Arsenic	ng/m3	BLQ (LOQ: 2.0)	HECS-G/INS/SOP/ 041 Issue No.:01 Issue Date:01.03.2021	6 (Annual)	6 (Annual)
2	Nickel	ng/m3	BLQ (LOQ: 2.0)	HECS-G/INS/SOP/ 041 Issue No.:01 Issue Date:01.03.2021	20 (Annual)	20 (Annual)
3	Benzene-AAQ	μg/m3	BLQ (LOQ: 0.1)	IS 5182 Part 11: 2006	5 (Annual)	5 (Annual)
4	Benzo (a) pyrene-AAQ	ng/m²	BLQ (LOQ: 0.1)	IS: 5182 Part 12: 2004	I (Annual)	i (Annual)
5	Ammonia as NH3	µg/m [†]	BLQ(LOQ 5)	IS 5182 (Part 25) 2018	400 (24 hours)	100 (Annual)
6	Carbon Monoxide (CO)	mg/ m³	BLQ(LOQ 0.05)	IS 5182 (Part 10) Clause 4 1999	4 (1 hours)	2 (8 hours)
7	Nitrogen dioxides as NO2	μg/m³	17.23	IS 5182 (Part 6) 2006	80 (24 hours)	40 (Annual)
8	Ozone as O3	μg/m³	BLQ(LOQ 10)	IS 5182 (Part 9) 1974	180 (1 hours)	100 (8 hours)
9	Particulate matter (Size less than 10 $$ $\mu m)$	μg/m³	91.63	IS 5182 (Part 23) 2006	100 (24 hours)	60 (Annual)
10	Particulate matter (Size less than 2.5 μ m)	μg/m³	27.95	1S 5182 (Part 24) 2019	60 (24 hours)	40 (Annual)
11	Sulphur dioxide as SO2	μg/m¹	9.87	IS 5182 (Part 2) 2001	80 (24 hours)	50 (Annual)
12	Lead	μg/m3	BLQ (LOQ: 0.002)	HECS-G/INS/SOP/ 041 Issue No.:01 Issue Date:01.03.2021	1 (24 hours)	0.5 (Annual)

Note: BLQ - Below the Limit of Quantification, LOQ-Limit of Quantification, µg/m3- Micrograms per cubic meter, mg/m3-Milligrams per cubic meter, ng/m3-Nanograms per cubic meter.

Remarks: The Tested Parameters as above are within the Limits of NAAQ Standards 2009.

"End of Report"

^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization 2. Samples are not drawn by HECS unless or otherwise 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items. HECS-G/O/FMT/049

Hubert Enviro Care Systems (P) Ltd. A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennal - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in

Laboratory Services Division (Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) BIS, FSSAI Notified Laboratory ISO 9001, 14001 & 45001 Certified.

TEST REPORT

Page: 1 of 1

Report No.

: HECS/AP/067/180325/N

Sample ID No

: 180325148

Sampling Date

Received Date

Completed On

Sample quantity : NA

Report Date

Commenced Date: 18/03/2025

: 18/03/2025

: 18/03/2025

: 04/04/2025

: 04/04/2025

Address of the Client

Name of the Client

: Vaipur Mathur

: M/s. SIPCOT

Group

: Atmospheric Pollution

: Ambient Air

Sample Name Sample Mark

: NA

Sample Reference

: NA

: M/s.Hubert Enviro care Systems (P) Ltd.

Sample Drawn By Sample Location

: Vattambakkam

: Temperature (°C): 30.8 | Humidity (%): 54.0

Environmental Condition nling Mathod 6 DL

sampti	ng Method & Plan : IS 5182 Part 5	& Part 14		
S.No.	Test Parameters	Units	Results	Test Method
Discip	line : Chemical			
1	TVOC	ppmv	BLQ(LOQ 0.1)	HECS-G/ENV/AAQ/SOP/005 Issue No:01 Issue Date:02:07.2020

Note:- BLQ - Below the Limit of Quantification, LOQ- Limit of Quantification, ppmv- Parts per million by Volume. ***End of Report***



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization. 2. Samples are not drawn by HECS unless or otherwise mentioned. 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances tab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items. HECS-G/O/FMT/49

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing)
Recognized by CPCB (MoEF & CC)
BIS FSSAI Notified Laboratory
ISO 9001, 14001 & 45001 Certified.

Name of the Client

TEST REPORT

Page: 1 of 1

ULR : TC1231025000016359F

Report No. : HECS/AP/068/180325

: 18/03/2025

: 04/04/2025

: 04/04/2025

Sample ID No : 180325149

Received Date

Completed On

Sample quantity : NA

Report Date

Sampling Date : 18/03/2025

Commenced Date: 18/03/2025

Address of the Client : Vaipur Mathur

Group : Atmospheric Pollution

Sample Name : Ambient Air

Sample Mark : NA Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

: M/s. SIPCOT

Sample Location : Mathur

Environmental Condition : Temperature (°C): 30.8 | Humidity (%): 54.0

Sampling Method & Plan : IS 5182 Part 5 & Part 14 S.No. Units Results **Test Parameters** Test Method NAAQ Standards: 2009 Discipline: Chemical BLQ (LOQ: 2.0) HECS-G/INS/SOP/ 041 Issue Arsenic ng/m3 6 (Annual) 6 (Annual) No.:01 Issue Date:01.03.2021 Nickel ng/m3 BLQ (LOQ: 2.0) HECS-G/INS/SOP/ 041 Issue 20 (Annual) 20 (Annual) No.:01 Issue Date:01.03.2021 Benzene-AAO 119/m3 BLO (LOO: 0.1) IS 5182 Part 11: 2006 5 (Annual) 5 (Annual) Benzo (a) pyrene-AAQ ng/m³ BLQ (LOQ: 0.1) IS: 5182 Part 12: 2004 1 (Annual) 1 (Annual) Ammonia as NH3 IS 5182 (Part 25) 2018 $\mu g/m^3$ 8 31 400 (24 hours) 100 (Annual) Carbon Monoxide (CO) IS 5182 (Part 10) Clause 4 6 mg/ m3 BLQ(LOQ 0.05) 4 (I hours) 2 (8 hours) 1999 Nitrogen dioxides as NO2 21.19 IS 5182 (Part 6) 2006 80 (24 hours) µg/m³ 40 (Annual) Ozone as O3 µg/m3 15.15 IS 5182 (Part 9) 1974 180 (1 hours) 100 (8 hours) Particulate matter (Size less than 10 82.36 IS 5182 (Part 23) 2006 100 (24 hours) µg/m³ 60 (Annual) 10 Particulate matter (Size less than 2.5 35.33 µg/m³ IS 5182 (Part 24) 2019 60 (24 hours) 40 (Annual) 11 Sulphur dioxide as SO2 µg/m3 13,44 IS 5182 (Part 2) 2001 80 (24 hours) 50 (Annual) Lead 12 $\mu g/m3$ BLQ (LOQ: HECS-G/INS/SOP/ 041 Issue 1 (24 hours) 0.5 (Annual) 0.002)No.:01 Issue Date:01.03.2021

Note:- BLQ - Below the Limit of Quantification, LOQ- Limit of Quantification, μg/m²- Micrograms per cubic meter, mg/m²-Milligrams per cubic meter, ng/m²-Nanograms per cubic meter.

Remarks: The Tested Parameters as above are within the Limits of NAAQ Standards 2009.

End of Report



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization 2. Samples are not drawn by HECS unless or otherwise mentioned 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances tab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items.

HECS-G/O/FMT/049

Hubert Enviro Care Systems (P) Ltd. A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in

Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) BIS, FSSAI Notified Laboratory ISO 9001, 14001 & 45001 Certified.

TEST REPORT

Page: 1 of 1

Report No.

: HECS/AP/068/180325/N

Sample ID No

: 180325149

Sampling Date

: 18/03/2025

Address of the Client

Name of the Client

: Vaipur Mathur

: M/s. SIPCOT

: 18/03/2025

Group Sample Name : Atmospheric Pollution

Received Date

Commenced Date: 18/03/2025

Sample Name Sample Mark

S.No.

: Ambient Air

Completed On

: 04/04/2025

Sample Reference

: NA

Report Date

: 04/04/2025

Sample Drawn By

: NA : M/s.Hubert Enviro care Systems (P) Ltd.

Test Parameters

Kepon D

Sample quantity: NA

Sample Location Environmental Condition : Mathur

weathur

: Temperature (°C): 30.8 | Humidity (%): 54.0

Sampling Method & Plan

: IS 5182 Part 5 & Part 14

Results	Test Method

Note:- BLQ - Below the Limit of Quantification, LOQ- Limit of Quantification, ppmv- Parts per million by Volume.

End of Report

Units



A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in

Name of the Client

Sample Location

Group



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) BIS FSSAI Notified Laboratory ISO 9001, 14001 & 45001 Certified.

TEST REPORT

: M/s. SIPCOT

Page: 1 of 4

ULR : TC1231025000016362F

Report No. : HECSL/WT/041/180325

Sample ID No : 180325151

Sampling Date : 18/03/2025

Address of the Client : Vaipur Mathur

: Water Received Date : 18/03/2025

 Sample Name
 : Ground Water
 Commenced Date: 18/03/2025

 Sample Mark
 : Panruti
 Completed On : 04/04/2025

 Sample Reference
 : NA
 Report Date : 04/04/2025

Sample Reference : NA Report Date : 04/04/2025
Sample Drawn By : M/s.Hubert Enviro care Systems (P) Ltd. Sample quantity: 2 Litres

Environmental Condition : Temperature (°C): 27.8 | Humidity (%): 56.0

Sampling Method & Plan : IS 17614(Part-1):2021

S.No.	Test Parameters	Units	Results	Test Method	IS 10500	: 2012
					Acceptable Limits (Max)	Permissible Limits (Max)
Disci	pline : Chemical					
1	Bi carbonate	mg/l	189.1	IS 3025 Part 51: 2001	NA	NA
2	Boron as B	mg/l	BLQ(LOQ:0.1)	IS 3025 Part 57 -Curcumin Method: 2021	0.5	2.4
3	Calcium as Ca	mg/l	24.05	IS 3025 Part 40: 1991(EDTA Titrimetric Method)	75	200
4	Carbonate	mg/l	BLQ(LOQ:1.0)	IS 3025 Part 51: 2001	NA	NA
5	Chloride as Cl	mg/l	42.06	IS 3025 Part 32: 1988 (Argentometric Method)	250	1000
6	Cyanide as CN	mg/l	BLQ(LOQ:0.01)	IS 3025 Part 27 Sec 1: 2021	0.05	No relaxation
7	Electrical Conductivity at 25°C	μS/cm	539.0	IS 3025 Part-14: 2013	NA	NA
8	Fluoride as F	mg/l	0.27	APHA 23rd edition (Method 4500F- B, D): 2017	1.0	1.5
9	Iron as Fe	mg/l	0.035	IS 3025 (Part 53): 2003	1.0	No relaxation
10	Magnesium as Mg	mg/l	9.72	IS 3025 Part 46: 1994 (Valumetric Method using EDTA)	30	100
11	Nitrate as NO3	mg/l	8.62	APHA 23rd edition (Method 4500 NO3B): 2017	45	No relaxation
12	Colour	Hazen units	BLQ(LOQ:1.0)	IS 3025 (Part4): 2021	5	15
13	pH at 25°C	¥	7.32	IS 3025(Part 11): 2022 (Electrometric method)	6.5-8.5	No relaxation



D.Anusuya Lab Manager

Authorized Signatory

t. The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization. 2. Samples are not drawn by HECS unless or otherwise mentioned. 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items.

HECS-G/Q/FMT/049

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) **BIS FSSAI Notified Laboratory** ISO 9001, 14001 & 45001 Certified.

Name of the Client

TEST REPORT

Page: 2 of 4

ULR

: TC1231025000016362F

Report No.

HECSL/WT/041/180325

Sample 1D No

: 180325151

Sampling Date

: 18/03/2025

Address of the Client

: Vaipur Mathur

: M/s. SIPCOT

: Water

Received Date

: 18/03/2025

Sample Name

Group

: Ground Water

Commenced Date: 18/03/2025

Sample Mark

: Panruti

Completed On

: 04/04/2025

Sample Reference

: NA

: 04/04/2025

Sample Drawn By

: M/s. Hubert Enviro care Systems (P) Ltd.

Report Date

Sample Location

Sample quantity : 2 Litres

Environmental Condition

: Temperature (°C): 27.8 | Humidity (%): 56.0

Sampling Method & Plan

: IS 17614(Part-1):2021

S.No.	Test Parameters	Units	Results	Test Method	IS 10500	0:2012
				00000000000	Acceptable Limits (Max)	Permissible Limits (Max)
14	Potassium as K	mg/l	5.0	IS 3025 Part 45: 1993 (Fleme emission Photometric Method)	NA	NA
5	Sodium as Na	mg/l	62.0	IS 3025 Part 45: 1993 (Fleme emission Photometric Method)	NA	NA
16	Sulphate as SO4	mg/l	27.12	IS 3025 Part 24 Sec 1: 2022(Turbidity Method)(Turbidity Method)	200	400
17	Total dissolved solids	mg/l	290.0	IS 3025 (Part 16): 1984	500	2000
8	Total Suspended Solids	mg/l	BLQ(LOQ:2.0)	IS 3025 (Part 17): 1984	NA.	NA
19	Phosphorous as P	mg/l	0.037	IS 3025 Part 31 Sec 1: 2022 (Stannous Chloride method)	NA	NA
20	Total hardness as CaCO3	mg/l	100.0	IS 3025 (Part 21): 2009	200	600
11	Turbidity, NTU	NTU	BLQ(LOQ:0.1)	IS 3025 (Part 10): 1984	1	5
22	Arsenic	mg/l	BLQ (LOQ: 0.005)	USEPA 200.8 : 1994	0.01	No relaxation
23	Barium	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8: 1994	0.7	No relaxation
24	Cadmium	mg/l	BLQ (LOQ: 0.001)	USEPA 200.8:1994	0.003	No relaxation
25	Chromium	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8: 1994	0.05	No relaxation
26	Copper	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8: 1994	0.05	1.5



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization. 2. Samples are not drawn by HECS unless or otherwise mentioned. 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances tab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items.

HECS-G/O/FMT/049 HECS-G/Q/FMT/049

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) **BIS FSSAI Notified Laboratory** ISO 9001, 14001 & 45001 Certified.



Name of the Client

TEST REPORT

Page: 3 of 4

ULR : TC1231025000016362F

Report No. HECSL/WT/041/180325

: 18/03/2025

: 04/04/2025

04/04/2025

Sample ID No : 180325151

Received Date

Completed On

Report Date

Sampling Date : 18/03/2025

Commenced Date: 18/03/2025

Sample quantity : 2 Litres

Address of the Client

: Vaipur Mathur

: M/s. SIPCOT

Group

: Water

Sample Name

Ground Water

Sample Mark

: Panruti

Sample Reference

: NA

Sample Drawn By

: M/s.Hubert Enviro care Systems (P) Ltd.

Sample Location

Environmental Condition

: Temperature (°C): 27.8 | Humidity (%): 56.0

Sampling Method & Plan

: IS 17614(Part-1):2021

S.No.	Test Parameters	Units	Results	Test Method	IS 10500	: 2012
					Acceptable Limits (Max)	Permissible Limits (Max)
27	Lead	mg/l	BLQ (LOQ: 0.005)	USEPA 200.8: 1994	0.01	No relaxation
28	Mercury	mg/l	BLQ (LOQ: 0.0005)	USEPA 200.8 : 1994	0.001	No relaxation
29	Nickel	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8: 1994	0.02	No relaxation
30	Zinc	mg/i	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	5	15
31	Phenolic compounds as C6H5OH	mg/l	BLQ(LOQ:0.00 1)	IS 3025 Part 43 Sec 1: 2022	0.001	0.002
32	Anionic Surface Active agents as MBAS	mg/l	BLQ(LOQ:0.05)	APHA 23rd edition (Method 5540 B , C): 2017	0.2	1
33	Percent Sodium	%	55.74	HECS /WT/SOP/002:: 2019	NA	NA
34	Barium	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8: 1994	0.7	No relaxation
35	Residual Sodium Carbonate	meq/l	BLQ(LOQ:1.0)	IS 11624: 2019	0.2	1.0
36	Ammonia as NH3	mg/l	BLQ(LOQ:0.02)	IS 3025 Part 34:Sec 2: 2021 (Nesslerization Method)	0.5	No relaxation
37	Sodium Adsorption Ratio(SAR)	Square root of (millimole/lit	2.7	IS 11624 : 2019	NA	NA
38	Dissolved oxygen	mg/l	6.6	IS 3025 (Part 38): 1989 (Titrimetric Method)	NA	NA



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization 2. Samples are not drawn by HECS unless or otherwise mentioned 3, Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items. HECS-G/Q/FMT/049

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) BIS FSSAI Notified Laboratory ISO 9001, 14001 & 45001 Certified.

TEST REPORT

Page: 4 of 4

ULR

: TC1231025000016362F

Report No.

: HECSL/WT/041/180325

Sample ID No

: 180325151

Sampling Date

: 18/03/2025

Address of the Client

Name of the Client

: M/s. SIPCOT : Vaipur Mathur

Received Date

: 18/03/2025

Group Sample Name : Water

Commenced Date: 18/03/2025

: Ground Water : Panruti

Completed On

: 04/04/2025

Sample Mark Sample Reference

: 04/04/2025

: NA

Report Date

Sample Drawn By

: M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location

Sample quantity : 2 Litres

Environmental Condition Sampling Method & Plan : Temperature (°C): 27.8 | Humidity (%): 56.0

: IS 17614(Part-1):2021

S.No.	Test Parameters	Units	Results	Test Method	IS 10500 : 2012	
		***************************************			Acceptable Limits (Max)	Permissible Limits (Max)
39	Biological Oxygen Demand (BOD)@ 27°C For 3 days	mg/l	BLQ(LOQ:2.0)	IS 3025 Part 44: 1993	NA	NA
40	Chemical Oxygen Demand (COD)	mg/l	BLQ(LOQ:4.0)	IS 3025 Part 58: 2006	NA	NA
41	Selenium	mg/l	BLQ (LOQ: 0.005)	USEPA 200.8: 1994	0.01	No relaxation
42	Manganese	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8: 1994	0.1	0.3
43	Total alkalinity as CaCO3	mg/l	155.0	IS 3025 (Part 23): 1986	200	600
44	Phosphate as PO4	mg/l	BLQ(LOQ:0.02)	IS 3025 Part 31 Sec 1: 2022	NA NA	NA

Note :- BLQ - Below the Limit of Quantification, LOQ-Limit of Quantification, NTU-Nephelometric Turbidity Unit. mg/l- Milligrams per litre, NA - Not Applicable,

End of Report



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization. 2. Samples are not drawn by HECS unless or otherwise mentioned. 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items.

HECS_C/O/EMT/049 HECS-G/Q/FMT/049

Hubert Enviro Care Systems (P) Ltd. A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in

Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) BIS, FSSAI Notified Laboratory ISO 9001, 14001 & 45001 Certified.

TEST REPORT

Page: 1 of 1

Report No.

HECSL/WT/041/180325N

Sample ID No

: 180325151

Sampling Date

: 18/03/2025

Address of the Client

Name of the Client

: Vaipur Mathur

: M/s. SIPCOT

Group

: Water

Received Date : 18/03/2025

Sample Name

: Ground Water

Completed On

Commenced Date: 18/03/2025

Sample Mark

: Panruti

: 04/04/2025

Sample Reference

: NA

Report Date

: 04/04/2025

Sample Drawn By

: M/s. Hubert Enviro care Systems (P) Ltd.

Sample quantity : 2 Litres

Sample Location

: Temperature (°C): 27.8 | Humidity (%): 56.0

Environmental Condition Sampling Method & Plan

: IS 17614(Part-1):2021

S.No.	Test Parameters	Units	Results	Test Method
Disciplin	ne : Chemical			
1 1	Hexavalent Chromium as Cr6+	mg/l	BLQ(LOQ:0.01)	IS 3025 Part 52 Clause 6: 2003

Note:- BLQ : Below Limit of Quantification, LOQ: Limit of Quantification, mg/l: milligram per Litre. ***End of Report***



A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in

Name of the Client

Group



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) BIS FSSAI Notified Laboratory ISO 9001, 14001 & 45001 Certified.

TEST REPORT

: M/s. SIPCOT

Page: 1 of 4

ULR : TC1231025000016363F

Report No. : HECSL/WT/042/180325

Sample ID No : 180325152

Sampling Date : 18/03/2025

Address of the Client : Vaipur Mathur

: Water Received Date : 18/03/2025

Sample Name : Ground Water Commenced Date: 18/03/2025
Sample Mark : Kanchivakkam Completed On : 04/04/2025

Sample Reference : NA Report Date : 04/04/2025
Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd. Sample quantity: 2 Litres

Sample Location ; NA

Environmental Condition : Temperature (°C): 27.8 | Humidity (%): 56.0

Sampling Method & Plan : IS 17614(Part-1):2021

S.No.	Test Parameters	Units	Results	Test Method	1S 10500	: 2012
-0.000			,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,		Acceptable Limits (Max)	Permissible Limits (Max)
Discip	pline : Chemical				- A	
1	Bi carbonate	mg/l	329.4	IS 3025 Part 51: 2001	NA	NA
2	Boron as B	mg/l	BLQ(LOQ:0.1)	IS 3025 Part 57 -Curcumin Method: 2021	0.5	2.4
3	Calcium as Ca	mg/l	BLQ(LOQ:1.0)	IS 3025 Part 40: 1991(EDTA Titrimetric Method)	75	200
4	Carbonate	mg/l	BLQ(LOQ:1.0)	IS 3025 Part 51: 2001	NA 1	NA
5	Chloride as CI	mg/l	79.18	IS 3025 Part 32: 1988 (Argentometric Method)	250	1000
6	Cyanide as CN	mg/l	BLQ(LOQ:0.01)	IS 3025 Part 27 Sec 1: 2021	0,05	No relaxation
7	Electrical Conductivity at 25°C	μS/cm	760.0	IS 3025 Part-14: 2013	NA	NA
8	Fluoride as F	mg/l	0.38	APHA 23rd edition (Method 4500F- B , D): 2017	1.0	1.5
9	Iron as Fe	mg/l	0.039	IS 3025 (Part 53): 2003	1.0	No relaxation
10	Magnesium as Mg	mg/l	41.31	1S 3025 Part 46: 1994 (Valumetric Method using EDTA)	30	100
11	Nitrate as NO3	mg/l	2.34	APHA 23rd edition (Method 4500 NO3B): 2017	45	No relaxation
12	Colour	Hazen units	BLQ(LOQ:1.0)	IS 3025 (Part4): 2021	5	15
13	pH at 25°C	**	7.88	1S 3025(Part 11) : 2022 (Electrometric method)	6.5-8.5	No relaxation



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization 2. Samples are not drawn by HECS unless or otherwise mentioned 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items.

HECS-G/Q/FMT/049

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) **BIS FSSAI Notified Laboratory** ISO 9001, 14001 & 45001 Certified.

Name of the Client

TEST REPORT

Page: 2 of 4

ULR

: TC1231025000016363F

Report No.

: HECSL/WT/042/180325

Sample ID No

: 180325152

Sampling Date

: 18/03/2025

Address of the Client

: Vaipur Mathur

: M/s. SIPCOT

: Water

Received Date

: 18/03/2025

Sample Name

Group

: Ground Water

Commenced Date: 18/03/2025

Sample Mark

: Kanchivakkam

Completed On

: 04/04/2025

Sample Reference

Report Date

: 04/04/2025

Sample Drawn By

: M/s. Hubert Enviro care Systems (P) Ltd.

Sample quantity : 2 Litres

Sample Location

Environmental Condition

: Temperature (°C): 27.8 | Humidity (%): 56.0

Sampling Method & Plan

: IS 17614(Part-1):2021

S.No.	Test Parameters	Units	Results	Test Method	1S 10500): 2012
Chron.					Acceptable Limits (Max)	Permissible Limits (Max)
14	Potassium as K	mg/l	8.0	IS 3025 Part 45: 1993 (Fleme emission Photometric Method)	NA	NA
1.5	Sodium as Na	mg/l	94.0	IS 3025 Part 45: 1993 (Fleme emission Photometric Method)	NA	NA
16	Sulphate as SO4	mg/l	16.45	IS 3025 Part 24 Sec 1: 2022(Turbidity Method)(Turbidity Method)	200	400
17	Total dissolved solids	mg/l	405.0	IS 3025 (Part 16): 1984	500	2000
18	Total Suspended Solids	mg/l	BLQ(LOQ:2.0)	IS 3025 (Part 17): 1984	NA	NA
19	Phosphorous as P	mg/l	0.021	IS 3025 Part 31 Sec 1: 2022 (Stannous Chloride method)	NA	NA
20	Total hardness as CaCO3	mg/l	310.0	IS 3025 (Part 21): 2009	200	600
21	Turbidity, NTU	NTU	BLQ(LOQ:0.1)	IS 3025 (Part 10): 1984	1	5
22	Arsenic	mg/l	BLQ (LOQ: 0.005)	USEPA 200.8: 1994	0.01	No relaxation
23	Barium	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8: 1994	0.7	No relaxation
24	Cadmium	mg/l	BLQ (LOQ: 0.001)	USEPA 200.8: 1994	0.003	No relaxation
25	Chromium	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	0.05	No relaxation
26	Copper	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	0.05	1.5



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization. 2. Samples are not drawn by HECS unless or otherwise mentioned. 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances tab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items.

HECS.C/O/FAIT/049 HECS-G/Q/FMT/049

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) BIS FSSAI Notified Laboratory ISO 9001, 14001 & 45001 Certified.



TEST REPORT

Page: 3 of 4

ULR

: TC1231025000016363F

Report No.

HECSL/WT/042/180325

Sample ID No

: 180325152

Sampling Date

Received Date

Completed On

Report Date

: 18/03/2025

: 18/03/2025

: 04/04/2025

: 04/04/2025

Commenced Date: 18/03/2025

Sample quantity : 2 Litres

Address of the Client

: Vaipur Mathur

: M/s. SIPCOT

with the same of

Sample Name

Group

: Water

: Ground Water

Sample Mark

: Kanchivakkam

Sample Reference

: NA

Sample Drawn By

: M/s.Hubert Enviro care Systems (P) Ltd.

Sample Location

: NA

Environmental Condition

: Temperature (°C) : 27.8 | Humidity (%) : 56.0

Sampling Method & Plan

: IS 17614(Part-1):2021

S.No.	Test Parameters	Units	Results	Test Method	IS 10500	: 2012
				0.000,700,000,000	Acceptable Limits (Max)	Permissible Limits (Max)
27	Lead	mg/l	BLQ (LOQ: 0.005)	USEPA 200.8: 1994	10.0	No relaxation
28	Mercury	mg/l	BLQ (LOQ: 0.0005)	USEPA 200.8: 1994	0.001	No relaxation
29	Nickel	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8: 1994	0.02	No relaxation
30	Zinc	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8: 1994	5	15
31	Phenolic compounds as C6H5OH	mg/l	BLQ(LOQ:0.00 1)	IS 3025 Part 43 Sec 1: 2022	0.001	0.002
32	Anionic Surface Active agents as MBAS	mg/I	BLQ(LOQ:0.05)	APHA 23rd edition (Method 5540 B , C): 2017	0.2	.1
33	Percent Sodium	%	52.84	HECS /WT/SOP/002:: 2019	NA	NA
34	Barium	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8: 1994	0.7	No relaxation
35	Residual Sodium Carbonate	meq/l	2.0	IS 11624: 2019	0.2	1.0
36	Ammonia as NH3	mg/l	BLQ(LOQ:0.02)	IS 3025 Part 34:Sec 2: 2021 (Nesslerization Method)	0.5	No relaxation
3.7	Sodium Adsorption Ratio(SAR)	Square root of (millimole/lit	3.1	IS 11624 : 2019	NA	NA
38	Dissolved oxygen	mg/l	6.5	IS 3025 (Part 38): 1989 (Titrimetric Method)	NA	NA



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization. 2. Samples are not drawn by HECS unless or otherwise mentioned. 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items.

HECS-G/O/FMT/049

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) **BIS FSSAI Notified Laboratory** ISO 9001, 14001 & 45001 Certified.

Name of the Client

Address of the Client

TEST REPORT

Page: 4 of 4

ULR : TC1231025000016363F

: 18/03/2025

: 04/04/2025

: 04/04/2025

Report No. HECSL/WT/042/180325 Sample ID No : 180325152

: 18/03/2025 Sampling Date

Commenced Date: 18/03/2025

Sample quantity : 2 Litres

Received Date

Completed On

Report Date

: Vaipur Mathur

: M/s. SIPCOT

Group : Water

Sample Name : Ground Water Sample Mark : Kanchivakkam

Sample Reference

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location

Environmental Condition

Sampling Method & Plan : IS 17614(Part-1):2021

: Temperature (°C): 27.8 | Humidity (%): 56.0

S.No.	Test Parameters	Units	Results	Test Method	IS 10500 : 2012	
					Acceptable Limits (Max)	Permissible Limits (Max)
39	Biological Oxygen Demand (BOD)@ 27°C For 3 days	mg/l	BLQ(LOQ:2,0)	IS 3025 Part 44: 1993	NA .	NA
40	Chemical Oxygen Demand (COD)	mg/l	BLQ(LOQ:4.0)	IS 3025 Part 58: 2006	NA	NA
41	Selenium	mg/l	BLQ (LOQ: 0.005)	USEPA 200.8: 1994	0.01	No relaxation
42	Manganese	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8: 1994	0.1	0.3
43	Total alkalinity as CaCO3	mg/l	270.0	1S 3025 (Part 23): 1986	200	600
44	Phosphate as PO4	mg/l	BLQ(LOQ:0.02)	IS 3025 Part 31 Sec 1: 2022	NA	NA

Note:- BLQ - Below the Limit of Quantification, LOQ-Limit of Quantification, NTU-Nephelometric Turbidity Unit, mg/l- Milligrams per litre, NA - Not Applicable.

End of Report



D.Anusuya Lab Manager Authorized Signatory

1. The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization. 2. Samples are not drawn by HECS unless or otherwise mentioned 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items. HECS-G/Q/FMT/049 Hubert Enviro Care Systems (P) Ltd. A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in

Laboratory Services Division (Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) BIS, FSSAI Notified Laboratory ISO 9001, 14001 & 45001 Certified.

TEST REPORT

Page: Lof I

Report No.

HECSL/WT/042/180325N

Sample ID No

Received Date

Completed On

Report Date

Commenced Date: 18/03/2025

Sample quantity : 2 Litres

: 180325152

Sampling Date

: 18/03/2025

: 18/03/2025

: 04/04/2025

: 04/04/2025

Address of the Client

Name of the Client

: Vaipur Mathur

: M/s. SIPCOT

Group

: Water

Sample Name

: Ground Water

Sample Mark

: Kanchiyakkam

Sample Reference Sample Drawn By : NA

: M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location Environmental Condition

: Temperature (°C): 27.8 | Humidity (%): 56.0

Sampling Method & Plan

: IS 17614(Part-1):2021

S.No.	Test Parameters	Units	Results	Test Method
Discipli	ine : Chemical			
	Hexavalent Chromium as Cr6+	mg/l	BLQ(LOQ:0.01)	IS 3025 Part 52 Clause 6: 2003

Note:- BLQ : Below Limit of Quantification, LOQ: Limit of Quantification, mg/l: milligram per Litre. ***End of Report***



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization. 2. Samples are not drawn by HECS unless or otherwise mentioned. 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss/damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items. HECS-G/O/FMT/49

A-21, III Phase, Thiru Vi Ka Industrial Estate.

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) **BIS FSSAI Notified Laboratory** ISO 9001, 14001 & 45001 Certified.

Name of the Client

TEST REPORT

Page: 1 of 4

ULR

: TC1231025000016364F

Report No.

HECSL/WT/043/180325

Sample ID No

: 180325153

Sampling Date

: 18/03/2025

Address of the Client

: Vaipur Mathur

: M/s. SIPCOT

: Water

Received Date

: 18/03/2025

Sample Name

Group

: Ground Water

Commenced Date: 18/03/2025

Sample Mark

: Mathur

Completed On

: 04/04/2025

Sample Reference

: NA

Report Date

: 04/04/2025

Sample Drawn By

: M/s.Hubert Enviro care Systems (P) Ltd.

Sample Location

Sample quantity : 2 Litres

Environmental Condition Sampling Method & Plan : Temperature (°C): 27.8 | Humidity (%): 56.0

: IS 17614(Part-1):2021

IS 10500 : 2012 Test Parameters Units Results S.No. Test Method Acceptable Limits Permissible (Max) Limits (Max) Discipline : Chemical Bi carbonate 317.2 IS 3025 Part 51: 2001 mg/l NA NA Boron as B mg/l BLQ(LOQ:0.1) IS 3025 Part 57 -Curcumin Method: 0.5 2.4 2021 Calcium as Ca 116.23 IS 3025 Part 40: 1991(EDTA mg/l 75 200 Titrimetric Method) Carbonate mg/1BLQ(LOQ:1.0) IS 3025 Part 51: 2001 NA NA Chloride as Cl mg/l 197.95 IS 3025 Part 32: 1988 (250 1000 Argentometric Method) 6 Cyanide as CN mg/l BLQ(LOQ:0.01) IS 3025 Part 27 Sec 1: 2021 0.05 No relaxation Electrical Conductivity at 1340.0 IS 3025 Part-14: 2013 µS/cm NA NA 25°C Fluoride as F 0.45 APHA 23rd edition (Method 4500Fmg/l 1.0 1.5 B, D): 2017 Iron as Fe mg/l 0.045 IS 3025 (Part 53): 2003 1.0 No relaxation 10 Magnesium as Mg mg/l 14.58 IS 3025 Part 46: 1994 (Valumetric 30 100 Method using EDTA) 11 Nitrate as NO3 mg/l 20.59 APHA 23rd edition (Method 4500) 45 No relaxation NO3B): 2017 12 Colour Hazen units BLQ(LOQ:1.0) IS 3025 (Part4): 2021 15 13 pH at 25°C 6.89 IS 3025(Part 11): 2022 6.5-8.5 No relaxation (Electrometric method)



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization. 2. Samples are not drawn by HECS unless or otherwise mentioned. 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items.

HECS-G/O/FMT/049 HECS-G/Q/FMT/049

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) **BIS FSSAI Notified Laboratory** ISO 9001, 14001 & 45001 Certified.



Name of the Client

TEST REPORT

Page: 2 of 4

ULR : TC1231025000016364F

Report No. HECSL/WT/043/180325

: 18/03/2025

: 04/04/2025

: 04/04/2025

Sample ID No : 180325153

Received Date

Completed On

Report Date

Sampling Date : 18/03/2025

Commenced Date: 18/03/2025

Sample quantity : 2 Litres

Address of the Client

: Vaipur Mathur

: M/s. SIPCOT

Group

: Water

Sample Name

: Ground Water

Sample Mark

: Mathur

Sample Reference

Sample Drawn By

: NA

Sample Location

: M/s. Hubert Enviro care Systems (P) Ltd.

Environmental Condition

: Temperature (°C): 27.8 | Humidity (%): 56.0

Sampling Method & Plan

S.No.	Test Parameters	Units	Results	Test Method	1S 10500 : 2012	
					Acceptable Limits (Max)	Permissible Limits (Max)
14	Potassium as K	mg/l	9.0	IS 3025 Part 45: 1993 (Fleme emission Photometric Method)	NA	NA
15	Sodium as Na	mg/l	120.0	IS 3025 Part 45: 1993 (Fleme emission Photometric Method)	NA	NA
16	Sulphate as SO4	mg/l	55.83	IS 3025 Part 24 Sec 1: 2022(Turbidity Method)(Turbidity Method)	200	400
17	Total dissolved solids	mg/l	708.0	IS 3025 (Part 16): 1984	500	2000
18	Total Suspended Solids	mg/l	BLQ(LOQ:2.0)	IS 3025 (Part 17): 1984	NA	NA
19	Phosphorous as P	mg/l	0.033	IS 3025 Part 31 Sec 1: 2022 (Stannous Chloride method)	NA	NA
20	Total hardness as CaCO3	mg/l	350.0	IS 3025 (Part 21): 2009	200	600
21	Turbidity, NTU	NTU	BLQ(LOQ:0.1)	IS 3025 (Part 10): 1984	1	5
22	Arsenic	mg/I	BLQ (LOQ: 0.005)	USEPA 200.8: 1994	0.01	No relaxation
23	Barium	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8: 1994	0.7	No relaxation
24	Cadmium	mg/l	BLQ (LOQ: 0.001)	USEPA 200.8: 1994	0.003	No relaxation
25	Chromium	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	0.05	No relaxation
26	Copper	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8: 1994	0.05	1.5



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization. 2. Samples are not drawn by HECS unless or otherwise mentioned. 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances tab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items.

HECS-C/O/FMT/049 HECS-G/Q/FMT/049

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) **BIS FSSAI Notified Laboratory** ISO 9001, 14001 & 45001 Certified.



TEST REPORT

Page: 3 of 4

ULR : TC1231025000016364F

Report No.

HECSL/WT/043/180325

Sample ID No

: 180325153

: M/s. SIPCOT

Sampling Date

: 18/03/2025

Address of the Client

Name of the Client

: Vaipur Mathur

Group

: Water

Received Date

: 18/03/2025

Sample Name

: Ground Water

Commenced Date: 18/03/2025

Sample Mark

: Mathur

Completed On

: 04/04/2025

Sample Reference

: NA

: 04/04/2025

Report Date

Sample Drawn By

: M/s. Hubert Enviro care Systems (P) Ltd.

Sample quantity : 2 Litres

Sample Location **Environmental Condition**

: Temperature (°C): 27.8 | Humidity (%): 56.0

Sampling Method & Plan

: IS 17614(Part-1):2021

S.No.	Test Parameters	Units	Results	Test Method	IS 10500 : 2012	
					Acceptable Limits (Max)	Permissible Limits (Max)
27	Lead	mg/l	BLQ (LOQ: 0.005)	USEPA 200.8: 1994	0.01	No relaxation
28	Mercury	mg/l	BLQ (LOQ: 0.0005)	USEPA 200.8: 1994	0.001	No relaxation
29	Nickel	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8: 1994	0.02	No relaxation
30	Zinc	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8: 1994	5	15
31	Phenolic compounds as C6H5OH	mg/l	BLQ(LOQ:0.00 1)	IS 3025 Part 43 Sec 1: 2022	0.001	0.002
32	Anionic Surface Active agents as MBAS	mg/l	BLQ(LOQ:0.05)	APHA 23rd edition (Method 5540 B , C): 2017	0.2	1
33	Percent Sodium	%	41.82	HECS /WT/SOP/002:: 2019	NA	NA
34	Barium	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	0.7	No relaxation
35	Residual Sodium Carbonate	meq/l	BLQ(LOQ:1.0)	IS 11624: 2019	0.2	1.0
36	Ammonia as NH3	mg/l	BLQ(LOQ:0.02)	IS 3025 Part 34:Sec 2: 2021 (Nesslerization Method)	0.5	No relaxation
37	Sodium Adsorption Ratio(SAR)	Square root of (millimole/lit	2.8	IS 11624 : 2019	NA	NA
38	Dissolved oxygen	mg/l	6.4	IS 3025 (Part 38): 1989 (Titrimetric Method)	NA	NA



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization. 2. Samples are not drawn by HECS unless or otherwise mentioned. 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances tab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items.

HECS-C/O/FMT/M49 HECS-G/Q/FMT/049

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) **BIS FSSAI Notified Laboratory** ISO 9001, 14001 & 45001 Certified.



Name of the Client

TEST REPORT

Page: 4 of 4

ULR

: TC1231025000016364F

Report No.

: HECSL/WT/043/180325

Sample ID No

: 180325153

Sampling Date

Received Date

Completed On

Report Date

Commenced Date: 18/03/2025

Sample quantity : 2 Litres

: 18/03/2025

: 18/03/2025

: 04/04/2025

: 04/04/2025

Address of the Client

: Vaipur Mathur

: M/s. SIPCOT

Group

: Water

Sample Name

: Ground Water : Mathur

Sample Mark

Sample Reference Sample Drawn By : NA

: M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location **Environmental Condition**

: Temperature (°C): 27.8 | Humidity (%): 56.0

Sampling Method & Plan

: IS 17614(Part-1):2021

S.No.	Test Parameters	Units	Results	Test Method	IS 10500 : 2012	
					Acceptable Limits (Max)	Permissible Limits (Max)
39	Biological Oxygen Demand (BOD)@ 27°C For 3 days	mg/l	BLQ(LOQ:2.0)	IS 3025 Part 44: 1993	NA	NA
40	Chemical Oxygen Demand (COD)	mg/l	BLQ(LOQ:4.0)	IS 3025 Part 58; 2006	NA	NA
9.1.	Selenium	mg/l	BLQ (LOQ: 0.005)	USEPA 200.8: 1994	0.01	No relaxation
12	Manganese	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	0.1	0.3
43	Total alkalinity as CaCO3	mg/l	260.0	IS 3025 (Part 23): 1986	200	600
14	Phosphate as PO4	mg/l	BLQ(LOQ:0.02)	IS 3025 Part 31 Sec 1: 2022	NA	NA

Note: - BLQ - Below the Limit of Quantification, LOQ- Limit of Quantification, NTU- Nephelometric Turbidity Unit, mg/l- Milligrams per litre, NA - Not Applicable d.

End of Report



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization. 2. Samples are not drawn by HECS unless or otherwise mentioned. 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items.

HECS_CIO/FMT/M49 HECS-G/O/FMT/049

Hubert Enviro Care Systems (P) Ltd. A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in

Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) BIS, FSSAI Notified Laboratory ISO 9001, 14001 & 45001 Certified.

TEST REPORT

Page: 1 of 1

Report No.

: HECSL/WT/043/180325N

Sample ID No

: 180325153

Sampling Date

: 18/03/2025

Address of the Client

Name of the Client

: Vaipur Mathur

: M/s. SIPCOT

Received Date

: 18/03/2025

Group Sample Name : Water

Commenced Date: 18/03/2025

: Ground Water

Completed On

: 04/04/2025

Sample Mark Sample Reference : Mathur : NA

: 04/04/2025

Sample Drawn By

: M/s. Hubert Enviro care Systems (P) Ltd.

Report Date

Sample Location

Sample quantity : 2 Litres

Environmental Condition

: Temperature (°C): 27.8 | Humidity (%): 56.0

Sampling Method & Plan

: IS 17614(Part-1):2021

S.No.	Test Parameters	Units	Results	Test Method
Discipl	ine : Chemical			
1	Hexavalent Chromium as Cr6+	mg/l	BLQ(LOQ:0.01)	IS 3025 Part 52 Clause 6: 2003

Note:- BLQ : Below Limit of Quantification, LOQ: Limit of Quantification, mg/l: milligram per Litre. ***End of Report***



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization. 2. Samples are not drawn by HECS unless or otherwise mentioned. 3. Unless specifically requested by customer the text items will not be retained more than 15 days from the date of issue of text report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of text report after invoicing or issue of text report. 5. The text results relate only to the text items.

HECS COVENTIAL HECS-G/Q/FMT/49

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing)
Recognized by CPCB (MoEF & CC)
BIS FSSAI Notified Laboratory
ISO 9001, 14001 & 45001 Certified.



Name of the Client

TEST REPORT

Page: 1 of 4

ULR : TC1231025000016889F

Report No. : HECSL/WT/044/180325

Sample ID No : 180325154

Sampling Date : 18/03/2025

Address of the Client : Vaipur Mathur

Group : Water Received Date : 18/03/2025

 Sample Name
 Surface Water
 Commenced Date: 18/03/2025

 Sample Mark
 : Vallakottai
 Completed On : 07/04/2025

 Sample Reference
 : NA
 Report Date : 07/04/2025

Sample Reference : NA Report Date : 07/04/20
Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd. Sample quantity : 2 Litres

Sample Location : NA

: M/s. SIPCOT

Environmental Condition : Temperature (°C): 27.8 | Humidity (%): 56.0

Sampling Method & Plan : IS 17614(Part-1):2021

S.No.	Test Parameters	Units	Results	Test Method	Inland Surface water Standards (Schedule -VI)
Discip	dine : Chemical				
1	Total alkalinity as CaCO3	mg/l	230.0	IS 3025 Part 23: 1986	NA
2	Bi carbonate	mg/l	280.6	IS 3025 Part 51: 2001	NA
3	Biological Oxygen Demand (BOD)@ 27°C For 3 days	mg/l	2.0	IS 3025 Part 44: 1993	30
4	Boron as B	mg/l	BLQ(LOQ:0.1)	1S 3025 Part 57: 2021 (Curcumin Method)	NA
5	Calcium as Ca	mg/l	26.05	IS 3025 Part 40: 1991(EDTA Titrimetric Method)	NA
6	Chemical Oxygen Demand (COD)	mg/l	16.0	IS 3025 Part 58: 2006	250
7	Chloride as Cl	mg/l	133.61	IS 3025 Part 32: 1988 (Argentometric Method)	NA
8	Colour	Hazen units	BLQ(LOQ:1.0)	IS 3025 Part 4: 2021	NA
9	Dissolved oxygen	mg/l	6.0	IS 3025 Part 38: 1989	NA
10	Electrical Conductivity at 25°C	μS/cm	910.0	1S:3025 Part 14: 2013	NA
11	Fluoride as F	mg/l	0.41	APHA 23rd edition Method 4500 F -B,D: 2017	2.0
12	Iron as Fe	mg/l	0.101	IS 3025 Part 53: 2003	3.0
13	Nitrate as NO3	mg/l	6.87	APHA 23rd edition Method 4500 NO3B; 2017	NA



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization 2. Samples are not drawn by HECS unless or otherwise mentioned 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after involcing or issue of test report. 5. The test results relate only to the test items.

HECS-G/O/FMT/049

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) **BIS FSSAI Notified Laboratory** ISO 9001, 14001 & 45001 Certified.



Name of the Client

Address of the Client

TEST REPORT

Results

BLQ (LOQ: 0.01)

BLQ (LOQ: 0.005)

0.127

8.11

484.0

BLQ(LOQ:1.0)

BLQ(LOQ:0.01)

18.23

10.0

124.0

13.74

BLQ(LOQ:0.001)

BLQ(LOQ:0.05)

Page: 2 of 4

NA

NA

0.2

NA

NA

NA

NA

1.0

ULR

: TC1231025000016889F

Report No.

: HECSL/WT/044/180325

Sample ID No

Received Date : 18/03/2025

: 180325154

Sampling Date

: 18/03/2025

: Vaipur Mathur

: M/s. SIPCOT

Group

S.No.

14

15

16

17

18

20

21

22

23

24

25

26

: Water

Sample Name

Surface Water

Sample Mark

: Vallakottai

Sample Reference

: NA

Sample Drawn By

: M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location

Test Parameters

Environmental Condition

: Temperature (°C): 27.8 | Humidity (%): 56.0

Units

mg/l

mg/l

mg/f

mg/l

mg/l

mg/l

mg/l

mg/l

mg/l

mg/l

mg/l

mg/l

Sampling Method & Plan

Manganese

Selenium

pH at 25°C

Carbonate

Cyanide as CN

Potassium as K.

Sodium as Na

Sulphate as SO4

Phenolic compounds as C6H5OH

Anionic Surface Active agents as MBAS

Magnesium as Mg

Phosphate as PO4

Total dissolved solids

: IS 17614(Part-1):2021

	Commenced Da	te: 18/03/2025	5
	Completed On	: 07/04/2025	5
	Report Date	: 07/04/2025	5
	Sample quantit	y:2 Litres	
5.0			
	Test Meti	nod	Inland Surface water Standards (Schedule -VI)
	USEPA 200.8	: 1994	2.0
	USEPA 200.8	: 1994	0.05
AP	HA 23rd edition M B,D: 201		NA
IS 3	025 Part 11: 2022 Method		5.5 – 9.0



D.Anusuva Lab Manager Authorized Signatory

IS 3025 Part 16: 1984

IS 3025 Part 51: 2001

IS 3025 Part 27 sec 1: 2021

IS 3025 Part 46: 1994 (Valumetric

Method using EDTA)

IS 3025 Part 45: 1993

IS 3025 Part 45: 1983

IS 3025 Part 24 Sec 1: 2022

IS 3025 Part 43:Sec 1: 2022

APHA 23rd edition Method 5540 B. C: 2017

^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization 2. Samples are not drawn by HECS unless or otherwise mentioned 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items. HECS-G/O/FMT/049

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) **BIS FSSAI Notified Laboratory** ISO 9001, 14001 & 45001 Certified.



Name of the Client

TEST REPORT

Page: 3 of 4

ULR

: TC1231025000016889F

Report No.

: HECSL/WT/044/180325

Sample 1D No

: 180325154

Sampling Date

: 18/03/2025

Address of the Client

: Vaipur Mathur

: M/s. SIPCOT

: Water

Received Date

: 18/03/2025

Sample Name

Group

: Surface Water

Commenced Date: 18/03/2025

Sample Mark

: Vallakottai

Completed On

: 07/04/2025

Sample Reference

: NA

: 07/04/2025

Sample Drawn By

: M/s. Hubert Enviro care Systems (P) Ltd.

Report Date

Sample quantity : 2 Litres

Sample Location Environmental Condition

: Temperature (°C): 27.8 | Humidity (%): 56.0

Sampling Method & Plan

: IS 17614(Part-1):2021

S.No.	Test Parameters	Units	Results	Test Method	Inland Surface water Standards (Schedule -VI)
27	Percent Sodium	%	63.66	HECSG /WT/SOP/002 Issue No:01,Issue date 18.12: 2021	NA NA
28	Barium	mg/I	BLQ (LOQ: 0.01)	USEPA 200,8 : 1994	NA
29	Residual Sodium Carbonate	mg/l	1.78	IS 11624: 2019	NA.
30	Ammonia as NH3	mg/I	0.41	IS 3025 Part 34 Sec 2: 2021	5.0
31	Sodium Adsorption Ratio(SAR)	Square root of (millimole/lit r	4.54	IS 11624: 2019	NA
32	Total Hardness as CaCO3	mg/l	140.0	IS 3025 Part 21: 2009	NA
33	Total Phosphorous as P	mg/l	0.04	IS 3025 Part 31 Sec 1: 2022	NA
34	Total Suspended Solids	mg/l	15.0	1S 3025 Part 17: 1984	100
35	Turbidity	NTU	1.4	IS 3025 Part 10: 1984	NA
36	Arsenic	mg/l	BLQ (LOQ: 0.005)	USEPA 200.8 : 1994	0.2
37	Cadmium	mg/l	BLQ (LOQ: 0.001)	USEPA 200.8: 1994	2.0
38	Chromium	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8: 1994	2.0
39	Copper	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8: 1994	3.0



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization 2. Samples are not drawn by HECS unless or otherwise mentioned 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items.

HECS-G/O/FMT/049 HECS-G/Q/FMT/049

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) **BIS FSSAI Notified Laboratory** ISO 9001, 14001 & 45001 Certified.



TEST REPORT

Page: 4 of 4

ULR

: TC1231025000016889F

Report No.

: HECSL/WT/044/180325

Sample ID No

: 180325154

Sampling Date

: 18/03/2025

Address of the Client

: Vaipur Mathur

: M/s. SIPCOT

Group

: Water

: Surface Water

Sample Name Sample Mark

: Vallakottai

Sample Reference

: NA

Sample Drawn By Sample Location : M/s. Hubert Enviro care Systems (P) Ltd.

Environmental Condition Sampling Method & Plan

: Temperature (°C): 27.8 | Humidity (%): 56.0 : IS 17614(Part-1):2021

Received Date : 18/03/2025

Commenced Date: 18/03/2025 Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 2 Litres

S.No.	Test Parameters	Units	Results	Test Method	Inland Surface water Standards (Schedule -VI)
40	Lead	mg/l	BLQ (LOQ: 0.005)	USEPA 200.8 : 1994	0.1
41	Mercury	mg/l	BLQ (LOQ: 0.0005)	USEPA 200.8: 1994	0.01
42	Nickei	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8: 1994	3.0
43	Zinc	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8: 1994	5.0

Note:- BLQ - Below the Limit of Quantification, LOQ-Limit of Quantification, mg/l - Milligrams per liter. ""End of Report""



Hubert Enviro Care Systems (P) Ltd. A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in

Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) BIS, FSSAI Notified Laboratory ISO 9001, 14001 & 45001 Certified.

TEST REPORT

Page: 1 of 1

Report No.

: HECSL/WT/044/180325N

Sample ID No

: 180325154

Sampling Date

Received Date

Completed On

Report Date

: 18/03/2025

: 18/03/2025

: 07/04/2025

: 07/04/2025

Commenced Date: 18/03/2025

Sample quantity : 2 Litres

Address of the Client

Name of the Client

: Vaipur Mathur

: M/s. SIPCOT

Group

: Water

Sample Name

: Surface Water

Sample Mark

: Vallakottai

: NA

Sample Reference

: M/s.Hubert Enviro care Systems (P) Ltd.

Sample Drawn By

Sample Location Environmental Condition

: Temperature (°C): 27.8 | Humidity (%): 56.0

Samp S.No.		Part-1):2021 Units	Results	Test Method	Inland Surface
12-52-51-50					(Schedule -VI)
Discip	oline : Chemical				
1	Hexavalent Chromium as Cr6+	mg/l	BLQ(LOQ:0.01)	IS 3025 Part 52 Clause 6: 2003	0.1

Note:- BLQ : Below the Limit of Quantification, LOQ: Limit of Quantification, mg/l: milligram per Litre, % - Percentage. ***End of Report***



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization. 2. Samples are not drawn by HECS unless or otherwise mentioned. 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items. HECS-G/Q/FMT/49

A-21, III Phase, Thiru Vi Ka Industrial Estate, Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) **BIS FSSAI Notified Laboratory** ISO 9001, 14001 & 45001 Certified.



Name of the Client

Address of the Client

TEST REPORT

Page: 1 of 4

ULR

Commenced Date: 18/03/2025

Sample quantity : 2 Litres

: TC1231025000016890F

Report No.

HECSL/WT/045/180325

Sample ID No

: 180325155

Sampling Date

Received Date

Completed On

Report Date

: 18/03/2025

: 18/03/2025

: 07/04/2025

: 07/04/2025

: Vaipur Mathur

: M/s. SIPCOT

Group

: Water

Sample Name

: Surface Water

: Perinjambakkam

Sample Mark Sample Reference

: NA

Sample Drawn By

Sample Location

: M/s. Hubert Enviro care Systems (P) Ltd.

Environmental Condition

: Temperature (°C): 27.8 | Humidity (%): 56.0

Sampling Method & Plan

: IS 17614(Part-1):2021

S.No.	Test Parameters	Units	Results	Test Method	Inland Surface water Standards (Schedule -VI)
Discip	line : Chemical				
1	Total alkalinity as CaCO3	mg/l	125.0	IS 3025 Part 23: 1986	NA
2	Bi carbonate	mg/l	152.5	IS 3025 Part 51: 2001	NA
3	Biological Oxygen Demand (BOD)(a) 27°C For 3 days	mg/l	2.0	IS 3025 Part 44: 1993	30
4	Boron as B	mg/l	BLQ(LOQ:0.1)	IS 3025 Part 57: 2021 (Curcumin Method)	NA
5	Calcium as Ca	mg/l	28.06	1S 3025 Part 40: 1991(EDTA Titrimetric Method)	NA
6	Chemical Oxygen Demand (COD)	mg/l	20.0	IS 3025 Part 58: 2006	250
7	Chloride as Cl	mg/l	49.45	IS 3025 Part 32: 1988 (Argentometric Method)	NA
8	Colour	Hazen units	BLQ(LOQ:1.0)	IS 3025 Part 4: 2021	NA
9	Dissolved oxygen	mg/l	5.9	IS 3025 Part 38: 1989	NA
10	Electrical Conductivity at 25°C	μS/cm	470.0	IS:3025 Part 14: 2013	NA
11	Fluoride as F	mg/l	0.28	APHA 23rd edition Method 4500 F -B,D: 2017	2.0
12	Iron as Fe	mg/l	0.081	IS 3025 Part 53: 2003	3.0
13	Nitrate as NO3	mg/l	5.42	APHA 23rd edition Method 4500 NO3B: 2017	NA



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization 2. Samples are not drawn by HECS unless or otherwise mentioned 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items. HECS-G/O/FMT/049

A-21, III Phase, Thiru Vi Ka Industrial Estate. Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) BIS FSSAI Notified Laboratory ISO 9001, 14001 & 45001 Certified.



Name of the Client

TEST REPORT

Page: 2 of 4

ULR

: TC1231025000016890F

Report No.

: HECSL/WT/045/180325

Sample 1D No

: 180325155

Sampling Date

: 18/03/2025

Address of the Client

: Vaipur Mathur

: M/s. SIPCOT

: Water

Received Date

: 18/03/2025

Sample Name

Surface Water

Commenced Date: 18/03/2025

Sample Mark

Group

: Perinjambakkam

Completed On

: 07/04/2025

Sample Reference

Report Date

: 07/04/2025

Sample Drawn By

: M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location

Sample quantity : 2 Litres

Environmental Condition

: Temperature (°C): 27.8 | Humidity (%): 56.0

Sampling Method & Plan

: IS 17614(Part-1):2021

S.No.	Test Parameters	Units	Results	Test Method	Inland Surface water Standards (Schedule -VI)
14	Manganese	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8: 1994	2.0
15	Selenium	mg/l	BLQ (LOQ: 0.005)	USEPA 200.8 : 1994	0.05
16	Phosphate as PO4	mg/I	0.103	APHA 23rd edition Method 4500-P B,D: 2017	NA
17	pH at 25°C		7.39	1S 3025 Part 11: 2022 (Electrometric Method)	5.5 - 9.0
18	Total dissolved solids	mg/l	235.0	IS 3025 Part 16: 1984	NA
19	Carbonate	mg/l	BLQ(LOQ:1.0)	IS 3025 Part 51: 2001	NA
20	Cyanide as CN	mg/l	BLQ(LOQ:0.01)	IS 3025 Part 27 sec 1; 2021	0.2
21	Magnesium as Mg	mg/l	12.15	IS 3025 Part 46: 1994 (Valumetric Method using EDTA)	NA
22	Potassium as K	mg/l	4.0	IS 3025 Part 45: 1993	NA
23	Sodium as Na	mg/l	39.0	IS 3025 Part 45: 1983	NA
24	Sulphate as SO4	mg/l	8.12	IS 3025 Part 24 Sec 1: 2022	NA
25	Phenolic compounds as C6H5OH	mg/l	BLQ(LOQ:0.001)	IS 3025 Part 43:Sec 1: 2022	1.0
26	Anionic Surface Active agents as MBAS	mg/l	BLQ(LOQ:0.05)	APHA 23rd edition Method 5540 B , C: 2017	NA



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization. 2. Samples are not drawn by HECS unless or otherwise mentioned. 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items. HECS-G/Q/FMT/049

A-21, III Phase, Thiru Vi Ka Industrial Estate, Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) **BIS FSSAI Notified Laboratory** ISO 9001, 14001 & 45001 Certified.

TEST REPORT

Page: 3 of 4

ULR

: TC1231025000016890F

Report No.

: HECSL/WT/045/180325

Sample ID No

: 180325155

Sampling Date

: 18/03/2025

: Vaipur Mathur

: Water

Received Date

: 18/03/2025

Sample Name

Group

: Surface Water

: M/s. SIPCOT

Commenced Date: 18/03/2025

: 07/04/2025

Sample Mark

; Perinjambakkam

Completed On

: 07/04/2025

Sample Reference

Name of the Client

Address of the Client

Report Date

Sample Drawn By

: M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location

Sample quantity : 2 Litres

Environmental Condition

: Temperature (°C): 27.8 | Humidity (%): 56.0

S.No.	Test Parameters	Units	Results	Test Method	Inland Surface water Standards (Schedule -VI)
27	Percent Sodium	%	40.24	HECSG /WT/SOP/002 Issue No:01,Issue date 18.12: 2021	NA
28	Barium	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8: 1994	NA
29	Residual Sodium Carbonate	mg/l	BLQ(LOQ:1.0)	IS 11624: 2019	NA
30	Ammonia as NH3	mg/l	0.29	IS 3025 Part 34 Sec 2: 2021	5.0
31	Sodium Adsorption Ratio(SAR)	Square root of (millimole/lit r	1.54	IS 11624: 2019	NA
32	Total Hardness as CaCO3	mg/l	120.0	IS 3025 Part 21: 2009	NA
33	Total Phosphorous as P	mg/l	0.03	IS 3025 Part 31 Sec 1: 2022	NA
34	Total Suspended Solids	mg/l	4.0	IS 3025 Part 17: 1984	100
35	Turbidity	NTU	1.9	IS 3025 Part 10: 1984	NA
36	Arsenic	mg/l	BLQ (LOQ: 0.005)	USEPA 200.8 : 1994	0.2
37	Cadmium	mg/l	BLQ (LOQ: 0.001)	USEPA 200.8 : 1994	2.0
38	Chromium	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8: 1994	2.0
39	Copper	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8: 1994	3.0



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization 2. Samples are not drawn by HECS unless or otherwise mentioned 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items. HECS-G/Q/FMT/049

A-21, III Phase, Thiru Vi Ka Industrial Estate. Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) **BIS FSSAI Notified Laboratory** ISO 9001, 14001 & 45001 Certified.



Name of the Client

Address of the Client

TEST REPORT

Page: 4 of 4

ULR

: TC1231025000016890F

Report No.

HECSL/WT/045/180325

Sample ID No

: 180325155

Sampling Date

Received Date

Completed On

Report Date

Commenced Date: 18/03/2025

Sample quantity : 2 Litres

: 18/03/2025

: 07/04/2025

: 07/04/2025

: 18/03/2025

Sample Name

: Vaipur Mathur

: M/s. SIPCOT

Group

: Water

: Surface Water

Sample Mark Sample Reference ; Perinjambakkam

Sample Drawn By

: M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location

Environmental Condition

: Temperature (°C): 27.8 | Humidity (%): 56.0

Sampli	Sampling Method & Plan : IS 17614(Part-1):2021							
S.No.	Test Parameters	Units	Results	Test Method	Inland Surface water Standards (Schedule -VI)			
40	Lead	mg/l	BLQ (LOQ: 0.005)	USEPA 200.8 : 1994	0.1			
41	Mercury	mg/l	BLQ (LOQ: 0.0005)	USEPA 200.8 : 1994	0.01			
42	Nickel	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	3.0			
43	Zinc	me/I	BLO (LOO: 0.01)	LISEPA 200 8 - 1994	5.0			

Note:- BLQ - Below the Limit of Quantification, LOQ-Limit of Quantification, mg/l - Milligrams per liter. ***End of Report***



D.Anusuya Lab Manager Authorized Signatory

1. The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization. 2. Samples are not drawn by HECS unless or otherwise mentioned. 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items.

HECS.CO/FIMT/049 HECS-G/Q/FMT/049 Hubert Enviro Care Systems (P) Ltd. A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in

Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) BIS, FSSAI Notified Laboratory ISO 9001, 14001 & 45001 Certified.

TEST REPORT

Page: 1 of 1

Report No.

: HECSL/WT/045/180325N

Sample ID No

: 180325155

Sampling Date

: 18/03/2025

Address of the Client

Name of the Client

: Vaipur Mathur

: M/s. SIPCOT

Received Date

: 18/03/2025

Sample Name

Group

: Water

Commenced Date: 18/03/2025

: Surface Water : Perinjambakkam

Completed On

: 07/04/2025

Sample Mark

Report Date

: 07/04/2025

Sample Reference Sample Drawn By

: M/s. Hubert Enviro care Systems (P) Ltd.

Sample quantity : 2 Litres

Sample Location

- NA

Environmental Condition

: Temperature (°C): 27.8 | Humidity (%): 56.0

Sampling Method & Plan

: IS 17614(Part-1):2021

S.No.		Units	Results	Test Method	Inland Surface water Standards (Schedule -VI)
Discip	pline : Chemical				
1	Hexavalent Chromium as Cr6+	mg/l	BLQ(LOQ:0.01)	IS 3025 Part 52 Clause 6: 2003	0.1

Note:- BLQ : Below the Limit of Quantification, LOQ: Limit of Quantification, mg/l: milligram per Litre, % - Percentage. ***End of Report***



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization. 2. Samples are not drawn by HECS unters or otherwise mentioned. 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items. HECS-G/Q/FMT/49

A-21, III Phase, Thiru Vi Ka Industrial Estate, Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) **BIS FSSAI Notified Laboratory** ISO 9001, 14001 & 45001 Certified.



Name of the Client

Address of the Client

TEST REPORT

Page: 1 of 2

ULR

: TC1231025000016847F

Report No.

: HECS/PE/035/180325

Sample ID No

: 180325156

: Vaipur Mathur

: M/s. SIPCOT

Sampling Date

: 18/03/2025

Group

: Pollution & Environment

Received Date

: 18/03/2025

Sample Name

: Soil

Commenced Date: 18/03/2025

Sample Mark

: Project Area

Completed On

: 05/04/2025

Sample Reference

: NA

Report Date

: 05/04/2025

Sample Drawn By

: M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location

Sample quantity : 1 Kg

Environmental Condition

: Temperature (°C): 27.8 | Humidity (%): 56.0

Sampling Method & Plan

: ICARDA:2013

S.No.	Test Parameters	Units	Results	Test Method
Discip	oline : Chemical		1	
1	Cadmium	mg/Kg	BLQ (LOQ: 0.1)	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021
2	Chromium	mg/Kg	32.02	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021
3	Copper	mg/Kg	26.00	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021
4	Zinc	mg/kg	23.31	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021
5	Soil Texture	-	Loam	FAO of United Nations, Rome Chapter - III 2008
6	Soil Texture i)Sand	%	35.2	FAO of United Nations, Rome Chapter - III 2008
7	Soil Texture ii)Silt	%	44.6	FAO of United Nations, Rome Chapter - 111 2008
8	Soil Texture iii)Clay	%	20.2	FAO of United Nations, Rome Chapter - III 2008
9	pH Value @ 25 ° C (1 : 2.5)	- 5	7.22	IS 2720 (Part 26) 1987
10	Electrical conductivity @ 25 ° C (1 : 2)	μS/cm	85.0	IS 14767: 2000



A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) **BIS FSSAI Notified Laboratory** ISO 9001, 14001 & 45001 Certified.

Name of the Client

Address of the Client

TEST REPORT

Page: 2 of 2

ULR

: TC1231025000016847F

Report No.

: HECS/PE/035/180325

Sample ID No

: 180325156

Sampling Date

: M/s. SIPCOT

: 18/03/2025

: Vaipur Mathur

Received Date : 18/03/2025

Sample Name

Group

: Pollution & Environment

Soil

Commenced Date: 18/03/2025

Sample Mark

: Project Area

Completed On

: 05/04/2025

Sample Reference

: NA

Report Date

: 05/04/2025

Sample Drawn By

: M/s, Hubert Enviro care Systems (P) Ltd.

Sample Location

Sample quantity : 1 Kg

Environmental Condition

: Temperature (°C): 27.8 | Humidity (%): 56.0

Sampling Method & Plan

· ICADDA - 7012

S.No.	Test Parameters	Units	Results	Test Method
11	Bulk Density	gm/cm3	0.99	FAO of United Nations Rome 2007
12	Organic Carbon	%	0.23	IS 2720 (Part 22) Section I 1972
13	Organic Matter	%	0.40	IS 2720 (Part 22) Section I 1972
14	Available Phosphorous as P	h8\ñ	5.67	FAO of United Nations, Rome Chapter - 1II 2008
15	Available Potassium	mEq/100g	15.18	FAO of United Nations, Rome Chapter III 2008
16	Boron as B	mg/kg	BLQ(LOQ 0.1)	HECS-G/ENV/SSW/SOP/018 Issue No.:01 Issue Date:02:07 2020
17	Total Nitrogen as N	%	0.0110	IS 14684 Clause 4 1999
18	Exchangable Calcium as Ca	mEq/L	9.45	FAO of United Nations, Rome Chapter- III 2008
19	Exchangable Magnesium as Mg	mEq/L	9.45	FAO of United Nations, Rome Chapter - III 2008
20	Cation Exchange Capacity	mEq/100g	2.2	IS 2720 (Part 24) Clause 5 1976
21	Water Holding capacity	%	29.4	IS 14765: 2000
22	Colour		Red	HECS-G/ENV/SSW/SOP/011 Issue No.:01 Issue Date:02:07: 2020

Note:- BLQ: Below the Limit of Quantification, LOQ: Limit of Quantification, mg/kg: milligram per kilogram, % - Percentage. ***End of Report***



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization 2. Samples are not drawn by HECS unless or otherwise mentioned 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items. HECS-G/O/FMT/049

Hubert Enviro Care Systems (P) Ltd. A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in

Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) BIS, FSSAI Notified Laboratory ISO 9001, 14001 & 45001 Certified.

TEST REPORT

Page: 1 of 1

Report No.

HECS/PE/035/180325/N

Sample ID No

: 180325156

Sampling Date

Completed On

Report Date

Received Date : 18/03/2025

Commenced Date: 18/03/2025

Sample quantity : 1 Kg

: 18/03/2025

: 05/04/2025

: 05/04/2025

Address of the Client

Name of the Client

: Vaipur Mathur

: M/s. SIPCOT

Group

: Pollution & Environment

: Soil

Sample Name Sample Mark

: Project Area

Sample Reference

: NA

Sample Drawn By

: M/s.Hubert Enviro care Systems (P) Ltd.

Sample Location Environmental Condition : NA

: Temperature (°C): 27.8 | Humidity (%): 56.0

S.No.	Test Parameters	Units	Results	Test Method
Discip	oline : Chemical			
1	Moisture	%	3.94	HECS-G/ENV/SSW/SOP/003 Issue No.:01 Issue Date:02:07: 2020
2	Manganese	mg/kg	112.53	HECS-G/INS/SOP/ 042
3	Iron	mg/kg	10.68	Inhouse method
4	Infiltration Rate	-	0.8	Inhouse method

Note:- BLQ : Below the Limit of Quantification, LOQ: Limit of Quantification, mg/kg: milligram per kilogram, % - Percentage. ***End of Report***



A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) **BIS FSSAI Notified Laboratory** ISO 9001, 14001 & 45001 Certified.

Name of the Client

TEST REPORT

Page: 1 of 2

ULR

: TC1231025000016848F

Report No.

HECS/PE/036/180325

Sample ID No.

: 180325157

Sampling Date

: 18/03/2025

Address of the Client

: Vaipur Mathur

: M/s. SIPCOT

Group

: Pollution & Environment

Sample Name

: Soil

: Panruti

Sample Mark

Sample Reference

: NA

Sample Drawn By

: M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location Environmental Condition

: Temperature (°C): 27.8 | Humidity (%): 56.0

Received Date : 18/03/2025 Commenced Date: 18/03/2025

Completed On

+ 05/04/2025

Report Date

: 05/04/2025

Sample quantity: 1 Kg

Sampling Method & Plan : ICARDA:2013

S.No.	Test Parameters	Units	Results	Test Method
Discip	line : Chemical		*	
ı	Cadmium	mg/Kg	BLQ (LOQ: 0.1)	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021
2	Chromium	mg/Kg	44.30	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021
3	Copper	mg/Kg	13.66	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021
4	Zinc	mg/kg	28.94	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021
5	Soil Texture	*	Sandy loam	FAO of United Nations, Rome Chapter - 111 2008
6	Soil Texture i)Sand	0%	54.8	FAO of United Nations, Rome Chapter - III 2008
7	Soil Texture ii)Silt	%	34.7	FAO of United Nations, Rome Chapter - III 2008
8	Soil Texture iii)Clay	%	10.5	FAO of United Nations, Rome Chapter - HI 2008
9	pH Value @ 25 ° C (1 : 2.5)	7-	7.25	IS 2720 (Part 26) 1987
10	Electrical conductivity @ 25 ° C (1:2)	μS/cm	102.0	IS 14767: 2000



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization. 2. Samples are not drawn by HECS unless or otherwise mentioned. 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances tab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items.

HECS_CONTINATO HECS-G/Q/FMT/049

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) **BIS FSSAI Notified Laboratory** ISO 9001, 14001 & 45001 Certified.



Name of the Client

TEST REPORT

Page: 2 of 2

ULR

: TC1231025000016848F

Report No.

: HECS/PE/036/180325

Sample ID No

: 180325157

Sampling Date

Completed On

Report Date

Received Date : 18/03/2025

Commenced Date: 18/03/2025

Sample quantity : 1 Kg

: 18/03/2025

: 05/04/2025

: 05/04/2025

Address of the Client

: Vaipur Mathur

: M/s. SIPCOT

Group

: Pollution & Environment

Sample Name

Soil

Sample Mark

: Panruti

Sample Reference

: NA

Sample Drawn By

Sample Location Environmental Condition

: M/s. Hubert Enviro care Systems (P) Ltd.

: Temperature (°C): 27.8 | Humidity (%): 56.0

S.No.	Test Parameters	Units	Results	Test Method
11	Bulk Density	gm/cm3	1.02	FAO of United Nations Rome 2007
12	Organic Carbon	%	0.22	IS 2720 (Part 22) Section I 1972
13	Organic Matter	%	0.39	IS 2720 (Part 22) Section I 1972
14	Available Phosphorous as P	в/вн	BLQ(LOQ 5.0)	FAO of United Nations, Rome Chapter - 111 2008
15	Available Potassium	mEq/100g	20.91	FAO of United Nations, Rome Chapter - III 2008
16	Boron as B	mg/kg	BLQ(LOQ 0.1)	HECS-G/ENV/SSW/SOP/018 Issue No.:01 Issue Date:02:07 2020
17	Total Nitrogen as N	%	0.0123	IS 14684 Clause 4 1999
18	Exchangable Calcium as Ca	mEq/L	15.75	FAO of United Nations, Rome Chapter - III 2008
19	Exchangable Magnesium as Mg	mEq/L	7.87	FAO of United Nations, Rome Chapter - III 2008
20	Cation Exchange Capacity	mEq/100g	2,4	IS 2720 (Part 24) Clause 5 1976
21	Water Holding capacity	%	20.8	IS 14765: 2000
22	Colour	-	Brown	HECS-G/ENV/SSW/SOP/011 Issue No.:01 Issue Date:02:07: 2020

Note:- BLQ : Below the Limit of Quantification, LOQ: Limit of Quantification, mg/kg: milligram per kilogram, % - Percentage. ***End of Report***



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization. 2. Samples are not drawn by HECS unless or otherwise mentioned. 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items. HECS-G/Q/FMT/049

Hubert Enviro Care Systems (P) Ltd. A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in

Laboratory Services Division (Chemical & Biological Testing)

Recognized by CPCB (MoEF & CC) BIS, FSSAI Notified Laboratory ISO 9001, 14001 & 45001 Certified.

TEST REPORT

Page: 1 of 1

Report No.

HECS/PE/036/180325/N

Sample ID No

: 180325157

Sampling Date

: 18/03/2025

Address of the Client

Name of the Client

: Vaipur Mathur

: M/s. SIPCOT

: 18/03/2025

Group Sample Name : Pollution & Environment

Received Date

: Soil

Commenced Date: 18/03/2025 Completed On

: 05/04/2025

Sample Mark

: Panruti

Report Date

: 05/04/2025

Sample Reference

: NA

Sample Drawn By Sample Location : M/s. Hubert Enviro care Systems (P) Ltd.

Sample quantity: 1 Kg

Environmental Condition Sampling Method & Plan

: Temperature (°C): 27.8 | Humidity (%): 56.0

· ICAPDA - 2013

Units	Results	Test Method
%	2.25	HECS-G/ENV/SSW/SOP/003 Issue No.:01 Issue Date:02:07: 2020
mg/kg	248.05	HECS-G/INS/SOP/ 042
mg/kg	6.24	Inhouse method
-	1.5	Inhouse method
	% mg/kg mg/kg	% 2.25 mg/kg 248.05 mg/kg 6.24

Note:- BLQ : Below the Limit of Quantification, LOQ: Limit of Quantification, mg/kg: milligram per kilogram, % - Percentage. ""End of Report""



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization 2. Samples are not drawn by HECS unless or otherwise mentioned 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items. HECS-G/Q/FMT/49

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) **BIS FSSAI Notified Laboratory** ISO 9001, 14001 & 45001 Certified.



Name of the Client

TEST REPORT

Page: 1 of 2

ULR

: TC1231025000016925F

Report No.

HECS/PE/037/180325

Sample ID No

Sampling Date

Completed On

Report Date

: 180325158

: 07/04/2025

: 07/04/2025

: 18/03/2025

Received Date : 18/03/2025

Commenced Date: 18/03/2025

Sample quantity : 1 Kg

Address of the Client

: Vaipur Mathur

: M/s. SIPCOT

Group

: Pollution & Environment

Sample Name

Sample Mark

: Kanchivakkam

Sample Reference

: NA

Sample Drawn By

: M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location

Environmental Condition

: Temperature (°C): 27.8 | Humidity (%): 56.0

Sampling Method & Plan

· ICAPDA-2013

S.No.	Test Parameters	Units	Results	Test Method
Discip	dine : Chemical		W	
1	Cadmium	mg/Kg	BLQ (LOQ: 0.1)	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021
2	Chromium	mg/Kg	21.67	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021
3	Copper	mg/Kg	37.79	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03,2021
4	Zinc	mg/kg	26.56	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021
5	Soil Texture	ā	Silt loam	FAO of United Nations, Rome Chapter III 2008
6	Soil Texture i)Sand	%	12.4	FAO of United Nations, Rome Chapter III 2008
7	Soil Texture ii)Silt	%	62.8	FAO of United Nations, Rome Chapter III 2008
8	Soil Texture iii)Clay	%	24.8	FAO of United Nations, Rome Chapter III 2008
9	pH Value @ 25 ° C (1 : 2.5)	*	8.32	IS 2720 (Part 26) 1987
10	Electrical conductivity @ 25 ° C (1:2)	μS/cm	1202.0	IS 14767: 2000



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization. 2. Samples are not drawn by HECS unless or otherwise mentioned. 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items.

HECS_CONEATT/MAD. HECS-G/Q/FMT/049

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) BIS FSSAI Notified Laboratory ISO 9001, 14001 & 45001 Certified.



TEST REPORT

Page: 2 of 2

ULR

: TC1231025000016925F

Report No.

HECS/PE/037/180325

Sample ID No

: 180325158

Sampling Date

Address of the Client

Name of the Client

: Vaipur Mathur

: M/s. SIPCOT

: 18/03/2025

: Pollution & Environment

Received Date : 18/03/2025

Sample Name

: Soil

Group

Commenced Date: 18/03/2025

Sample Mark

: Kanchiyakkam

Completed On

: 07/04/2025

Sample Reference

: NA

Report Date

: 07/04/2025

Sample Drawn By Sample Location : M/s.Hubert Enviro care Systems (P) Ltd.

Sample quantity: 1 Kg

Environmental Condition

: NA

: Temperature (°C): 27.8 | Humidity (%): 56.0

Sampling Method & Plan

: ICARDA:2013

S.No.	Test Parameters	Units	Results	Test Method
11	Bulk Density	gm/cm3	0.98	FAO of United Nations Rome 2007
12	Organic Carbon	9/6	0.63	IS 2720 (Part 22) Section I 1972
13	Organic Matter	%	1.09	IS 2720 (Part 22) Section I 1972
14	Available Phosphorous as P	рууц	BLQ(LOQ 5.0)	FAO of United Nations, Rome Chapter - 111 2008
15	Available Potassium	mEq/100g	12.84	FAO of United Nations, Rome Chapter - III 2008
16	Boron as B	mg/kg	BLQ(LOQ 0.1)	HECS-G/ENV/SSW/SOP/018 Issue No.:01 Issue Date:02:07 2020
17	Total Nitrogen as N	%	0.0146	IS 14684 Clause 4 1999
18	Exchangable Calcium as Ca	mEq/L	11.26	FAO of United Nations, Rome Chapter - 111 2008
19	Exchangable Magnesium as Mg	mEq/L	7.50	FAO of United Nations, Rome Chapter - III 2008
20	Cation Exchange Capacity	mEq/100g	1.8	IS 2720 (Part 24) Clause 5 1976
21	Water Holding capacity	%	32.2	IS 14765: 2000
22	Colour	2	Black	HECS-G/ENV/SSW/SOP/011 Issue No.:01 Issue Date:02:07; 2020

Note:- BLQ: Below the Limit of Quantification, LOQ: Limit of Quantification, mg/kg: milligram per kilogram, % - Percentage, ***End of Report***



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization. 2. Samples are not drawn by HECS unless or otherwise mentioned. 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items.

HECS-C/O/FMT/849 HECS-G/O/FMT/049

Hubert Enviro Care Systems (P) Ltd. A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in

Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) BIS, FSSAI Notified Laboratory ISO 9001, 14001 & 45001 Certified.

TEST REPORT

Page: 1 of I

Report No.

: HECS/PE/037/180325/N

Sample 1D No

: 180325158

Sampling Date

: 18/03/2025

Address of the Client

Name of the Client

: Vaipur Mathur

: M/s, SIPCOT

Group

: Pollution & Environment

Received Date : 18/03/2025

Sample Name

Commenced Date: 18/03/2025

Completed On

: 07/04/2025

Sample Mark

: Kanchivakkam

: 07/04/2025

Sample Reference

: NA

Report Date

Sample Drawn By Sample Location : M/s. Hubert Enviro care Systems (P) Ltd.

Sample quantity : 1 Kg

Environmental Condition

: Temperature (°C): 27.8 | Humidity (%): 56.0

Sampling Method & Plan

: ICARDA:2013

S.No.	Test Parameters	Units	Results	Test Method
Discip	oline : Chemical	0		
1	Moisture	%	5.38	HECS-G/ENV/SSW/SOP/003 Issue No.:01 Issue Date:02:07: 2020
2	Manganese	mg/kg	153.28	HECS-G/INS/SOP/ 042
3	Iron	mg/kg	4.62	Inhouse method
4	Infiltration Rate	-	0.9	Inhouse method

Note:- BLQ: Below the Limit of Quantification, LOQ: Limit of Quantification, mg/kg: milligram per kilogram, % - Percentage. ***End of Report***



A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) **BIS FSSAI Notified Laboratory** ISO 9001, 14001 & 45001 Certified.

Name of the Client

TEST REPORT

Page: 1 of 2

ULR

: TC1231025000016926F

Report No.

: HECS/PE/038/180325

Sample ID No

Received Date

Completed On

Report Date

: 180325159

: 18/03/2025

: 07/04/2025

: 07/04/2025

Sampling Date : 18/03/2025

Commenced Date: 18/03/2025

Sample quantity: 1 Kg

Address of the Client

: Vaipur Mathur

: M/s. SIPCOT

Group

: Pollution & Environment

: Soil

Sample Name

: Vattambakkam

Sample Mark

Sample Reference

: NA

: M/s.Hubert Enviro care Systems (P) Ltd.

Sample Drawn By

Sample Location

Environmental Condition

: Temperature (°C): 27.8 | Humidity (%): 56.0

Sampling Method & Plan

· ICARDA:2013

S.No.	Test Parameters	Units	Results	Test Method
Discip	oline : Chemical			
1	Cadmium	mg/Kg	BLQ (LOQ: 0.1)	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021
2	Chromium	mg/Kg	16.94	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021
3	Copper	mg/Kg	26.14	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021
4	Zinc	mg/kg	17.62	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021
5	Soil Texture	\$	Clay Ioam	FAO of United Nations, Rome Chapter III 2008
5	Soil Texture i)Sand	%	23.8	FAO of United Nations, Rome Chapter III 2008
7	Soil Texture ii)Silt	%	43.6	FAO of United Nations, Rome Chapter III 2008
8	Soil Texture iii)Clay	%	32.6	FAO of United Nations, Rome Chapter III 2008
)	pH Value @ 25 ° C (1 : 2.5)		8.49	IS 2720 (Part 26) 1987
01	Electrical conductivity @ 25 ° C (1:2)	μS/cm	616.0	IS 14767: 2000



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization 2. Samples are not drawn by HECS unless or otherwise mentioned 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items.

HECS-G/O/FMT/049 HECS-G/Q/FMT/049

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) BIS FSSAI Notified Laboratory ISO 9001, 14001 & 45001 Certified.



Name of the Client

S.No.

11

TEST REPORT

Page: 2 of 2

ULR : TC1231025000016926F

Report No. : HECS/PE/038/180325

Sample ID No : 180325159

Sampling Date : 18/03/2025

Received Date : 18/03/2025

Commenced Date: 18/03/2025

Address of the Client : Vaipur Mathur

Group : Pollution & Environment

Sample Name : Soil

Sample Mark : Vattambakkam

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

: M/s. SIPCOT

Sample Location : NA

Bulk Density

Environmental Condition : Temperature (°C): 27.8 | Humidity (%): 56.0

Sampling Method & Plan : ICARDA:2013

Test Parameters

Comple	ed On : 07/04/2025	
Report		
	quantity:1 Kg	
sults	Test Method	
97	FAO of United Nations Rome 2007	
74	IS 2720 (Part 22) Section I 1972	
10	IS 2720 (Part 22) Section I 1972	
11	FAO of United Nations, Rome Chapter III 2008	-
36	FAO of United Nations, Rome Chapter III 2008	-
.00 0.1)	HECS-G/ENV/SSW/SOP/018 Issue	

12	Organic Carbon	%	0.74	IS 2720 (Part 22) Section I 1972
13	Organic Matter	%	1.10	IS 2720 (Part 22) Section I 1972
14	Available Phosphorous as P	μg/g	6.11	FAO of United Nations, Rome Chapter - III 2008
15	Available Potassium	mEq/100g	25.36	FAO of United Nations, Rome Chapter III 2008
16	Boron as B	mg/kg	BLQ(LOQ 0.1)	HECS-G/ENV/SSW/SOP/018 Issue No.:01 Issue Date:02:07 2020
17	Total Nitrogen as N	%	0.0126	IS 14684 Clause 4 1999
18	Exchangable Calcium as Ca	mEq/L	7.94	FAO of United Nations, Rome Chapter III 2008
19	Exchangable Magnesium as Mg	mEq/L	7.94	FAO of United Nations, Rome Chapter III 2008
20	Cation Exchange Capacity	mEq/100g	2.2	IS 2720 (Part 24) Clause 5 1976
21	Water Holding capacity	%	18.2	IS 14765: 2000
22	Colour	*	Black	HECS-G/ENV/SSW/SOP/011 Issue No.:01 Issue Date:02:07: 2020

Res

0.

Units

gm/cm3

Note:- BLQ: Below the Limit of Quantification, LOQ: Limit of Quantification, mg/kg: milligram per kilogram, % - Percentage.

End of Report



The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization.
 Samples are not drawn by HECS unless or otherwise mentioned.
 Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report.
 Under no circumstances tab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report.
 The test results relate only to the test items.

HECS-G/Q/FMT/049

Hubert Enviro Care Systems (P) Ltd. A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in

Laboratory Services Division (Chemical & Biological Testing)

Recognized by CPCB (MoEF & CC) BIS, FSSAI Notified Laboratory ISO 9001, 14001 & 45001 Certified.

TEST REPORT

Page: 1 of 1

Report No.

· HECS/PE/038/180325/N

Sample ID No

: 180325159

Sampling Date

: 18/03/2025

Address of the Client

Name of the Client

: Vaipur Mathur

: M/s. SIPCOT

Group

: Pollution & Environment

Received Date : 18/03/2025

Sample Name

Commenced Date: 18/03/2025

: Soil

Completed On

: 07/04/2025

Sample Mark

: Vattambakkam

: 07/04/2025

Sample Reference

Report Date

Sample Drawn By Sample Location : M/s. Hubert Enviro care Systems (P) Ltd.

Sample quantity : 1 Kg

Environmental Condition

: Temperature (°C): 27.8 | Humidity (%): 56.0

S.No.	Test Parameters	Units	Results	Test Method
Discip	oline : Chemical			
	Moisture	%	9.93	HECS-G/ENV/SSW/SOP/003 Issue No.:01 Issue Date:02:07; 2020
	Manganese	mg/kg	178.23	HECS-G/INS/SOP/ 042
li.	Iron	mg/kg	6.70	Inhouse method
1.	Infiltration Rate	-	0.9	Inhouse method

Note:- BLQ: Below the Limit of Quantification, LOQ: Limit of Quantification, mg/kg: milligram per kilogram, % - Percentage. ***End of Report***



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization. 2. Samples are not drawn by HECS unless or otherwise mentioned. 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances iab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items. HECS-G/O/FMT/49

A-21, III Phase, Thiru Vi Ka Industrial Estate, Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) BIS FSSAI Notified Laboratory ISO 9001, 14001 & 45001 Certified.



Name of the Client

TEST REPORT

Page: 1 of 2

ULR : TC1231025000016927F

Report No. : HECS/PE/039/180325

Sample ID No : 180325160

Sampling Date : 18/03/2025

Address of the Client : Vaipur Mathur

: Pollution & Environment Group

: M/s, SIPCOT

Sample Name Sample Mark : Mathur

: NA Sample Reference

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location

Environmental Condition

: ICARDA-2013 Sampling Method & Plan

Received Date : 18/03/2025

Commenced Date : 18/03/2025 Completed On : 07/04/2025 : 07/04/2025 Report Date

Sample quantity : 1 Kg

: Temperature (°C): 27.8 | Humidity (%): 56.0

S.No.	Test Parameters	Units	Results	Test Method	
Discip	line : Chemical				
1	Cadmium	mg/Kg	BLQ (LOQ: 0.1)	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021	
2	Chromium	mg/Kg	26.85	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021	
3	Copper	mg/Kg	45.21	HECS-G/INS/SOP/ 042 Issue No.:0 Issue Date:01.03.2021	
4	Zinc	mg/kg	34.20	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03,2021	
5	Soil Texture	*	Loam	FAO of United Nations, Rome Chapter - III 2008	
6	Soil Texture i)Sand	%	30.8	FAO of United Nations, Rome Chapter - 111 2008	
7	Soil Texture ii)Silt	%	48.4	FAO of United Nations, Rome Chapter - III 2008	
8	Soil Texture iii)Clay	%	20.8	FAO of United Nations, Rome Chapter - 111 2008	
9	pH Value @ 25 ° C (1 : 2.5)	\$	7.75	IS 2720 (Part 26) 1987	
10	Electrical conductivity @ 25 ° C (1:2)	μS/cm	265.0	1S 14767: 2000	



D.Anusuya Lab Manager

Authorized Signatory

^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization 2. Samples are not drawn by HECS unless or otherwise mentioned 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items.

HECS-CIO/FMT/049 HECS-G/O/FMT/049

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) **BIS FSSAI Notified Laboratory** ISO 9001, 14001 & 45001 Certified.



Name of the Client

TEST REPORT

Page: 2 of 3

ULR

: TC1231025000016927F

Report No.

: HECS/PE/039/180325

Sample ID No

: 180325160

Sampling Date

Received Date

Completed On

Report Date

Commenced Date: 18/03/2025

Sample quantity: 1 Kg

: 18/03/2025

: 18/03/2025

: 07/04/2025

: 07/04/2025

Address of the Client

: Vaipur Mathur

: M/s. SIPCOT

Group

: Pollution & Environment

Sample Name

: Soil

Sample Mark

: Mathur

Sample Reference

: NA

Sample Drawn By

: M/s.Hubert Enviro care Systems (P) Ltd.

Sample Location Environmental Condition

: Temperature (°C): 27.8 | Humidity (%): 56.0

S.No.	Test Parameters	Units	Results	Test Method	
11	Bulk Density	gm/cm3	0.99	FAO of United Nations Rome 2007	
12	Organic Carbon	%	0.23	IS 2720 (Part 22) Section I 1972	
13	Organic Matter	%	0.40	IS 2720 (Part 22) Section I 1972	
14	Available Phosphorous as P	и г /д	5.93	FAO of United Nations, Rome Chapter III 2008	
15	Available Potassium	mEq/100g	18.22	FAO of United Nations, Rome Chapter III 2008	
16	Boron as B	mg/kg	BLQ(LOQ 0.1)	HECS-G/ENV/SSW/SOP/018 Issue No.:01 Issue Date:02:07 2020	
17	Total Nitrogen as N	%	0,0087	IS 14684 Clause 4 1999	
18	Exchangable Calcium as Ca	mEq/L	7.41	FAO of United Nations, Rome Chapter - III 2008	
19	Exchangable Magnesium as Mg	mEq/L	11.29	FAO of United Nations, Rome Chapter - III 2008	
20	Cation Exchange Capacity	mEq/100g	2.0	IS 2720 (Part 24) Clause 5 1976	
21	Water Holding capacity	%	28.8	1S 14765: 2000	
22	Colour		Brown	HECS-G/ENV/SSW/SOP/011 Issue No.:01 Issue Date:02:07: 2020	

End of Report



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization 2. Samples are not drawn by HECS unless or otherwise mentioned 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss/damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items.

HECS-C/O/FMT/849 HECS-G/O/FMT/049

Hubert Enviro Care Systems (P) Ltd. A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in

Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) BIS, FSSAI Notified Laboratory ISO 9001, 14001 & 45001 Certified.

TEST REPORT

Page: 1 of 1

Report No.

HECS/PE/039/180325/N

Sample ID No

: 180325160

Sampling Date

: 18/03/2025

Address of the Client

Name of the Client

: Vaipur Mathur

: M/s. SIPCOT

Group

: Pollution & Environment

: Soil

Sample Name Sample Mark

: Mathur

Sample Reference Sample Drawn By

: NA

: M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location Environmental Condition Sampling Method & Plan : NA

: Temperature (°C): 27.8 | Humidity (%): 56.0

: ICARDA:2013

Received Date : 18/03/2025

Commenced Date: 18/03/2025 Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 1 Kg

S.Ne	o. Test Parameters	Units	Results	Test Method
Disc	ipline : Chemical			
1	Moisture	%	3.84	HECS-G/ENV/SSW/SOP/003 Issue No.:01 Issue Date:02:07: 2020
2	Manganese	mg/kg	162.49	HECS-G/INS/SOP/ 042
3	Iron	mg/kg	6.20	Inhouse method
4	Infiltration Rate	-	0.9	Inhouse method

Note:- BLQ: Below the Limit of Quantification, LOQ: Limit of Quantification, mg/kg: milligram per kilogram, % - Percentage. ***End of Report***



D.Anusuya Lab Manager Authorized Signatory

1. The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization 2. Samples are not drawn by HECS unless or otherwise mentioned 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items. HECS-G/Q/FMT/49

A-21, III Phase, Thiru Vi Ka Industrial Estate, Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax: 42985500

E-mail: labsales@hecs.in



Laboratory Services Division

(Chemical & Biological Testing) Recognized by CPCB (MoEF & CC) **BIS FSSAI Notified Laboratory** ISO 9001, 14001 & 45001 Certified.



Name of the Client

Address of the Client

TEST REPORT

Page: 1 of 1

ULR

Commenced Date: 18/03/2025

: TC1231025000016360F

Report No.

: HECS/AP/069/180325

Sample ID No

: 180325150

Sampling Date

Received Date

Completed On

Sample quantity : NA

Report Date

: 18/03/2025

: 18/03/2025

: 04/04/2025

: 04/04/2025

: M/s. SIPCOT

: Vaipur Mathur

Group

: Atmospheric Pollution

Sample Name

: Ambient Noise Levels (Excluding vibration)

Sample Mark

Sample Reference

: NA

Sample Drawn By

: M/s.Hubert Enviro care Systems (P) Ltd.

Sample Location

Environmental Condition

: Temperature (°C): 30.8 | Humidity (%): 54.0

Campling Mathed & Plan

18 0080 1081

.No	Sampling Location	Day Noise level in dB (A)	Night Noise level in dB (A)
Į.	Project Site	56.1	50.4
2	Panruti	55.9	49.0
3	Kanchivakkam	58.7	50.9
4	Vattambakkam	57,9	46.6
5	Mathur	50.6	47.7

Noise Standards - CPCB:

Industrial Area i.

: Day Time-75 dB (A);

Night Time-70 dB (A).

ii. Commercial Area

: Day Time-65 dB (A);

Night Time-55 dB (A).

iii. Residential Area : Day Time-55 dB (A);

Night Time-45 dB (A).

Silence Zone

: Day Time-50 dB (A);

Night Time-40 dB (A).

Note:

1. Day Time shall mean from 6.00 am to 10.00 pm.

2. Night Time shall mean from 10.00 pm to 6.00 am.

Remarks:- The noise level meets the requirement of CPCB Limits.

End of Report



^{1.} The report in full or part shall not be used for any promotional or publicity purpose without written consent by HECS organization 2. Samples are not drawn by HECS unless or otherwise mentioned 3. Unless specifically requested by customer the test items will not be retained more than 15 days from the date of issue of test report. 4. Under no circumstances lab accepts any liability or loss / damage caused by use or misuse of test report after invoicing or issue of test report. 5. The test results relate only to the test items.

HECS_C/O/FMT/M40 HECS-G/Q/FMT/049

THE NEW INDIAN EXPRESS

Page 559 11 April 2015 Saturday



SIPCOT INDUSTRIAL PARK, VAIPUR MATHUR SRIPERUMBUDUR TALUK KANCHEEPURAM DISTRICT

ENVIRONMENTAL CLEARANCE

Environmental Clearance has been obtained for the proposed SIPCOT Industrial Park at Vaipur Mathur, Kancheepuram District from State Level Environment Impact Assessment Authority (SEIAA), Tamil Nadu vide their Lr.No.SEIAA-TN/F-662/EC/8(b)/385/2012, dated 01.04.2015.

The contents of the Environmental Clearance can be viewed in SIPCOT website www.sipcot.com and also in the SEIAA website www.seiaa.tn.gov.in. Further, the copies of the Environmental Clearance could be obtained from the Head Office of Tamil Nadu Pollution Control Board (TNPCB).

MANAGING DIRECTOR

19-A, Rukmani Lakshmipathy Road, Egmore, Chennai-600 008

DIPR/390/DISPLAY/2015

हीन्नां मुंडी

Page -10 % (11-4-2015) Joshibby on 6



சிப்காட் தொழிற் பூங்கா வைப்பூர் மாத்தூர்

திருப்பெரும்புதூர் தாலுகா / காஞ்சிபுரம் மாவட்டம்

சுற்றுச்சூழல் இசைவாணை


மாநீல சுற்றுச்சூழல் தாக்க மதிப்பீட்டு ஆணையம், தமிழ்நாடு கடித எண். SEIAA/TN/F.662/EC/8(b)/385/2012 தேதி O1.O4.2O15 மூலம் காஞ்சிபுரம் மாவட்டம், வைப்பூர் மாத்தூர் கிராமங்களில் அமையவுள்ள தொழிற் பூங்காவிற்கு சுற்றுச்சூழல் இசைவாணை வழங்கியுள்ளது.

இவ்விசைவாணையின் முழு விவரங்களை சிப்காட் இணையதளமான <u>www.sipcot.com</u> மற்றும் மாநில சுற்றுச்சூழல் தாக்க மதிப்பீட்டு ஆணையத்தின் இணையதளமான <u>www.seiaa.tn.gov.in</u> ஆகியவற்றில் காணலாம். மேலும் இசைவாணையின் நகலினை தமிழ்நாடு மாசுக் கட்டுப்பாட்டு வாரியத் தலைமை அலுவலகத்தில் பெற்றுக்கொள்ளலாம்.


. மேலாண்மை இயக்குநர் சீப்காட்

19-அ, ருக்மணி இலட்சுமிபத் சாலை, எழும்பூர், சென்னை - 600 008

OF 10 Day 8/390/20094800/2015



Annexure - 7



ENVIRONMENTAL MANAGEMENT CELL

1. INTRODUCTION:

- 1.1. For effective implementation and monitoring of environmental management system, it is necessary to have a permanent organizational set-up as Environmental Management Cell (EMC). This is done by assigning responsibility to the concerned personnel for implementation of environmental control measures.
- 1.2. SIPCOT Environmental Management Cell consist of 7 team members headed by SIPCOT Managing Director, General Manager (Projects), Manager and two Environmental Consultants assisted by two Office Staffs which will enforce and implement the Environmental Plan.
- 1.3. The Organization of Environmental Management Cell (EMC) proposed is given in **Figure 1.**

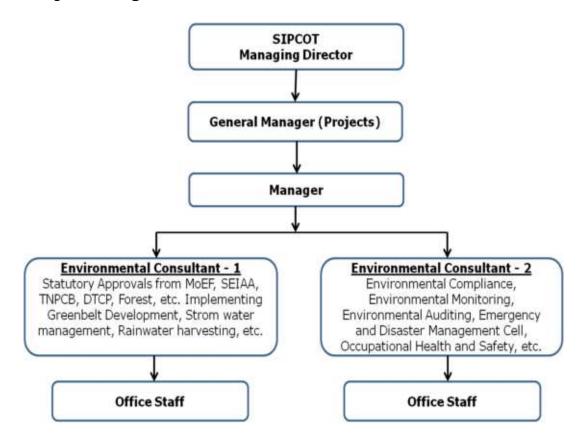


Figure - 1 Organogram for Environmental Management Cell

2. RESPONSIBILITIES OF ENVIRONMENTAL MANAGEMENT CELL:

- 2.1. Environmental Management Cell (EMC) shall obtain all applicable statutory clearances and approvals as mandated by the regulatory authorities and maintain the Industrial Parks in compliance with all applicable rules and regulations.
- 2.2. Other responsibilities of the cell will include:
 - a) Review the progress of regulatory compliance of SIPCOT and initiate necessary action for the compliance of the same.
 - b) The EMC will review, implement, update, and comply with the Environment Policy to ensure the effective implementation of environmental safeguard measures.
 - c) Keeping the Board updated on regular basis about the activities carried out under environmental measures and suggests measures to improve environment preservation and protection.
 - d) Encourages allottee units to implement, adopt and use of green and sustainable technologies such as Solar, Wind, Thermal, Biomass, Electric & Hybrid vehicles, etc. to achieve more resource-efficient, clean and resilient growth towards reducing pollution during their process, manufacturing and transportation of goods and encourages energy recovery for self sustainability from their Industrial process.
 - e) Mandate industries to reduce the use of one time use plastics, Styrofoam, and other plastic material during the packing and delivery of goods.

Table – 1: Roles and responsibilities of EMC

S.No.	Designation	Responsibilities		
		> Responsible for overall environmental management.		
1	Managing Director	Regularly conduct meeting with EMC and take feedback regarding all the activities performed under Environmental Management and give directions to succeeding component.		
		 Approval of funds for carrying out environmental management activities. 		
2	GM – Projects	 Keep aware about all the activities performed under EMC in the industrial parks. Issuing direction to Project officers for implementing Greenbelt development, Storm water management, rain water harvesting, etc. To deal with legal entity pertaining to environmental issues. 		
3	 To prepare and allocate budget for Environment Plan. Ensuring compliance to the conditions prescristatutory authority. Manager Mandating member industries to comply where conditions stipulated in the statutory approved non-compliance if any shall be reported to comply immediately required action will be taken. 			
4	Environmental Consultants (Two)	 Obtaining Statutory Approvals from MoEF&CC / SEIAA / TNPCB, etc. Addressing the various queries received from statutory authorities on environmental front. Submitting Environmental compliance report and coordinating with project officers for Environmental monitoring, audit, etc. Compliance with the environmental laws and implications which dynamically changes from time to time due to the emerging challenges. 		



I/172476/2024 Date: 24-09-2024

To, The Member Secretary, Tamil Nadu Pollution Control Board, No.76, Mount Salai, Guindy, Chennai – 600 032.

Sir,

Sub: SIPCOT Industrial Park, Vaipur Mathur - Environmental Statement for the

Financial Year ending 31st March 2024 - Submitted - Reg.

Ref: SEIAA EC Lr. No. SEIAA-TN/F-662/EC/8(b)/385/2012 dated 01.04.2015.

With reference to the above, we hereby submit the Environmental Statement in Form-V as prescribed under the Environmental (Protection) Rules, 1986 and its subsequent amendment in respect of SIPCOT Industrial Park at Vaipur, Mathur and Perinjambakkam Villages, Sriperumbudur Taluk, Kancheepuram District, Tamil Nadu for the Financial Year ending 31st March 2024.

Yours faithfully,

GENERAL MANAGER (P-III)

Encl: As above.


Annexure-10

SIPCOT – VAIPUR MATHUR MONITORING PHOTOGRAPH

AMBIENT AIR QUALITY MONITORING PHOTOGRAPH:

NEAR PROJECT SITE Oragadam, Tamil Nadu, India Vw2r+jxj, Oragadam, Tamil Nadu 631604, India Lat 12.852457° Long 79.94201° 18/03/2025 10:50 AM GMT +05:30 948

PANRUTI



KANCHIVAKKAM



VATTAMBAKKAM



MATHUR



NOISE MONITORING PHOTOGRAPH



PANRUTI



KANCHIVAKKAM



VATTAMBAKKAM



MATHUR



SOIL SAMPLING PHOTOGRAPH

Chemai, Tamil Nadu, India

PANRUTI




Umayalparamancheri, Tamil ... 3/11, Umayalparamancheri, Tamil Nadu 60/301, India Lat 12.843649* Long 76.988447* 18/03/2025 04:21 PM GMT +05:30 1280



MATHUR




GROUND WATER SAMPLING PHOTOGRAPH

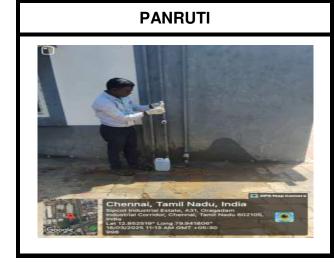



Mathur, Tamil Nadu, India Verifyer Nathur, Tamil Nadu, India Verifyer Nathur, Tamil Nadu 802105, India India

SURFACE WATER SAMPLING PHOTOGRAPH

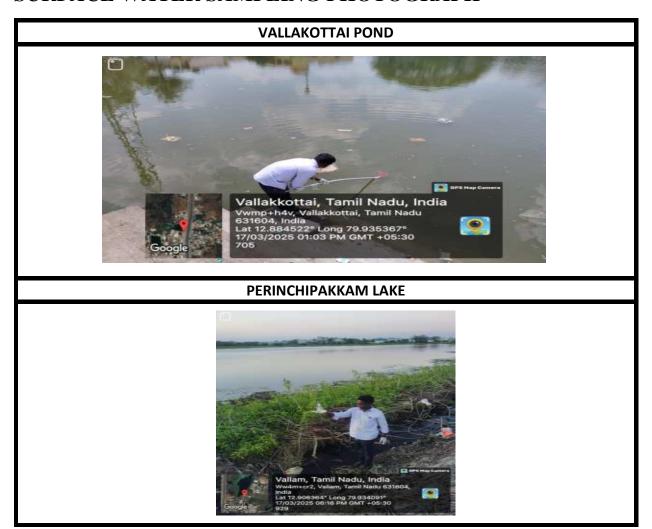



STORM DRAIN PHOTOGRAPHS





ROAD PHOTOGRAPHS

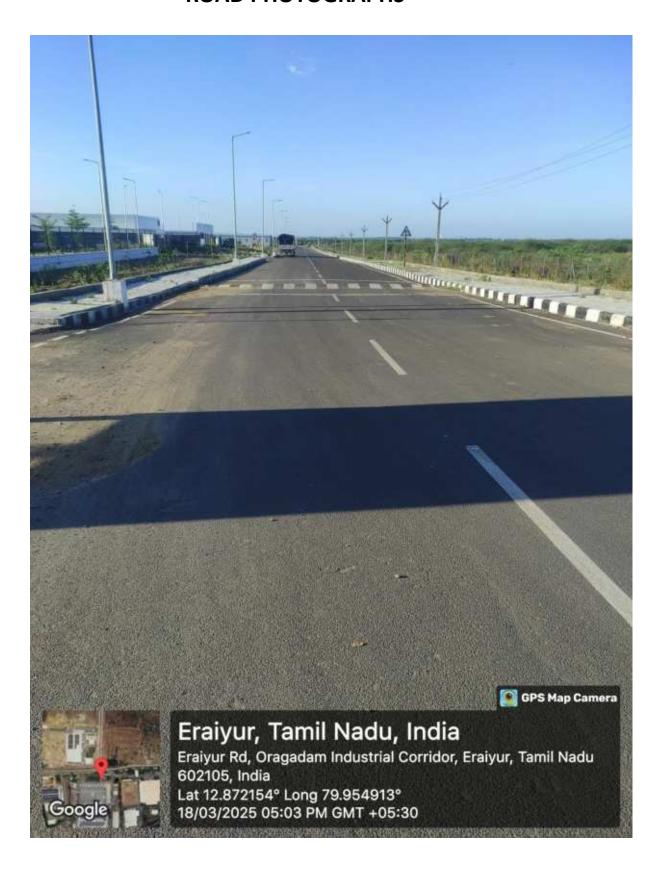

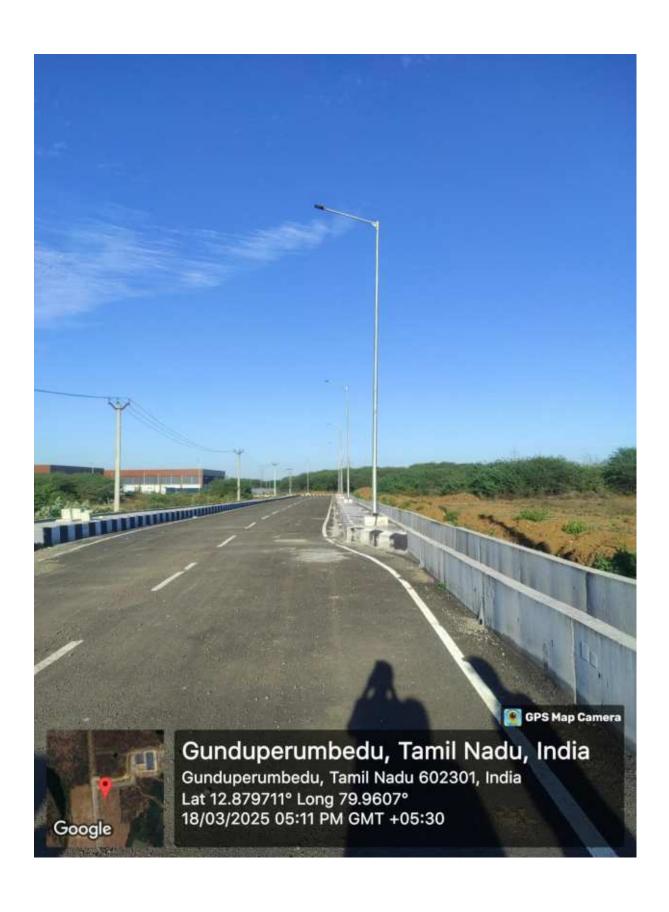

Solid Waste Management Area Photographs

