

EC/Tindivanam/HYC/June/2025

Date: 30.05.2025

To,  
The Member Secretary,  
State Level Environment Impact Assessment Authority,  
Chennai Metro Rail Limited (Head office),  
No.327, Anna Salai, Nandanam,  
Chennai - 600 035.

Sir/Madam,

Sub: SIPCOT Industrial Park at Tindivanam - Submission of Half Yearly Compliance Report for June 2025 (i.e., for the period of October 2024 to March 2025) - Reg.

Ref: EC vide Letter No. SEIAA-TN/F.6497/EC/8(b)/681/2019 dated: 27.11.2019

\*\*\*\*

We hereby submit the Half Yearly Compliance Report for the Development of Industrial Park at Pelakuppam, Venmaniyathoor, Kollar Villages of Thindivanam Taluk, Villupuram District, Tamil Nadu for June 2025 (i.e., for the period of October 2024 to March 2025) along with the supporting documents for your perusal.

Thanking you

Yours faithfully,

CONSULTANT (PROJECT MANAGEMENT)

Encl: As above.

Copy to:

1. The Director,  
The Ministry of Environment and Forest & Climate Change,  
Integrated Regional Office,  
1st Floor, Additional Office Block for GPOA,  
Shastri Bhawan, Haddows Road,  
Nungambakkam, Chennai - 600 006
2. The Director,  
CPCB Zonal Office,  
77-A, South Avenue Road,  
Ambattur Industrial Estate,  
Ambattur Taluk, Thiruvallur District,  
Chennai - 600 058.

P.T.O.

**State Industries Promotion Corporation of Tamil Nadu Limited**  
(A Government of Tamil Nadu Undertaking)

CIN I U74999TN1971SGC005967

Regd. Office : 19-A, Rukmani Lakshmipathy Road, Post Box No. 7223, Egmore, Chennai - 600 008.

Phone : 4526 1777, Fax : 4526 1796 Website : www.sipcot.tn.gov.in

3. The Chairman,  
Tamil Nadu Pollution Control Board,  
No-76, Mount Road, Guindy,  
Chennai-600 032
4. The Project Officer  
SIPCOT Industrial Park,  
Tindivanam.

**State Industries Promotion Corporation of Tamil Nadu Limited**

**(A Government of Tamil Nadu Undertaking)**

CIN | U74999TN1971SGC005967

Regd. Office : 19-A, Rukmani Lakshmipathy Road, Post Box No. 7223, Egmore, Chennai - 600 008.

Phone : 4526 1777, Fax : 4526 1796 Website : [www.sipcot.tn.gov.in](http://www.sipcot.tn.gov.in)

**HALF YEARLY ENVIRONMENTAL CLEARANCE  
COMPLIANCE REPORT**

**For the period of October 2024 – March 2025**

**For**

**“Establishment of Industrial Park”**

**At**

**Pelakuppam, Venmaniyathoor, Kollar Villages of Thindivanam  
Taluk, Villupuram District, Tamil Nadu**

**EC OBTAINED Vide Letter No SEIAA-TN/F.6497/EC/8(b)/681/2019 dated: 27.11.2019**

**Submitted by**



**M/s. STATE INDUSTRIES PROMOTION CORPORATION OF TAMILNADU  
LTD,**

**19/A, RukmaniLakshmipathy Road,  
Egmore, Chennai-600008.**

**Prepared by**



**HUBERT ENVIRO CARE SYSTEMS (P) LTD CHENNAI  
(ENVIRONMENTAL CONSULTANT)**

**May 2025**

## TABLE OF CONTENTS

S. No	List of Contents		Page No
1.	Project details		4
2.	Location map		5
3.	Site photograph		6
4.	Six monthly environmental clearance statement		8
5.	Environmental Monitoring Details		30
	5.1	Ambient air quality monitoring	30
	5.2	Ambient noise level monitoring	30
	5.3	Soil Quality monitoring	30
	5.4	Ground water quality monitoring	30
	5.5	Surface water quality monitoring	30
6.	Conclusion		31




## LIST OF ANNEXURE

S. No	List of Contents
Annexure 1	Copy of Environmental Clearance
Annexure 2	Consent To Establish from TNPCB
Annexure 3	TWAD Board Letter
Annexure 4	Environmental Management Cell Organogram with responsibilities
Annexure 5	Environmental Monitoring reports
Annexure 6	Environmental Monitoring Photos
Annexure 7 A	Newspaper advertisement copy
Annexure 7 B	Press release of EC advertisement submitted to Regional office of MoEF & SEIAA acknowledgement copy
Annexure 8 A	Acknowledgement copy of EC submission to local bodies
Annexure 8 B	Screenshot of EC details uploaded in our website
Annexure 9	Screenshot of Compliance Report and Environment Statement uploaded at website
Annexure 10	Form V acknowledgement
Annexure 11	Greenbelt photograph
Annexure 12	Storm water photographs
Annexure 13	LED photographs

## 1. PROJECT DETAILS

Name of the Project	SIPCOT Industrial Park, Thindivanam
Name of the Proponent	State Industries Promotion Corporation of Tamil Nadu Ltd.
EC. No	<b>SEIAA-TN/F.6497/EC/8(b)/681/2019 dated 27.11.2019</b> (Enclosed as <b>Annexure- 1</b> )
Area of the Land	291.60.5 Hectares
Water Requirement:	<ul style="list-style-type: none"><li>a) Total Water Requirement: 4 MLD</li><li>b) Source: 3 MLD Tertiary Treatment Reverse Osmosis (TTRO water) from Thindivanam Municipality.</li><li>c) 1 MLD for drinking water from Tamil Nadu Water Supply and Drainage Board (TWAD)</li></ul>
Project Cost	Rs. 300 Crores

## 2. LOCATION MAP

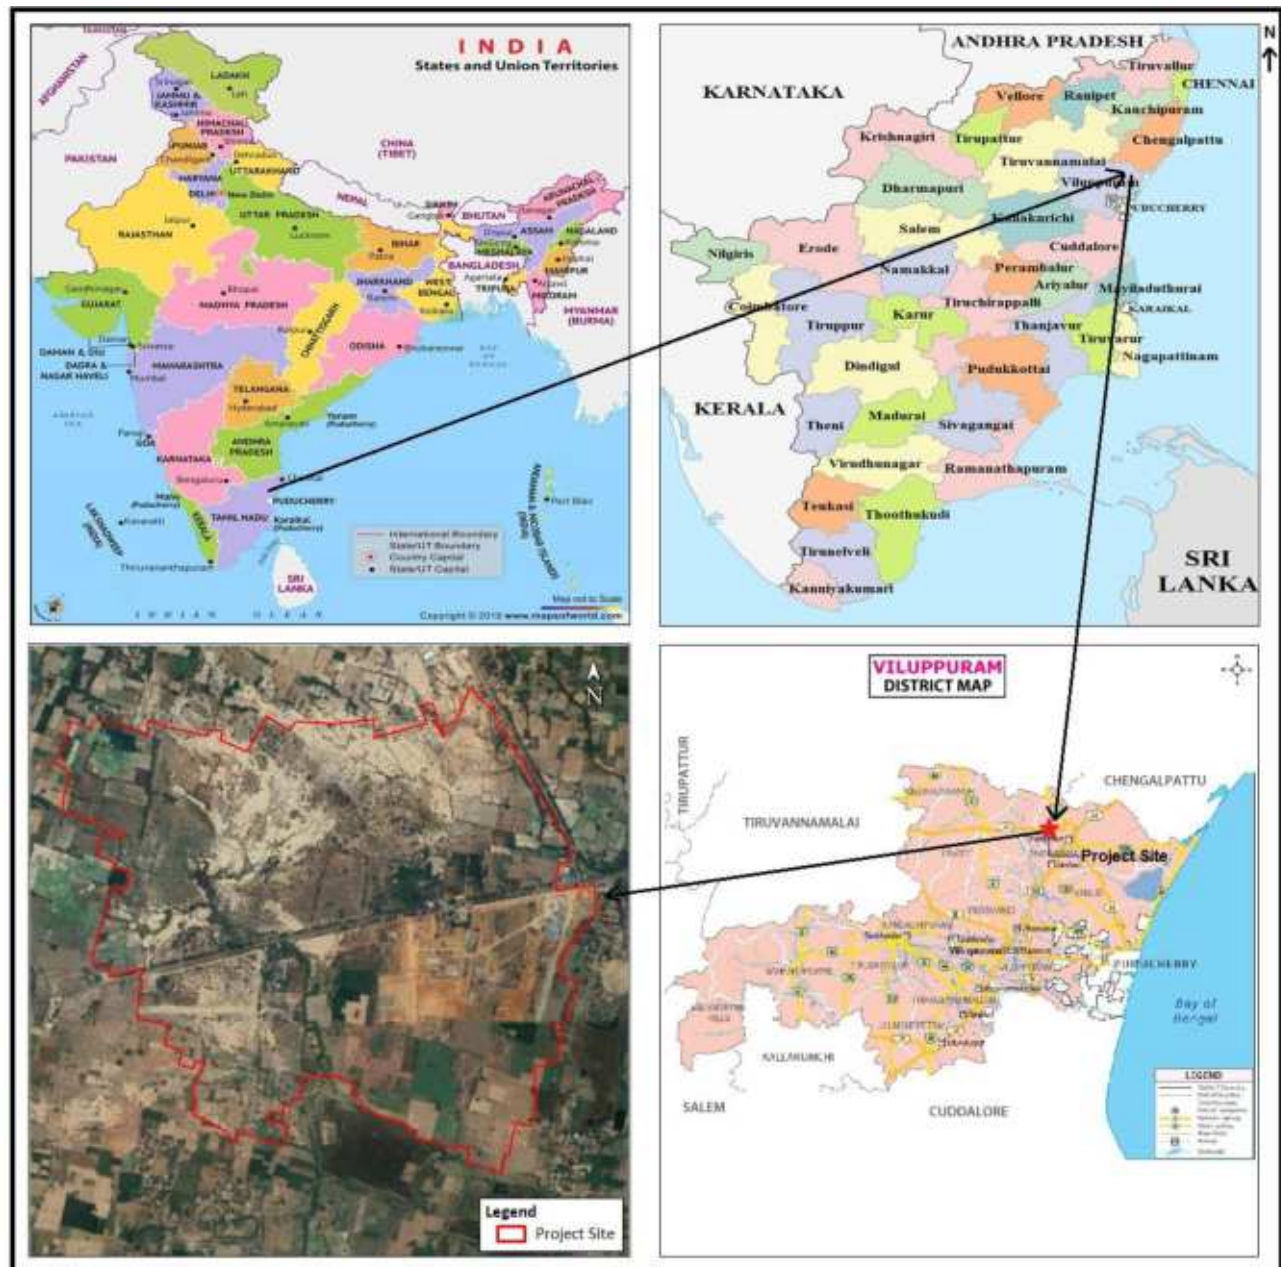

### 3. SITE PHOTOGRAPHS







#### **4. SIX MONTHLY ENVIRONMENTAL CLEARANCE COMPLIANCE STATEMENT**

##### **Part – A: Common Conditions Applicable for Pre construction, Construction and Operational Phase**

<b>S. No.</b>	<b>Condition</b>	<b>Status of Compliance</b>
1.	Any appeal against this environmental clearance shall lie with the Hon'ble National Green Tribunal, if preferred, within a period of 30 days as prescribed under section 16 of the National Green Tribunal Act,2010.	There is no appeal lies against this Environmental Clearance.
2.	The construction of STP, Solid Waste Management facility, E-waste .Management facility, DG sets, etc., should be made in the earmarked area only. In any case, the location of these utilities should not be changed later on.	Construction shall be carried out as per the layout approval.
3.	The Environmental safeguards contained in the application of the proponent /mentioned during the presentation before the State Level Environment Impact Assessment Authority / State Level Expert Appraisal Committee should be implemented in the letter and spirit.	SIPCOT shall comply with all the applicable conditions issued in the EC.

4.	All other statutory clearances such as the approvals for storage of diesel from Chief Controller of Explosives, Fire and Rescue Services Department, Civil Aviation Department, Forest Conservation Act, 1980 and Wild Life (Protection) Act, 1972, State/Central Ground Water Authority, Coastal Regulatory Zone Authority, other statutory and other authorities as applicable to the project shall be obtained by project proponent from the concerned competent authorities.	<b>Condition Noted.</b>
5.	The SEIAA reserves the right to add additional safeguard measures subsequently, if non-compliance of any of the EC conditions is found and to take action, including revoking of this Environmental Clearance as the case may be.	Condition noted.
6.	A proper record showing compliance of all the conditions of Environmental Clearance shall be maintained and made available at all the times.	Condition is being complied.
7.	The environmental statement for each financial year ending 31st March in Form- V as is mandated to be submitted by the project proponent to the concerned State Pollution Control Board as prescribed under the Environment (Protection) Rules, 1986, as amended subsequently, shall also be put on the website of the company. The status of compliance of environmental clearance conditions and shall also be sent to the Regional Office of the Ministry of Environment and Forests, Chennai by e- mail.	Condition is being complied.  Proof of dispatch of Form V to TNPCB and the screenshot of uploading the environmental statement in SIPCOT website is enclosed as <b>Annexure – 9 and Annexure – 10</b> respectively. The status of compliance of environmental clearance conditions sent to the Regional Office of the Ministry of Environment and Forests, Chennai By e- mail and the proof is enclosed as <b>Annexure – 7.</b>



8.	The Regional Office of the Ministry located at Chennai shall monitor compliance of the stipulated conditions. The project authorities should extend full cooperation to the officer (s) of the Regional Office by furnishing the requisite data/information/monitoring reports.	Condition noted.
9.	"Consent for Establishment" shall be obtained from the Tamil Nadu Pollution Control Board and a copy shall be submitted to the SEIAA, Tamil Nadu.	Condition complied. Consent to Establishment has been obtained from TNPCB. Copy of the same is enclosed as <b>Annexure-2.</b>
10	In the case of any change(s) in the scope of the project, a fresh appraisal by the SEAC/SEIAA shall be obtained before implementation.	Condition noted. There is no change in the scope of the project.
11	The conditions will be enforced inter-alia, under the provisions of the Water (Prevention & Control of Pollution) Act, 1974, the Air (Prevention & Control of Pollution) Act, 1981, the Environment (Protection) Act, 1986, the Public Liability Insurance Act, 1991, along with their amendments, draft Minor Mineral Conservation & Development Rules, 010 framed under MMDR Act 1957, National Commission for protection of Child Right Rules, 2006 and rules made there under also any other orders passed by the Hon'ble Supreme Court of India/Hon'ble National Green Tribunal relating to the subject matter.	Condition complied. Consent to Establishment has been obtained from TNPCB. Copy of the same is enclosed as <b>Annexure-2.</b>
12	The Environmental Clearance shall not be cited for relaxing the other applicable rules to this project.	Condition Noted.
13	Failure to comply with any of the conditions mentioned above may result in withdrawal of this clearance and attract action under the provisions of the Environment (Protection) Act, 1986.	Condition Noted.

14	The proponent shall upload the status of compliance of the stipulated EC conditions, including results of monitored data on their website and shall update the same periodically. It shall simultaneously be sent to the Regional Office of MoEF, Chennai, the respective Zonal Office of CPCB, Bengaluru and the TNPCB. The criteria pollutant levels namely; PM10, PM 2.5, SO, NOX (ambient levels as well as stack emissions) or critical sectoral parameters, indicated for the project shall be monitored.	<p><b>Condition is being complied.</b></p> <p>Six Monthly compliance report is being submitted periodically with the monitored data to MoEF, CPCB &amp; SPCB and also uploaded in PARIVESH portal .</p> <p>Proof of submission of six monthly reports on the status of compliance of the stipulated EC conditions including results of monitored data is enclosed as <b>Annexure – 9</b></p> <p>Air pollutant indicated for the project is monitored regularly and air quality monitoring report is enclosed as <b>annexure-5</b>.</p>
15	The SEIAA, TN may cancel the environmental clearance granted to this project under the provisions of EIA Notification 2006, if, at any stage of the validity of this environmental clearance, if it is found or if it comes to the knowledge of this SEIAA, TN that the project proponent has deliberately concealed and/or submitted false or misleading information or inadequate data for obtaining the environmental clearance.	<b>Condition noted.</b>
16	The Environmental Clearance does not imply that the other statutory / administrative clearances shall be granted to the project by the concerned authorities. Such authorities would be considering the project on merits and be taking decisions independently of the Environmental Clearance or inadequate data for obtaining the environmental clearance.	<p>Condition Noted.</p> <p>All the member industries will be instructed to obtain necessary approvals / clearances.</p>
17	The SEIAA, TN may alter/modify the above conditions or stipulate any further condition in the interest of environment protection, even during the subsequent period.	Condition noted.

18	The Environmental Clearance does not absolve the applicant/proponent of his obligation/requirement to obtain other statutory and administrative clearances from other statutory and administrative authorities.	Condition Noted.
19	Where the trees need to be cut, compensation plantation in the ratio of 1: 10 (i.e. planting of 10 trees for every one tree that is cut) should be done with the obligation to continue maintenance.	Condition noted.
20	A separate environmental management cell with suitable qualified personnel should be set-up under the control of a Senior Executive who will report directly to the Head of the Organization and the shortfall shall be strictly reviewed and addressed.	Condition complied. Separate environmental management cell has been assigned and will report to the General Manager, SIPCOT who will report directly to the Head of the Organization for implementation monitoring and compliance of the environmental safeguards. Details of Environmental Management Cell with Roles and Responsibilities are enclosed as <b>Annexure-4.</b>
21	The EMP cost of Rs.1.5 Crores shall be deposited in a Nationalized bank by opening separate account and the head wise expenses statement shall be submitted to TNPCB with a copy to SEIAA annually.	<b>Condition Noted.</b>
22	The project activity should not cause any disturbance & deterioration of the local bio diversity.	<b>Condition Noted.</b>
23	The project activity should not impact the water bodies. A detailed inventory of the water bodies and forest should be evaluated and fact reported to the Forest Department & PWD for monitoring.	<b>Condition is being complied.</b> Surface monitoring report is enclosed as <b>annexure- 5</b>

24	All the assessed flora & fauna should be conserved and protected.	Condition Noted.
25	The proponent should strictly comply with, Tamil Nadu Government Order (Ms) No.84 Environment and forests (EC.2) Department dated 25.06.2018 regarding ban on one time use and throwaway plastics irrespective of thickness with effect from O 1.01.2019 under Environment (Protection) Act, 1986.	Condition will be complied.
26	As per MoEF & CC, Gol, Office Memorandum dated 30.03.2015, prior clearance from Forestry & Wildlife angle including clearance from obtaining committee of the National Board for Wildlife as applicable shall be obtained before starting the quarrying operation, if the project site is located within 10 KM from National Park and Sanctuaries.	Not applicable.
27	Traffic congestion near the entry and exit points from the roads adjoining the proposed project site must be avoided.	Condition noted.
28	The safety measures proposed in the report should be strictly followed.	Condition Noted.
29	The Developer shall ensure that no allotment letter/ sale deed in any form shall be made to house Category B Industry as prescribed in the schedule of EIA notification 2006. However, in case any category A or category B type of industry as prescribed in the schedule of EIA notification 2006 is proposed then the individual unit shall apply and seek Environmental Clearance under the EIA notification 2006.	Condition Noted.  If any EC category industry is proposed within the Industrial Park, Individual Industries will be mandated to obtain separate EC on their own.

30	The Developer shall mandate the member industries of the Industrial Park to allot 33% of the plot area for green belt development and to install RWH structures.	<b>Condition Noted.</b> Individual Industries shall comply with.
31	The Developer has to ensure that all the member industries within the Industrial Park shall make their own arrangements to achieve zero discharge of the trade effluents, solid waste & E waste management, gaseous emission and noise control measures to achieve the standards prescribed by the TNPCB.	<b>Condition will be complied.</b> All the member units will be mandated to provide individual ETP with Zero Liquid Discharge system and to handle the domestic wastewater as per the prescribed standards. All the member units will be instructed to follow all applicable rules and guidelines.
32	The project proponent shall ensure that the individual member units will not be allowed to carry out manufacturing of products stipulated in G.O. (Ms) No. 84 dated 25/06/2018 on banning of one time use on and throwaway plastics.	<b>Condition Noted.</b> Individual Industries shall comply with.
33	The project proponent must submit the permissible land use classification Certificate obtained from competent authority for the proposed project before obtain the CTE from TNPCB.	<b>Condition complied.</b> Land use classification certificate obtained from DTCP.
34	The proponent shall obtain the necessary permission/ NOC of water supply from the TWAD Board/competent Authority.	Condition is being complied. We SIPCOT has obtained water supply permission from TWAD board Letter from TWAD Board is enclosed as <b>Annexure- 3.</b>
35	The CER fund shall be utilized as per the office memorandum of MoEF&CC dated 01.05.2018 before obtaining CTO from TNPCB.	<b>Condition will be complied.</b>

36	The allotted industrial units shall obtain consent from the TNPCB separately for their establishment & operation in this industrial estate.	All the member units will be instructed to obtain consent from the TNPCB separately for their establishment & operation in this industrial estate.
37	The project proponent shall ensure that 33% of the total area of the project site should be covered with green belt.	Condition Noted. We SIPCOT ensure that 33 % of the total area of the project site should be covered with greenbelt. Greenbelt photograph is enclosed as <b>annexure-11</b> .
38	The proponent shall provide Rain Water Harvesting pits so as to recharge the ground water table.	<b>Condition Noted.</b> Individual Industries shall comply with.
39	Discharge of treated sewage shall conform to the norms & standards prescribed by the Tamil Nadu Pollution Control Board.	STP is not proposed by SIPCOT. All the member units will be instructed to follow all applicable rules and guidelines.
40	It is the sole responsibility of the proponent that the treated sewage disposed for green belt development/ avenue plantation should not pollute the soil/ ground water/ adjacent canals/ lakes/ ponds, etc.	STP is not proposed by SIPCOT. All the member Industries will be mandated to provide adequate capacity of STP and the treated sewage will be reused for their greenbelt development.
41	The Developer has to ensure that all the member industries within the Industrial Park shall make their own arrangements to achieve zero discharge of the trade effluents.	Condition will be complied. All the member units will be mandated to provide individual ETP with Zero Liquid Discharge system and to handle the domestic wastewater as per the prescribed standards.
42	The project proponent shall ensure that all the member units should treat and dispose solid waste & E-waste as per the Solid Waste Management Rule 2016 as amended and E-Waste Management. Rules, 2016.	<b>Condition noted.</b> All the member units will be instructed to comply all applicable rules and guidelines.

43	There shall be no discharge of effluent outside the Industrial Park at any time.	All the member units will be mandated to provide individual ETP with Zero Liquid Discharge system.
44	The Developer shall mandate the member units of the Industrial Park to install adequate APC measures/Acoustic to achieve air emissions standards within permissible limits prescribed by the CPCB.	<b>Condition noted.</b> All the member units will be instructed to comply all applicable rules and guidelines.

**Part - B - Specific Conditions - Pre Construction Phase:**

S.No	CONDITIONS	STATUS OF COMPLIANCE
1.	The project authorities should advertise with basic details at least in two local newspapers widely circulated, one of which shall be in the vernacular language of the locality concerned, within 7 days of the issue of clearance. The press releases also mention that a copy of the clearance letter is available with the State Pollution Control Board and also at website of SEIAA, TN. The copy of the press release should be forwarded to the Regional Office of the Ministry of Environment and Forests located at Chennai and SEIAA-TN.	Condition complied. We, SIPCOT have advertised in two local newspapers in Tamil and English that we have obtained Environmental clearance from SEIAA /TN along with the details of SEIAA website where it is displayed Newspaper advertisement copy is enclosed as <b>Annexure-7A.</b> The copy of the press release has been forwarded to the Regional Office of the Ministry of Environment and Forests located at Chennai and SEIAA-TN and acknowledgement for the same is enclosed as <b>Annexure-7B.</b>
2.	In the case of any change(s) in the scope of the project, a fresh appraisal by the SEAC/SEIAA shall be obtained before implementation.	Condition noted. There is no change in the scope of the project



3.	A copy of the clearance letter shall be sent by the proponent to the Local Body. The clearance letter shall also be put on the website of the Proponent.	Condition complied. Acknowledgement copy of clearance letter sent to local body is enclosed as <b>Annexure-8A</b> . The clearance letter also uploaded on SIPCOT website and it is enclosed as <b>Annexure-8B</b> .
4.	The approval of the competent authority shall be obtained for structural safety of the buildings during earthquake, adequacy of firefighting equipments, etc as per National Building Code including protection measures from lightning etc before commencement of the work.	<b>Condition Noted.</b> All the member industries are being mandated to obtain all necessary clearance / approvals.
5.	All required sanitary and hygienic measures for the workers should be in place before starting construction activities and they have to be maintained throughout the construction phase.	Condition Noted. All the member units will be instructed to maintain sanitary and hygienic measures for the workers throughout the construction phase..
6.	Design of buildings should be in conformity with the Seismic Zone Classifications.	Condition Noted.
7.	The Construction of the structures should be undertaken as per the plans approved by the concerned local authorities / local administration.	Construction will be carried out as per the DTCP approved layout.
8.	No construction activity of any kind shall be taken up in the OSR area.	Condition noted.
9.	Consent of the local body concerned should be obtained for using the treated sewage in the OSR area for gardening purpose. The quality of treated sewage shall satisfy the bathing quality prescribed by the CPCB.	Condition will be complied. Individual industries will be mandated to treat the Sewage as per the norms and reuse within their premises.
10.	The height and coverage of the constructions shall be in accordance with the existing FSI/ FAR norms as per Coastal Regulation Zone Notification, 2011.	Not applicable. The project site is away from the CRZ.

11.	The Project Proponent shall provide car parking exclusively for the visiting guest in the proposed residential apartments as per CMDA norms.	Not Applicable. The proposed project is an Industrial Park.
12.	The project proponent shall ensure the level of basement shall be above maximum flood level.	<b>Condition will be complied.</b> All the member units will be instructed to comply with.
13.	The proponent shall prepare completion plans showing Separate pipelines marked with different colours with the following details: <ol style="list-style-type: none"> <li>1. Location of STP, compost system, underground sewer line</li> <li>2. Pipe Line conveying the treated effluent for green belt development</li> <li>3. Pipe Line conveying the treated effluent for toilet flushing</li> <li>4. Water supply pipeline</li> <li>5. Gas supply pipe line, if proposed</li> <li>6. Telephone cable</li> <li>7. Power cable</li> <li>8. Storm water drains, and</li> <li>9. Rain water harvesting system, etc., and</li> </ol> it shall be made available to the owners.	<b>Conditions applicable will be complied.</b>
14.	A First Aid Room shall be provided in the project site during the entire construction and operation phases of the project.	<b>Condition Noted.</b>
15.	The present land use surrounding the project site shall not be disturbed at any point of time.	<b>Condition Noted.</b>
16.	The green belt area shall be planted with indigenous native trees.	Greenbelt will be developed with indigenous native species. Greenbelt photograph is enclosed as <b>annexure-11.</b>

17.	Natural vegetation listed particularly the trees shall not be removed during the construction /operation phase. In case any trees are likely to be disturbed, shall be replanted.	<b>Condition noted.</b>
18.	During the construction and operation phase, there should be no disturbance to the aquatic eco-system within and outside the area.	<b>Condition noted.</b>
19.	The Provisions of Forest conservation act 1980, Wild Life Protection Act 1972 & Bio diversity Act 2002 should not be violated.	<b>Condition noted.</b>
20	There should be Firefighting plan and all required safety plan.	<b>Condition Noted.</b>
21.	Regular fire drills should be held to create awareness among owners/ residents.	<b>Condition noted.</b>

### **Part C - Specific Condition Construction Phase**

<b>S.NO</b>	<b>CONDITIONS</b>	<b>STATUS OF COMPLIANCE</b>
<b>1.</b>	<b>Construction Schedule:</b>	
	i) The Project proponent shall have to furnish the probable date of commissioning of the project supported with necessary bar charts to SEIAA-TN.	<b>Condition Noted.</b>
<b>2.</b>	<b>Labour Welfare:</b>	
	i) All the laborers to be engaged for construction should be screened for health and adequately treated before and during their employment on the work at the site.	Condition will be complied. All the member units will be instructed to comply with.

	<p>ii) Personnel working in dusty areas should wear protective respiratory devices and they should also be provided with adequate training and information on safety and health aspects. Occupational health surveillance program of the workers should be undertaken periodically to observe any contradictions due to exposure to dust and take corrective measures, if needed.</p>	<p>Condition will be complied. All the member units will be instructed to comply with.</p>
	<p>iii) Periodical medical examination of the workers engaged in the project shall be carried out and maintained. For the purpose, schedule of health examination of the workers should be drawn and followed accordingly. The workers shall be provided with personnel protective measures such as masks, gloves, boots etc.</p>	<p>Condition will be complied. All the member units will be instructed to comply with.</p>
<b>3.</b>	<b>Water Supply:</b>	
	<p>i) The entire water requirement during construction phase may be met from ground water source from the source with approval of the PWD Department of water resources/ may be out source.</p>	<p>Condition will be complied. The entire water requirement met from TWAD board.</p>
	<p>ii) Provision shall be made for the housing labour within the site with all necessary infrastructures and facilities such as fuel for cooking, mobile toilets, mobile STP, safe drinking water, medical health care, creche etc. The housing may be in the form of temporary structures to be removed after the completion of the project.</p>	<p>Housing for labours is not proposed, local manpower will be used for construction.</p>

	iii) Adequate drinking water and sanitary facilities should be provided for construction workers at the site. The treatment and disposal of waste water shall be through dispersion trench after treatment through septic tank. The MSW generated shall be disposed through Local Body and the identified dumpsite only.	Condition will be complied. All the member units will be instructed to comply with.
	iv) Water demand during construction should be reduced by use of premixed concrete, curing agents and other best practices prevalent.	<b>Condition is being complied.</b>
	v) Fixtures for showers, toilet flushing and drinking water should be of low flow type by adopting the use of aerators / pressure reducing devices / sensor based control.	<b>Condition Noted.</b> All the member units shall comply with.
<b>4.</b>	<b>Solid Waste Management:</b>	
	i) In the solid waste management plan, the STP sludge management plan for direct use as manure, gardens is not acceptable; it must be co-composted with biodegradables.	All the member units will be instructed to comply with all applicable rules and guidelines.
	ii) House hold hazardous wastes such as batteries, small electronics, CFL bulbs, expired medicines and used cleaning solvent bottles should be segregated at source, in a month from residences and disposed as per the SWM rules 2016.	Not applicable It is an infrastructure development project.
	iii) Domestic solid wastes to be regularly collected in bins or waste handling receptacles as per the solid waste management rules 2016.	<b>Condition will be complied.</b> All the member units will be instructed to follow all applicable rules and guidelines.
	iv) No waste of any type to be disposed of in any watercourse including drains, canals and the surrounding environment.	<b>Condition will be complied.</b> All the member units will be instructed to follow all applicable rules and guidelines.

	v) E-waste shall be disposed through Authorized vendor as per E-waste (Management and Handling) Rules, 2016 and subsequent amendment.	<b>Condition will be complied.</b> All the member units will be instructed to follow all applicable rules and guidelines.
<b>5.</b>	<b>Top Soil Management:</b>	
	i) All the top soil excavated during construction activities should be stored for use in horticulture/ landscape development within the project site.	<b>Condition will be complied.</b>
<b>6.</b>	<b>Construction Debris disposal:</b>	
	i) Disposal of construction debris during construction phase should not create any adverse effect on the neighboring communities and be disposed off only in approved sites, with the approval of Competent Authority with necessary precautions for general safety and health aspects of the people. The construction and demolition waste shall be managed as per Construction & Demolition Waste Management rules, 2016.	All the member units will be instructed to follow all applicable rules and guidelines.
	ii) Construction spoils, including bituminous materials and other hazardous materials must not be allowed to contaminate watercourses. The dump sites for such materials must be secured so that they should not leach into the adjacent land/lake/stream etc.	Condition noted.
<b>7.</b>	<b>Diesel Generator sets:</b>	
	i) Low Sulphur Diesel shall be used for operating diesel generator sets to be used during construction phase. The air and noise emission shall conform to the standards prescribed in the Rules under the Environment (Protection) Act, 1986, and the Rules framed thereon.	All the member units will be instructed to follow all applicable rules and guidelines.

	ii) The diesel required for stand by DG sets shall be stored in underground tanks fulfilling the safety norms and if required, clearance from Chief Controller of explosives shall be taken.	All the member units will be instructed to follow all applicable rules and guidelines.
	iii) The acoustic enclosures installed at all noise generating equipments such as DG sets, air conditioning systems, cooling water tower etc.	All the member units shall comply with.
<b>8.</b>	<b>Air &amp; Noise Pollution Control:</b>	
	i) Vehicles hired for bringing construction materials to the site should be in good condition and should conform to air and noise emission standards, prescribed by TNPCB/CPCB'. The vehicles should be operated only during non-peak hours.	<b>Condition will be complied.</b>
	ii) Ambient air and noise levels should conform to residential standards prescribed by the TNPCB, both during day and night. Incremental pollution loads on the ambient air and noise quality should be closely monitored during the construction phase. The pollution abatement measures shall be strictly implemented.	<b>Condition is being complied.</b> All the member units will be instructed to follow all applicable rules and guidelines. Ambient Air and Noise monitoring reports are attached as <b>Annexure - 5</b> .
	iii) Traffic congestion near the entry and exit points from the roads adjoining the proposed project site shall be avoided. Parking shall be fully internalized and no public space should be utilized. Parking plan to be as per DTCP norms. The traffic department shall be consulted and any cost effective traffic regulative facility shall be meet before commissioning.	<b>Condition will be complied.</b>



	iv) The buildings should have adequate distance between them to allow free movement of fresh air .and passage of natural light, air and ventilation.	All the member units will be instructed to follow all applicable rules and guidelines.
<b>9.</b>	<b>Building material:</b>	
	i) Fly-ash blocks should be used as building material in the construction as per the provision of Fly ash Notification of September, 1999 and amended as on 27th August, 2003 and Notification No. S.O. 2807 (E) dated: 03.11.2009.	<b>Condition Noted.</b> All the member units shall comply with.
	ii) Ready-mix concrete shall alone be used in building construction and necessary cube- tests should be conducted ascertain their quality.	Condition will be complied.
	iii) Use of glass shall be reduced up to 40% to reduce the electricity consumption and load on air conditioning. If necessary, high quality double glass with special reflecting coating shall be used in windows.	All the member units shall comply with.
<b>10.</b>	<b>Storm Water Drainage:</b>	
	i) Storm water management around the site and on site shall be established by following the guidelines laid down by the storm water manual.	<b>Condition noted.</b> Storm water drain will be provided all along the internal roads. All the member units will be instructed to follow all applicable rules and guidelines. Storm water photograph is enclosed as <b>annexure - 12</b>
	ii) Storm water management plan shall be obtained by engaging the services of Anna University/IIT.	<b>Condition Noted.</b>
<b>11.</b>	<b>Energy Conservation Measures:</b>	

i) Roof should meet prescriptive requirement as per Energy Conservation Building Code by using appropriate thermal insulation material, to fulfil the requirement.	All the member units will be instructed to follow all applicable rules and guidelines.
ii) Opaque wall should meet prescribed requirement as per Energy Conservation Building Code which is mandatory for all air conditioned spaces by use of appropriate thermal insulation material to fulfill the requirement.	All the member units will be instructed to follow all applicable rules and guidelines.
iii) All norms of Energy Conservation Building Code (ECBC) and National Building Code, 2005 as energy conservation have to be adopted Solar lights shall be provided for illumination of common areas.	All the member units will be instructed to follow all applicable rules and guidelines.
iv) Application of solar energy should be incorporated for illumination of common areas, lighting for gardens and street lighting. A hybrids system or fully solar system for a portion of the apartments shall be provided.	All the member units will be instructed to follow all applicable rules and guidelines.
v) A report on the energy conservation measures conforming to energy conservation norms prescribed by the Bureau of Energy Efficiency shall be prepared incorporating details about building materials & technology; R & U factors etc and submitted to the SEIAA in three month's time.	All the member units will be instructed to follow all applicable rules and guidelines.

	vi) Energy conservation measures like installation of CFLs/TFLs for lighting the areas outside the building should be integral part of the project design and should be in place before project commissioning.	<b>Condition is being complied</b> LED photographs is enclosed as <b>annexure-13</b>
<b>12.</b>	<b>Fire Safety</b>	
	i) Adequate fire protection equipments and rescue arrangements should be made as per the prescribed standards.	All the member units will be instructed to follow all applicable rules and guidelines.
	ii) Proper and free approach road for fire- fighting vehicles up to the buildings and for rescue in the event of emergency shall be made.	All the member units will be instructed to follow all applicable rules and guidelines.
<b>13.</b>	<b>Green Belt Development:</b>	
	i) The Project Proponent shall plant tree species with large potential for carbon capture in the proposed green belt area based on the recommendation of the Forest department well before the project is completed.	<b>Condition noted and will be complied.</b> All the member units will be instructed to plant tree species with large potential for carbon capture in the proposed greenbelt area . Greenbelt photograph is enclosed as <b>annexure</b>

	<p>ii) The purpose of Green belt around the project is to capture the fugitive emissions and to attenuate the noise generated, in addition to the improvement in the aesthetics. A wide range of indigenous plants species should be planted in and around the premise in consultation with the DFO, Villupuram District / State Agriculture University. The plants species should have thick canopy cover, perennial green nature, native origin and large leaf areas. Medium size trees and small trees alternating with shrubs shall be planted. If possible Miyawaki method of planting i.e planting different types of trees at very close escapement may be tried which will give a good green cover. A total of 15% of the plot area should be designated for green belt which should be raised along the boundaries of the plot and in between blocks in an organized manner.</p>	<p>Condition will be complied.</p> <p>Greenbelt will be developed in minimum 33% of total developable area with indigenous native species.</p> <p>Greenbelt photograph is enclosed as <b>annexure.</b></p>
	<p>iii)The proponent shall develop the green belt as per the plan furnished and area earmarked for the greenbelt shall not be alter at any point of time for any other purpose.</p>	<p>Greenbelt will be developed as per the DTCP approved layout plan.</p> <p>Green belt photograph is enclosed as <b>Annexure-11.</b></p>
	<p>iv) The proponent has to earmark the greenbelt area with dimension and GPS coordinates for the green belt area and the same shall be included in the layout out plan to be submitted for DTCP approval.</p>	<p>Greenbelt will be developed as per the DTCP approved layout plan.</p> <p>Green belt photograph is enclosed as <b>Annexure-11.</b></p>
<b>14.</b>	<b>Sewage Treatment Plant:</b>	

	<p>i) The Sewage Treatment Plant (STP) installed should be certified by an independent expert/reputed academic institution for its adequacy and a report in this regard should be submitted to the SEIAA, TN before the project is commissioned for operation. Explore the less power consuming systems viz baffle reactor, etc., for the treatment of sewage.</p>	<p>STP is not proposed by SIPCOT. Individual industries will be mandated to have STP/ETP as per the requirement and to reuse the treated wastewater as per the norms. All the member industries will be instructed to follow applicable rules and guidelines.</p>
	<p>ii) The Proponent shall install STP as furnished. Any alteration to satisfy the bathing quality shall be informed to SEIAA-TN.</p>	<p>STP is not proposed by SIPCOT. All the member industries will be instructed to follow applicable rules and guidelines</p>
	<p>iii) The project proponent shall operate and maintain the Sewage treatment Plant effectively to meet out the standards prescribed by the CPCB.</p>	<p>STP is not proposed by SIPCOT. All the member units will be instructed to handle their Treated effluent as per prescribed by CPCB norms.</p>
	<p>iv) The project proponent shall continuously operate and maintain the Sewage treatment plant to achieve the standards prescribed by the CPCB.</p>	<p>STP is not proposed by SIPCOT. All the member units will be instructed to handle their Treated effluent as per prescribed by CPCB norms.</p>
	<p>v) The project proponent has to ensure the complete recycling of treated sewage after achieving the standards prescribed by the CPCB.</p>	<p>STP is not proposed by SIPCOT. All the member units will be instructed to handle their Treated effluent as per prescribed by CPCB norms.</p>
	<p>vi) The project proponent has to provide separate standby D.G set for the STP for the continuous operation of the STP in case of power failure.</p>	<p>All the member units shall comply with.</p>
<b>15.</b>	<b>Rain Water Harvesting:</b>	

	i) The proponent/Owner of the Flats shall ensure that roof rain water collected from the covered roof of the buildings, etc shall be harvested so as to ensure the maximum beneficiation of rain water harvesting by constructing adequate sumps so that 100% of the harvested water shall be reused.	All the member units shall comply with.
	ii) Rain water harvesting for surface run-off, as per plan submitted should be implemented. Before recharging the surface run off, pre- treatment with screens, settlers etc. must be done to remove suspended matter, oil and grease, etc.	All the member units shall comply with.
	iii) The project activity should not cause any disturbance & deterioration of the local bio diversity.	Condition noted.
<b>16.</b>	<b>Building Safety:</b>	
	Lightning arrester shall be properly designed and installed at top of the building and where ever is necessary.	All the member industries will be instructed to follow applicable rules and guidelines.

## **5. ENVIRONMENTAL MONITORING DETAILS**

It is mandatory to submit six month compliance report of EC conditions to MoEF & CC Regional Office by the proponent. For the purpose of submitting Six-Monthly Compliance report, the environmental monitoring was carried out by M/s. Hubert Enviro Care Systems Pvt. Ltd an NABL Accredited Laboratory for the period of October 2024 – March 2025.

### **5.1 Ambient Air Quality monitoring**

During construction phase, particulate matter and gaseous emissions are likely to arise from the site movement of vehicles, operation of DG sets etc., the ambient air quality parameters such as suspended Particulate matter (PM<sub>10</sub>), Respirable Particulate matter (PM<sub>2.5</sub>), Sulphur dioxide, Oxides of Nitrogen (NO<sub>x</sub>), Ammonia, Ozone and Carbon monoxide were monitored. The test report of ambient air quality for the period of October 2024 – March 2025.is enclosed as **Annexure - 5**.

### **5.2 Ambient Noise level monitoring**

Ambient noise levels were monitored and the test report of ambient noise recorded during the period of October 2024 – March 2025.is enclosed as **Annexure - 5**.

### **5.3 Soil quality monitoring**

Soil samples were collected and analyzed for nutrients and heavy metals. The test report of soil samples collected and analyzed during the period of October 2024 – March 2025 is enclosed as **Annexure - 5**.

### **5.4 Ground water quality monitoring**

Ground water was tested for various water quality parameters during the period of October 2024 – March 2025. The test report of ground water collected and analyzed is enclosed as **Annexure-5**.

### **5.5 Surface water quality monitoring**

The surface water was collected and tested for various water quality parameters during the period of October 2024 – March 2025.The test report of surface water collected and analyzed is enclosed as **Annexure- 5**.



## 6. CONCLUSION

1. The environmental monitoring was carried out at site during the period of October 2024 – March 2025.
2. All the conditions stipulated in Environmental Clearance are being complied / will be complied.

  
**Dr. RAJKUMAR SAMUEL**  
Director Technical

**Name:** Dr. Rajkumar Samuel  
**Designation:** Director Technical  
**Company Name:** Hubert Enviro  
Care Systems Private Limited



**Dr. JAYANTHI. M, I.F.S**  
**MEMBER SECRETARY**

**STATE LEVEL ENVIRONMENT IMPACT  
ASSESSMENT AUTHORITY – TAMIL NADU**

3rd Floor, Panagal Maaligai,  
No.1 Jeenis Road, Saidapet,  
Chennai-15.  
Phone No.044-24359973  
Fax No. 044-24359975

**ENVIRONMENTAL CLEARANCE (EC)**

**Letter No. SEIAA-TN/F. 6497/EC/ 8(b)/ 681/2019 dated: 27.11.2019.**

To

The Managing Director  
M/s. State Industries Promotion Corporation of Tamil Nadu Limited.  
19-A, Rukmani Lakshmiipathy Road  
Post Box No.7223  
Egmore  
Chennai-600 008

Sir,

Sub: SEIAA, TN - Environmental Clearance -- Proposed establishment of Industrial Park at Thindivanam by M/s. State Industries Promotion Corporation of Tamil Nadu Limited at S.F. No. 1, 2, 3, 4, 5, 6, 10pt, 13pt, 14, 15, 16, 17, 18, 19, 20, 21pt, 22/1, 2, 32, 33, 34, 35, 36, 37, 38pt, 39, 40, 41, 42, 43/1pt, 2, 45, 46, 47, 48/1, 49, 50, 51, 52, 53, 54, 55, 56, 57, 60, 61/1, 2, 3pt, 62, 63, 64, 118, 120, 121, 123, 125, 126, 129 of Pelakuppam Village, 46pt, 47pt, 48pt, 50pt, 51, 52pt, 53pt, 55pt of Venmaniyathoor Village, 181pt, 182, 183, 184, 194, 195, 196, 197, 198, 199, 200, 201, 202, 203, 204, 205, 206, 207, 208, 209, 210, 212, 213pt, 214, 237, 244, 245 & 246pt of Kollar Village, Thindivanam Taluk, Villupuram District, Tamil Nadu - Issued -- Regarding.

Ref: 1. Your application for Terms of Reference dated: 01.02.2018

2. ToR Issued by SEIAA-TN Vide Lr.No.SEIAA-TN/F.No.6497/2018/8(b)/ToR-506/2018 dated: 16.07.2018



*Jayanthi*  
**MEMBER SECRETARY**  
**SEIAA-TN**

3. EIA report submitted to SEIAA-TN on 05.04.2019
4. Minutes of the 133<sup>rd</sup> SEAC Meeting held on 25.07.2019
5. Proponent reply dated: 30.10.2019
6. Minutes of the 139<sup>th</sup> SEAC Meeting held on 23.11.2019
7. Minutes of the 362<sup>nd</sup> SEIAA Meeting held on 27.11.2019

\*\*\*\*\*

This has reference to your application 1<sup>st</sup> cited, the proposal is for obtaining Environmental Clearance to establish a construction project under Category B2 and Schedule S.No. 8(b) under the Environment Impact Assessment Notification, 2006, as amended.

The Competent Authority and Authorized signatory furnished detailed information in Form 1 and Form 1A and liquidate enclosures are as Annexures:

**Annexure 1**

PROJECT DETAILS		
SL No	Description	Details
1)	Name of the Project proponent and address	The Managing Director M/s. State Industries Promotion Corporation of Tamil Nadu Limited. 19-A, Rukmani Lakshmipathy Road Post Box no.7223 Egmore Chennai-600 008
2)	Proposed Activity	Proposed establishment of Industrial Park at Thindivanam
3)	Schedule No.	8(b)
4)	Project Location	
	i) Survey No	1, 2, 3, 4, 5, 6, 10pt, 13pt, 14, 15, 16, 17, 18, 19, 20, 21pt, 22/1, 2, 32, 33, 34, 35, 36, 37, 38pt, 39, 40, 41, 42, 43/1pt, 2, 45, 46, 47, 48/1, 49, 50, 51, 52, 53, 54, 55,



*Jagan*  
MEMBER SECRETARY  
SEIAA-TN

		56, 57, 60, 61/1, 2, 3pt, 62, 63, 64, 118, 120, 121, 123, 125, 126, 129 of Pelakuppam Village, 46pt, 47pt, 48pt, 50pt, 51, 52pt, 53pt, 55pt of Venmaniyathoor Village, 181pt, 182, 183, 184, 194, 195, 196, 197, 198, 199, 200, 201, 202, 203, 204, 205, 206, 207, 208, 209, 210, 212, 213pt, 214, 237, 244, 245 & 246pt of Kollar																																	
	ii)Revenue Village	Pelakuppam, Venmaniyathoor, Kollar Village																																	
	iii)Taluk	Thindivanam																																	
	iv)District	Villupuram																																	
5)	Area of the Land	291.60.5 Hectares																																	
6)	Built up Area																																		
	<table border="1"> <thead> <tr> <th>Sl.No.</th><th>Description</th><th>Area (Hectares)</th></tr> </thead> <tbody> <tr> <td>1</td><td>Plot area</td><td>195.29</td></tr> <tr> <td>2</td><td>Roads and Storm water drainage</td><td>13.56</td></tr> <tr> <td>3</td><td>Common amenities (EB, Water storage, Fire Services, Administrative Office, etc.)</td><td>4.37</td></tr> <tr> <td>4</td><td>Commercial activities</td><td>14.57</td></tr> <tr> <td>5</td><td>Green Belt outside plot area (OSR)</td><td>26.81</td></tr> <tr> <td>6</td><td>Green Belt along roadside</td><td>3.51</td></tr> <tr> <td>7</td><td>Solid Waste Management</td><td>10.00</td></tr> <tr> <td></td><td><b>Total developable area</b></td><td><b>268.11</b></td></tr> <tr> <td></td><td>Water bodies (which will not be encroached)</td><td>23.49</td></tr> <tr> <td></td><td><b>Total IP area</b></td><td><b>291.60</b></td></tr> </tbody> </table>	Sl.No.	Description	Area (Hectares)	1	Plot area	195.29	2	Roads and Storm water drainage	13.56	3	Common amenities (EB, Water storage, Fire Services, Administrative Office, etc.)	4.37	4	Commercial activities	14.57	5	Green Belt outside plot area (OSR)	26.81	6	Green Belt along roadside	3.51	7	Solid Waste Management	10.00		<b>Total developable area</b>	<b>268.11</b>		Water bodies (which will not be encroached)	23.49		<b>Total IP area</b>	<b>291.60</b>	
Sl.No.	Description	Area (Hectares)																																	
1	Plot area	195.29																																	
2	Roads and Storm water drainage	13.56																																	
3	Common amenities (EB, Water storage, Fire Services, Administrative Office, etc.)	4.37																																	
4	Commercial activities	14.57																																	
5	Green Belt outside plot area (OSR)	26.81																																	
6	Green Belt along roadside	3.51																																	
7	Solid Waste Management	10.00																																	
	<b>Total developable area</b>	<b>268.11</b>																																	
	Water bodies (which will not be encroached)	23.49																																	
	<b>Total IP area</b>	<b>291.60</b>																																	
7)	<p>Brief description of the project</p> <p>The proposal is an infrastructure development project. It involves development of roads, water supply, storm water drainage, street lights, green belt</p>																																		



*Jayaram*  
MEMBER SECRETARY  
SEIAA-TN

	<p>development, and such other amenities.</p> <p>Industrial Park will house industries which do not fall under EIA Notification 2009 and amendments thereof. The proposed industries include the following:</p> <ul style="list-style-type: none"> <li>• All General Engineering units such as fabrication, machining, forging, castings etc.,</li> <li>• Auto components Industries.</li> <li>• Food Processing Industries.</li> <li>• Packaging units.</li> </ul> <p>Any other industries that are not under the purview of EIA Notification, 2006</p>																			
8)	Land Use Classification	Patta dry land & Govt Poramboke Land																		
9)	<p>Green Belt</p> <table border="1"> <thead> <tr> <th>Sl.No.</th><th>Description</th><th>Area (Hectares)</th></tr> </thead> <tbody> <tr> <td>1.</td><td>By SIPCOT outside the plot area</td><td>58.59</td></tr> <tr> <td>2.</td><td>By SIPCOT along the Road sides and Central meridian</td><td>26.81</td></tr> <tr> <td>3.</td><td>By Member Industries (30 % of the total plot area allotted to Member Industries) i.e 30% of 195.29 Ha</td><td>3.51</td></tr> <tr> <td></td><td><b>Total</b></td><td>88.91</td></tr> <tr> <td></td><td>Percentage of Green Belt among Total developable Area of Industrial Park i.e 268.11 hectares</td><td>33.16%</td></tr> </tbody> </table>		Sl.No.	Description	Area (Hectares)	1.	By SIPCOT outside the plot area	58.59	2.	By SIPCOT along the Road sides and Central meridian	26.81	3.	By Member Industries (30 % of the total plot area allotted to Member Industries) i.e 30% of 195.29 Ha	3.51		<b>Total</b>	88.91		Percentage of Green Belt among Total developable Area of Industrial Park i.e 268.11 hectares	33.16%
Sl.No.	Description	Area (Hectares)																		
1.	By SIPCOT outside the plot area	58.59																		
2.	By SIPCOT along the Road sides and Central meridian	26.81																		
3.	By Member Industries (30 % of the total plot area allotted to Member Industries) i.e 30% of 195.29 Ha	3.51																		
	<b>Total</b>	88.91																		
	Percentage of Green Belt among Total developable Area of Industrial Park i.e 268.11 hectares	33.16%																		
10)	<b>UTILITIES-WATER</b>																			
	a) Total Water Requirements	4 MLD																		
	b) Source from where the water is proposed to be drawn	<p>3 MLD Tertiary Treatment Reverse Osmosis (TTRRO) water from Thindivanam Municipality</p> <p>1 MLD for drinking water from Tamil Nadu Water Supply and Drainage Board (TWAD)</p>																		
	c) Sewage system	All member units will be mandated to																		



*Jayasi*  
**MEMBER SECRETARY**  
 SEIAA-TN

		install "Zero Liquid Discharge" based Effluent Treatment Plants to reclaim water for recycle/reuse in their utilities and green belt development. The quantity of sewage that will be generated from SIPCOT administrative office will be managed in septic tank followed by soak pit .
	d) ETP & Recycle line	All member units will be mandated to install "Zero Liquid Discharge" based Effluent Treatment Plants to reclaim water for recycle/reuse in their utilities and green belt development.
11)	Solid Waste Management	Area of 10Ha has been earmarked for establishing a solid waste management facility SIPCOT will identify a TSDF provider and facilitate to establish such a treatment, storage and disposal facility(TSDF) in line with guidelines of CPCB & MoEF & CC Solid waste generated will be disposed to the approved Municipal Solid Waste Management or else SIPCOT will set up its facility through renowned agencies by outsourcing their services on annual contract basis
12)	Power requirement	50MW from TANGEDCO
13)	Project Cost	Rs. 300 Crores
14)	EMP Cost	For Operation Phase: Capital Cost -1 Crores,



*Tajani*  
MEMBER SECRETARY  
SEIAA-TN



	Operation cost- 50 Lakhs per annum
--	------------------------------------

**Annexure 2- Affidavit**

The Proponent has furnished affidavit in Twenty Rupees stamp paper attested by the Notary stating that

I Thiru. J.Kumargurubaran, IAS, Managing Director, Authorised Signatory, represent M/s. State Industries Promotion Corporation of Tamilnadu Limited (SIPCOT), 19-A, Rukmani Lakshmiopathy Road, Egmore, Chennai - 600008.

We have proposed to establish an industrial park over an extent of 291.605 hectares at Pelakuppam, Kollar & Venmaniyathur villages of Tindivanam taluk, Villupuram district. An application submitted by us seeking Environmental Clearance under the EIA Notification, 2006 is under scrutiny in the Authority. I am furnishing the following undertaking to the Authority, hereby solemnly affirm and state as follows:-

1. we will develop Green belt in OSR areas and along the roadsides in 11.31 % of the total developable area of 268.11 hectares i.e 30.32 hectares. Further, we will also ensure the development of green belt in 30% of the allotted area by the member units i.e 58.59 hectares, which is 21.85% of total developable area. It will be made as a mandatory condition in the land allotment order as well as the lease deed to be executed between SIPCOT and allottees. The net area of green belt of the proposed industrial park in the post project scenario will be 88.91 hectares, which is 33.16% of the total developable area of the park.
2. We commit to SEIAA that the total water requirement for the park is 4 MLD out of which potable water would be around 1 MLD and the balance 3 MLD would be for non potable purposes. The required potable water will be obtained from Tamil Nadu Water Supply and Drainage Board (TWAD) and non potable water from Tertiary Treatment Reverse Osmosis (TTRO) plant to be setup at Tindivanam. SIPCOT is already in discussion with Commissioner of Municipal Administration (CMA) for setting up of TTRO plant. We assure that the required permission from the competent Authority for supply of water for entire period of operation will be obtained before applying for Consent for Operation (CTO) from Tamilnadu Pollution Control Board (TNPCB).



*Jagan*  
MEMBER SECRETARY  
SEIAA-TN

3. We commit to SEIAA that all member units will be mandated to install "Zero Liquid Discharge" based Effluent Treatment Plants to reclaim water for recycle/reuse in their utilities and green belt development. We will mandate to member units to manage the sewage as per TNPCB norms. The solid waste stream will be sent to TNPCB approved vendors/TSDf for proper and ultimate disposal. The quantity of sewage that will be generated from SIPCOT administrative office will only be 1000 litres/day and it will be managed in septic tank followed by soak pit as onsite construction.
4. We commit to SEIAA that all member units will be mandated to provide rain water harvesting structures as per norms. SIPCOT will construct percolation tanks for harvesting the rainwater in the project office.
5. We commit to SEIAA that we will provide storm water drainage system as open concrete channels, all along the road side for ensuring proper collection of storm water and will let out in the nearby water bodies. We also assure that the storm water drain would not carry any untreated or treated sewage.
6. We commit to SEIAA that we will undertake CER activities as per norms with the approval of board of SIPCOT.
7. We also assure that our project site does not encroach any water bodies such as rivers, canals, nallas, lakes, ponds, tanks, etc., from its original boundary.
8. We are aware that we can be prosecuted under relevant Act and Rules, if we are not ensuring the adherence of the above commitment.

Commitment signed by me as an Authorized signatory of the Project Proponent before the SEIAA, Tamil Nadu.

The project activity is covered in 8(b) of the Schedule and is of B2 category. It does not require Public Consultation as per Para 7 III Stage (3) (i) (d) of EIA Notification, 2006.

The Authority after consideration all the requisite documents with status and data and based on SEAC appraisal and recommendations for issue of Environmental Clearance in its 139<sup>th</sup> meeting held on 23.11.2019, SEIAA placed the proposal in the



*Jayaram*  
MEMBER SECRETARY  
SEIAA-TN



362<sup>nd</sup> SEIAA meeting held on 27.11.2019 hereby conveyed Environmental Clearance along with the conditions containing four parts namely

Part - A –Common conditions applicable for Pre-construction, Construction and Operational Phases

Part - B –Specific Conditions – Pre construction phase

Part - C - Specific Conditions – Construction phase

Part – D - Specific Conditions – Operational Phase/Post constructional Phase / Entire life of the project.

**Validity:**

The SEIAA hereby accords Environmental Clearance to the above project under the provisions of EIA Notification dated 14<sup>th</sup> September, 2006 as amended, with validity for Seven years from the date of issue of EC, subject to the compliance of the terms and conditions stipulated below:


**Part - A – Common conditions applicable for Pre-construction, Construction and Operational Phases:**

1. Any appeal against this environmental clearance shall lie with the Hon'ble National Green Tribunal, if preferred, within a period of 30 days as prescribed under Section 16 of the National Green Tribunal Act, 2010.
2. The construction of STP, Solid Waste Management facility, E-waste management facility, DG sets, etc., should be made in the earmarked area only. In any case, the location of these utilities should not be changed later on.
3. The Environmental safeguards contained in the application of the proponent /mentioned during the presentation before the State Level Environment Impact Assessment Authority / State Level Expert Appraisal Committee should be implemented in the letter and spirit.
4. All other statutory clearances such as the approvals for storage of diesel from Chief Controller of Explosives, Fire and Rescue Services Department, Civil Aviation Department, Forest Conservation Act, 1980 and Wild Life (Protection) Act, 1972, State / Central Ground Water Authority, Coastal Regulatory Zone



*Jayanti*  
MEMBER SECRETARY  
SEIAA-TN

- Authority, other statutory and other authorities as applicable to the project shall be obtained by project proponent from the concerned competent authorities.
5. The SEIAA reserves the right to add additional safeguard measures subsequently, if non-compliance of any of the EC conditions is found and to take action, including revoking of this Environmental Clearance as the case may be.
  6. A proper record showing compliance of all the conditions of Environmental Clearance shall be maintained and made available at all the times.
  7. The environmental statement for each financial year ending 31st March in Form-V as is mandated to be submitted by the project proponent to the concerned State Pollution Control Board as prescribed under the Environment (Protection) Rules, 1986, as amended subsequently, shall also be put on the website of the company. The status of compliance of environmental clearance conditions and shall also be sent to the Regional Office of the Ministry of Environment and Forests, Chennai by e-mail.
  8. The Regional Office of the Ministry located at Chennai shall monitor compliance of the stipulated conditions. The project authorities should extend full cooperation to the officer (s) of the Regional Office by furnishing the requisite data / information / monitoring reports.
  9. "Consent for Establishment" shall be obtained from the Tamil Nadu Pollution Control Board and a copy shall be submitted to the SEIAA, Tamil Nadu.
  10. In the case of any change(s) in the scope of the project, a fresh appraisal by the SEAC/SEIAA shall be obtained before implementation.
  11. The conditions will be enforced inter-alia, under the provisions of the Water (Prevention & Control of Pollution) Act, 1974, the Air (Prevention & Control of Pollution) Act, 1981, the Environment (Protection) Act, 1986, the Public Liability Insurance Act, 1991, along with their amendments, draft Minor Mineral Conservation & Development Rules, 2010 framed under MMDR Act 1957, National Commission for protection of Child Right Rules, 2006 and rules made there under and also any other orders passed by the Hon'ble Supreme



  
MEMBER SECRETARY  
SEIAA-TN


Court of India/Hon'ble High Court of Madras and any other Courts of Law, including the Hon'ble National Green Tribunal relating to the subject matter.

12. The Environmental Clearance shall not be cited for relaxing the other applicable rules to this project.
13. Failure to comply with any of the conditions mentioned above may result in withdrawal of this clearance and attract action under the provisions of the Environment (Protection) Act, 1986.
14. The proponent shall upload the status of compliance of the stipulated EC conditions, including results of monitored data on their website and shall update the same periodically. It shall simultaneously be sent to the Regional Office of MoEF, Chennai, the respective Zonal Office of CPCB, Bengaluru and the TNPCB. The criteria pollutant levels namely; PM10, PM2.5, SO2, NOx (ambient levels as well as stack emissions) or critical sectoral parameters, indicated for the project shall be monitored.
15. The SEIAA, TN may cancel the environmental clearance granted to this project under the provisions of EIA Notification, 2006, if, at any stage of the validity of this environmental clearance, if it is found or if it comes to the knowledge of this SEIAA, TN that the project proponent has deliberately concealed and/or submitted false or misleading information or inadequate data for obtaining the environmental clearance.
16. The Environmental Clearance does not imply that the other statutory / administrative clearances shall be granted to the project by the concerned authorities. Such authorities would be considering the project on merits and be taking decisions independently of the Environmental Clearance.
17. The SEIAA, TN may alter/modify the above conditions or stipulate any further condition in the interest of environment protection, even during the subsequent period.
18. The Environmental Clearance does not absolve the applicant/proponent of his obligation/requirement to obtain other statutory and administrative clearances from other statutory and administrative authorities.



*Jayaram*  
MEMBER SECRETARY  
SEIAA-TN

19. Where the trees need to be cut, compensation plantation in the ratio of 1:10 (i.e. planting of 10 trees for every one tree that is cut) should be done with the obligation to continue maintenance.
20. A separate environmental management cell with suitable qualified personnel should be set-up under the control of a Senior Executive who will report directly to the Head of the Organization and the shortfall shall be strictly reviewed and addressed.
21. The EMP cost of Rs.1.5 Crores shall be deposited in a Nationalized bank by opening separate account and the head wise expenses statement shall be submitted to TNPCB with a copy to SEIAA annually.
22. The project activity should not cause any disturbance & deterioration of the local bio diversity.
23. The project activity should not impact the water bodies. A detailed inventory of the water bodies and forest should be evaluated and fact reported to the Forest Department & PWD for monitoring.
24. All the assessed flora & fauna should be conserved and protected.
25. The proponent should strictly comply with, Tamil Nadu Government Order (Ms) No.84 Environment and forests (EC.2) Department dated 25.06.2018 regarding ban on one time use and throwaway plastics irrespective of thickness with effect from 01.01.2019 under Environment (Protection) Act, 1986.
26. As per MoEF & CC, GoI, Office Memorandum dated 30.03.2015, prior clearance from Forestry & Wildlife angle including clearance from obtaining committee of the National Board for Wildlife as applicable shall be obtained before starting the quarrying operation, if the project site is located within 10KM from National Park and Sanctuaries.
27. Traffic congestion near the entry and exit points from the roads adjoining the proposed project site must be avoided.
28. The safety measures proposed in the report should be strictly followed.
29. The Developer shall ensure that no allotment letter/ sale deed in any form shall be made to house category A or category B industry as prescribed in the



*Jagani*  
MEMBER SECRETARY  
SEIAA-TN



schedule of EIA notification 2006. However, in case any category A or category B type of industry as prescribed in the schedule of EIA notification 2006 is proposed then the individual unit shall apply and seek Environmental Clearance under the EIA notification 2006.

30. The Developer shall mandate the member industries of the Industrial Park to allot 33% of the plot area for green belt development and to install RWH structures.
31. The Developer has to ensure that all the member industries within the Industrial Park shall make their own arrangements to achieve zero discharge of the trade effluents, solid waste & E waste management, gaseous emission and noise control measures to achieve the standards prescribed by the TNPCB.
32. The project proponent shall ensure that the individual member units will not be allowed to carry out manufacturing of products stipulated in G.O. (Ms) No. 84 dated 25/06/2018 on banning of one time use on and throwaway plastics.
33. The project proponent must submit the permissible land use classification certificate obtained from competent authority for the proposed project before obtain the CTE from TNPCB.
34. The proponent shall obtain the necessary permission/ NOC of water supply from the TWAD Board/competent Authority.
35. The CER fund shall be utilized as per the office memorandum of MoEF & CC dated 01.05.2018 before obtaining CTO from TNPCB.
36. The allotted industrial units shall obtain consent from the TNPCB separately for their establishment & operation in this industrial estate.
37. The project proponent shall ensure that 33% of the total area of the project site should be covered with green belt.
38. The proponent shall provide Rain Water Harvesting pits so as to recharge the ground water table.
39. Discharge of treated sewage shall conform to the norms & standards prescribed by the Tamil Nadu Pollution Control Board.



  
MEMBER SECRETARY  
SEIAA-TN

40. It is the sole responsibility of the proponent that the treated sewage disposed for green belt development/ avenue plantation should not pollute the soil/ ground water/ adjacent canals/ lakes/ ponds, etc.
41. The Developer has to ensure that all the member industries within the Industrial Park shall make their own arrangements to achieve zero discharge of the trade effluents,
42. The project proponent shall ensure that all the member units should treat and dispose solid waste & E-waste as per the Solid Waste Management Rule 2016 as amended and E-Waste Management Rules, 2016
43. There shall be no discharge of effluent outside the Industrial Park at any time.
44. The Developer shall mandate the member units of the Industrial Park to install adequate APC measures/Acoustic to achieve air emissions standards within permissible limits prescribed by the CPCB.

**Part - B – Specific Conditions – Pre construction phase:**

1. The project authorities should advertise with basic details at least in two local newspapers widely circulated, one of which shall be in the vernacular language of the locality concerned, within 7 days of the issue of clearance. The press releases also mention that a copy of the clearance letter is available with the State Pollution Control Board and also at website of SEIAA, TN. The copy of the press release should be forwarded to the Regional Office of the Ministry of Environment and Forests located at Chennai and SEIAA-TN.
2. In the case of any change(s) in the scope of the project, a fresh appraisal by the SEAC/SEIAA shall be obtained before implementation.
3. A copy of the clearance letter shall be sent by the proponent to the Local Body. The clearance letter shall also be put on the website of the Proponent.
4. The approval of the competent authority shall be obtained for structural safety of the buildings during earthquake, adequacy of fire fighting equipments, etc as per National Building Code including protection measures from lightning etc before commencement of the work.



*Jayaram*  
**MEMBER SECRETARY**  
**SEIAA-TN**

5. All required sanitary and hygienic measures for the workers should be in place before starting construction activities and they have to be maintained throughout the construction phase.
6. Design of buildings should be in conformity with the Seismic Zone Classifications.
7. The Construction of the structures should be undertaken as per the plans approved by the concerned local authorities/local administration.
8. No construction activity of any kind shall be taken up in the OSR area.
9. Consent of the local body concerned should be obtained for using the treated sewage in the OSR area for gardening purpose. The quality of treated sewage shall satisfy the bathing quality prescribed by the CPCB.
10. The height and coverage of the constructions shall be in accordance with the existing FSI/FAR norms as per Coastal Regulation Zone Notification, 2011.
11. The Project Proponent shall provide car parking exclusively for the visiting guest in the proposed residential apartments as per CMDA norms.
12. The project proponent shall ensure the level of basement shall be above maximum flood level.
13. The proponent shall prepare completion plans showing Separate pipelines marked with different colours with the following details
  - i. Location of STP, compost system, underground sewer line.
  - ii. Pipe Line conveying the treated effluent for green belt development.
  - iii. Pipe Line conveying the treated effluent for toilet flushing
  - iv. Water supply pipeline
  - v. Gas supply pipe line, if proposed
  - vi. Telephone cable
  - vii. Power cable
  - viii. Storm water drains, and
  - ix. Rain water harvesting system, etc., and it shall be made available to the



*Jayam*  
MEMBER SECRETARY  
SEIAA-TN

14. A First Aid Room shall be provided in the project site during the entire construction and operation phases of the project.
15. The present land use surrounding the project site shall not be disturbed at any point of time.
16. The green belt area shall be planted with indigenous native trees.
17. Natural vegetation listed particularly the trees shall not be removed during the construction/operation phase. In case any trees are likely to be disturbed, shall be replanted.
18. During the construction and operation phase, there should be no disturbance to the aquatic eco-system within and outside the area.
19. The Provisions of Forest conservation Act 1980, Wild Life Protection Act 1972 & Bio diversity Act 2002 should not be violated.
20. There should be Fire fighting plan and all required safety plan.
21. Regular fire drills should be held to create awareness among owners/ residents.

**Part - C - Specific Conditions – Construction phase:**

**1. Construction Schedule:**

- i) The Project proponent shall have to furnish the probable date of commissioning of the project supported with necessary bar charts to SEIAA-TN.

**2. Labour Welfare:**

- i) All the labourers to be engaged for construction should be screened for health and adequately treated before and during their employment on the work at the site.
- ii) Personnel working in dusty areas should wear protective respiratory devices and they should also be provided with adequate training and information on safety and health aspects. Occupational health surveillance program of the workers should be undertaken periodically to observe any contradictions due to exposure to dust and take corrective measures, if needed.



*Jagan*  
**MEMBER SECRETARY**  
**SEIAA-TN**




- iii) Periodical medical examination of the workers engaged in the project shall be carried out and records maintained. For the purpose, schedule of health examination of the workers should be drawn and followed accordingly. The workers shall be provided with personnel protective measures such as masks, gloves, boots etc.

### 3. Water Supply:

- i) The entire water requirement during construction phase may be met from ground water source from the source with approval of the PWD Department of water resources/ may be out sourced.
- ii) Provision shall be made for the housing labour within the site with all necessary infrastructures and facilities such as fuel for cooking, mobile toilets, mobile STP, safe drinking water, medical health care, crèche etc. The housing may be in the form of temporary structures to be removed after the completion of the project.
- iii) Adequate drinking water and sanitary facilities should be provided for construction workers at the site. The treatment and disposal of waste water shall be through dispersion trench after treatment through septic tank. The MSW generated shall be disposed through Local Body and the identified dumpsite only.
- iv) Water demand during construction should be reduced by use of pre-mixed concrete, curing agents and other best practices prevalent.
- v) Fixtures for showers, toilet flushing and drinking water should be of low flow type by adopting the use of aerators / pressure reducing devices / sensor based control.

### 4. Solid Waste Management:

- i) In the solid waste management plan, the STP sludge management plan for direct use as manure for gardens is not acceptable; it must be co-composted with biodegradables.
- ii) House hold hazardous waste such as batteries, small electronics, CFL bulbs, expired medicines and used cleaning solvent bottles should be



*Jayaram*  
MEMBER SECRETARY  
SEIAA-TN

segregated at source, collected once in a month from residences and disposed as per the SWM rules 2016.

- iii) Domestic solid wastes to be regularly collected in bins or waste handling receptacles and disposed as per the solid waste management rules 2016.
- iv) No waste of any type to be disposed of in any watercourse including drains, canals and the surrounding environment.
- v) E-waste shall be disposed through Authorized vendor as per E-waste (Management and Handling) Rules, 2016 and subsequent amendment.

**5. Top Soil Management:**

- i) All the top soil excavated during construction activities should be stored for use in horticulture/ landscape development within the project site.

**6. Construction Debris disposal:**

- i) Disposal of construction debris during construction phase should not create any adverse effect on the neighboring communities and be disposed off only in approved sites, with the approval of Competent Authority with necessary precautions for general safety and health aspects of the people. The construction and demolition waste shall be managed as per Construction & Demolition Waste Management Rules, 2016.
- ii) Construction spoils, including bituminous materials and other hazardous materials, must not be allowed to contaminate watercourses. The dump sites for such materials must be secured so that they should not leach into the adjacent land/ lake/ stream etc.

**7. Diesel Generator sets:**

- i) Low Sulphur Diesel shall be used for operating diesel generator sets to be used during construction phase. The air and noise emission shall conform to the standards prescribed in the Rules under the Environment (Protection) Act, 1986, and the Rules framed thereon.



*[Signature]*  
**MEMBER SECRETARY**  
SEIAA-TN

- ii) The diesel required for operating stand by DG sets shall be stored in underground tanks fulfilling the safety norms and if required, clearance from Chief Controller of Explosives shall be taken.
- iii) The acoustic enclosures shall be installed at all noise generating equipments such as DG sets, air conditioning systems, cooling water tower etc.

#### 8. Air & Noise Pollution Control:

- i) Vehicles hired for bringing construction materials to the site should be in good condition and should conform to air and noise emission standards, prescribed by TNPCB/CPCB. The vehicles should be operated only during non-peak hours.
- ii) Ambient air and noise levels should conform to residential standards prescribed by the TNPCB, both during day and night. Incremental pollution loads on the ambient air and noise quality should be closely monitored during the construction phase. The pollution abatement measures shall be strictly implemented.
- iii) Traffic congestion near the entry and exit points from the roads adjoining the proposed project site shall be avoided. Parking shall be fully internalized and no public space should be utilized. Parking plan to be as per DTCP norms. The traffic department shall be consulted and any cost effective traffic regulative facility shall be met before commissioning.
- iv) The buildings should have adequate distance between them to allow free movement of fresh air and passage of natural light, air and ventilation.

#### 9. Building material:

- i) Fly-ash blocks should be used as building material in the construction as per the provision of Fly ash Notification of September, 1999 and amended as on 27th August, 2003 and Notification No. S.O. 2807 (E) dated: 03.11.2009.
- ii) Ready-mix concrete shall alone be used in building construction and necessary cube-tests should be conducted to ascertain their quality.



*Dayan*  
MEMBER SECRETARY  
SEIAA-TN

- iii) Use of glass shall be reduced up to 40% to reduce the electricity consumption and load on air conditioning. If necessary, high quality double glass with special reflecting coating shall be used in windows.

#### 10. Storm Water Drainage:

- i) Storm water management around the site and on site shall be established by following the guidelines laid down by the storm water manual.
- ii) Storm water management plan shall be obtained by engaging the services of Anna University/IIT.

#### 11. Energy Conservation Measures:

- i) Roof should meet prescriptive requirement as per Energy Conservation Building Code by using appropriate thermal insulation material, to fulfill the requirement.
- ii) Opaque wall should meet prescribed requirement as per Energy Conservation Building Code which is mandatory for all air conditioned spaces by use of appropriate thermal insulation material to fulfill the requirement.
- iii) All norms of Energy Conservation Building Code (ECBC) and National Building Code, 2005 as energy conservation have to be adopted Solar lights shall be provided for illumination of common areas.
- iv) Application of solar energy should be incorporated for illumination of common areas, lighting for gardens and street lighting. A hybrids system or fully solar system for a portion of the apartments shall be provided.
- v) A report on the energy conservation measures conforming to energy conservation norms prescribed by the Bureau of Energy Efficiency shall be prepared incorporating details about building materials & technology; R & U factors etc and submitted to the SEIAA in three month's time.
- vi) Energy conservation measures like installation of CFLs/TFLs for lighting the areas outside the building should be integral part of the project design and should be in place before project commissioning.

#### 12. Fire Safety:



*T. Jayaraj*  
MEMBER SECRETARY  
SEIAA-TN



- i) Adequate fire protection equipments and rescue arrangements should be made as per the prescribed standards.
- ii) Proper and free approach road for fire-fighting vehicles upto the buildings and for rescue operations in the event of emergency shall be made.

### 13. Green Belt Development:

- i) The Project Proponent shall plant tree species with large potential for carbon capture in the proposed green belt area based on the recommendation of the Forest department well before the project is completed.
- ii) The purpose of Green belt around the project is to capture the fugitive emissions and to attenuate the noise generated, in addition to the improvement in the aesthetics. A wide range of indigenous plants species should be planted in and around the premise in consultation with the DFO, Viluppuram District / State Agriculture University. The plants species should have thick canopy cover, perennial green nature, native origin and large leaf areas. Medium size trees and small trees alternating with shrubs shall be planted. If possible Miyawaki method of planting i.e planting different types of trees at very close escapement may be tried which will give a good green cover. A total of 15% of the plot area should be designated for green belt which should be raised along the boundaries of the plot and in between blocks in an organized manner
- iii) The proponent shall develop the green belt as per the plan furnished and area earmarked for the greenbelt shall not be alter at any point of time for any other purpose.
- iv) The proponent has to earmark the greenbelt area with dimension and GPS coordinates for the green belt area and the same shall be included in the layout out plan to be submitted for DTCP approval

### 14. Sewage Treatment Plant:



*Tanjan*  
MEMBER SECRETARY  
SEIAA-TN

- i) The Sewage Treatment Plant (STP) installed should be certified by an independent expert/ reputed Academic institutions for its adequacy and a report in this regard should be submitted to the SEIAA, TN before the project is commissioned for operation. Explore the less power consuming systems viz baffle reactor, etc., for the treatment of sewage.
- ii) The Proponent shall install STP as furnished. Any alteration to satisfy the bathing quality shall be informed to SEIAA-TN.
- iii) The project proponent shall operate and maintain the Sewage treatment Plant effectively to meet out the standards prescribed by the CPCB.
- iv) The project proponent shall continuously operate and maintain the Sewage treatment plant to achieve the standards prescribed by the CPCB.
- v) The project proponent has to ensure the complete recycling of treated sewage after achieving the standards prescribed by the CPCB.
- vi) The project proponent has to provide separate standby D.G set for the STP for the continuous operation of the STP in case of power failure.

**15. Rain Water Harvesting:**

- i) The proponent/ Owner of the Flats shall ensure that roof rain water collected from the covered roof of the buildings, etc shall be harvested so as to ensure the maximum beneficiation of rain water harvesting by constructing adequate sumps so that 100% of the harvested water shall be reused.
- ii) Rain water harvesting for surface run-off, as per plan submitted should be implemented. Before recharging the surface run off, pre-treatment with screens, settlers etc. must be done to remove suspended matter, oil and grease, etc.
- iii) The project activity should not cause any disturbance & deterioration of the local bio diversity.

**16. Building Safety:**

Lightning arrester shall be properly designed and installed at top of the building and where ever necessary.



*Jayanti*  
MEMBER SECRETARY  
SEIAA-TN

**Part – D - Specific Conditions – Operational Phase/Post constructional phase/Entire life of the project:**

1. There should be Fire fighting plan and all required safety plan.
2. Regular fire drills should be held to create awareness among owners/ residents.
3. House hold hazardous waste such as batteries, small electronics, CFL bulbs, expired medicines and used cleaning solvent bottles should be segregated at source, collected once in a month from residences and disposed as per the SWM rules 2016.
4. The building should not spoil the green views and acsthetics of surroundings and should provide enough clean air space.
5. The project proponent has to furnish the certificate stating that the proposed site had not encroached any water body (rivers, canals, lakes, ponds, tanks, etc) from its original boundary shall be obtained from the competent authority before obtaining CTE from TNPCB.
6. The project proponent shall obtain the necessary permission for drawl of ground water / surface water required for the project from the competent authority.
7. Solar energy saving shall be increased to atleast 10% of total energy utilization.
8. The project proponent shall comply with the provisions contained in this Ministry's OM vide F.No. 22-65/2017-IA.III dated 1st May 2018, as applicable, regarding Corporate Environment Responsibility.
9. The company shall have a well laid down environmental policy duly approved by the Board of Directors. The environmental policy should prescribe for standard operating procedures to have proper checks and balances and to bring into focus any infringements/deviation/violation of the environmental / forest / wildlife norms / conditions. The company shall have defined system of reporting infringements / deviation / violation of the environmental / forest / wildlife norms / conditions and / or shareholders / stake holders. The copy of the board resolution in this regard shall be submitted to the MoEF & CC as a part of six-monthly report.



*Jayanti*  
MEMBER SECRETARY  
SEIAA-TN

10. The EMP cost shall be printed in the Brochure / Pamphlet for the preparation of the sale of the property and should also mention the component involved.
11. The Project proponent shall get due permission from the wetland Authority before the commencement of the work, if applicable.
12. The project activities should in no way disturb the manmade structures.
13. The Proponent shall do afforestation/ restoration programme contemplated to strengthen the open spaces shall preferably include native species along with the financial forecast for planting and maintenance for 5 years.
14. "Consent to Operate" should be obtained from the Tamil Nadu pollution Control Board before the start of the operation of the project and copy shall be submitted to the SEIAA-TN.
15. Raw water quality to be checked for portability and if necessary RO plant shall be provided.
16. The Proponent should be responsible for the maintenance of common facilities including greening, rain water harvesting, sewage treatment and disposal, solid waste disposal and environmental monitoring including terrace gardening for a period of 3 years. Within one year after handing over the flats to all allottees a viable society or an association among the allottees shall be formed to take responsibility of continuous maintenance of all facilities with required agreements for compliance of all conditions furnished in Environment Clearance (EC) order issued by the SEIAA-TN or the Proponent himself shall maintain all the above facilities for the entire period. The copy of MOU between the buyers Association and proponent shall be communicated to SEIAA-TN.
17. The ground water level and its quality should be monitored and recorded regularly in consultation with Ground Water Authority.
18. Treated effluent emanating from STP shall be recycled / reused to the maximum extent possible. The treated sewage shall conform to the norms and standards for bathing quality laid down by CPCB irrespective of any use. Necessary measures should be made to mitigate the odour and mosquito problem from STP.



*Jayanti*  
MEMBER SECRETARY  
SEIAA-TN



19. The Proponent shall operate STP continuously by providing stand by DG set in case of power failure.
20. Adequate measures should be taken to prevent odour emanating from solid waste processing plant and STP.
21. The E - waste generated should be collected and disposed to a nearby authorized e-waste centre as per E- waste (Management & Handling), Rules 2016 as amended.
22. Diesel power generating sets proposed as source of back-up power during operation phase should be of enclosed type and conform to rules made under the Environment (Protection) Act, 1986. The height of stack of DG sets should be equal to the height needed for the combined capacity of all proposed DG sets.
23. The noise level shall be maintained as per MoEF/CPCB/TNPCB guidelines/norms both during day and night time.
24. Spent oil from D.G sets should be stored in HDPE drums in an isolated covered facility and disposed as per the Hazardous & other Wastes (Management & Transboundary Movement) Rules 2016. Spent oil from D.G sets should be disposed off through registered recyclers.
25. The proponent is required to provide a house hold hazardous waste / E-waste collection and disposal mechanism.
26. The proponent/ Owner of the Flats shall ensure that storm water drain provided at the project site shall be maintained without choking or without causing stagnation and should also ensure that the storm water shall be properly disposed off in the natural drainage / channels without disrupting the adjacent public. Adequate harvesting of the storm water should also be ensured.
27. Used CFLs and TFLs should be properly collected and disposed off/sent for recycling as per the prevailing guidelines/rules of the regulatory authority to avoid mercury contamination.
28. A copy of the Environmental clearance (EC) letter shall be made available to all the allottees along with the allotment order / sale deed.



*Jayan*  
MEMBER SECRETARY  
SEIAA-TN

29. Failure to comply with any of the conditions mentioned above may result in withdrawal of this clearance and attract action under the provisions of the Environment (Protection) Act, 1986.

  
MEMBER SECRETARY  
SEIAA-TN

**Copy to:**

1. The Principal Secretary to Government, Environment & Forests Dept,  
Govt. of Tamil Nadu, Fort St. George, Chennai - 9.
2. The Chairman, Central Pollution Control Board, Parivesh Bhavan,  
CBD Cum-Office Complex, East Arjun Nagar, New Delhi 110032.
3. The Member Secretary, Tamil Nadu Pollution Control Board,  
76, Mount Salai, Guindy, Chennai-600 032.
4. The APCCF (C), Regional Office, Ministry of Environment & Forest (SZ),  
34, HEPC Building, 1<sup>st</sup>& 2<sup>nd</sup> Floor, Cathedral Garden Road, Nungambakkam,  
Chennai - 34.
5. Monitoring Cell, I A Division, Ministry of Environment & Forests,  
Paryavaran Bhavan, CGO Complex, New Delhi 110003.
6. The District Collector, Viluppuram District
7. Stock File.



**TAMILNADU POLLUTION CONTROL BOARD**

Category of the Industry :

**RED****CONSENT ORDER NO. 2101231962104****DATED: 16/03/2021.****PROCEEDINGS NO.T2/TNPCB/F.1357VPM/RL/VPM/A/2021 DATED: 16/03/2021**

**SUB:** TNPC Board-Consent for Establishment-M/s. SIPCOT INDUSTRIAL PARK AT THINDIVANAM, S.F. No. 181pt, 182, 183, 184, 194, 195, 196, 197, 198, 199, 200, 201, 202, 203, 204, 205, 206, 207, 208, 209, 210, 212, 213pt, 214, 237, 244, 245 & 246pt of Kollar Village, 46pt, 47pt, 48pt, 50pt, 51, 52pt, 53pt, 55pt of Venmaniyathoor Village and 1, 2, 3, 4, 5, 6, 10pt, 13pt, 14, 15, 16, 17, 18, 19, 20, 21pt, 22/1, 2, 32, 33, 34, 35, 36, 37, 38pt, 39, 40, 41, 42, 43/1pt, 2, 45, 46, 47, 48/1, 49, 50, 51, 52, 53, 54, 55, 56, 57, 60, 61/1, 2, 3pt, 62, 63, 64, 118, 120, 121, 123, 125, 126, 129 of Pelakuppam Village, PELAKUPPAM village, Tindivanam Taluk and Villupuram District - for the establishment or take steps to establish the industry under Section 21 of the Air(Prevention and control of Pollution)Act,1981, as amended in 1987(Central Act. 14 of 1981)-Issued -Reg.

**REF:** 1. Unit's application for CTE – New on 19.06.2020/ 27-02-2021  
 2. IR.No : F.1357VPM/RL/AE/VPM/2020 dated 18/12/2020  
 3. Minutes of TSC Resolution No. 185-3 Dated 20.01.2021  
 4. Minutes of TSC Resolution No. 186-13 Dated 10.03.2021

Consent to establish or take steps to establish is hereby granted under Section 21 of the Air (Prevention and control of Pollution) Act,1981, as amended in 1987 and the Rules and Orders made there under to

The Managing Director,

M/s . SIPCOT INDUSTRIAL PARK AT THINDIVANAM

S.F No.181pt, 182, 183, 184, 194, 195, 196, 197, 198, 199, 200, 201, 202, 203, 204, 205, 206, 207, 208, 209, 210, 212, 213pt, 214, 237, 244, 245 & 246pt of Kollar Village, 46pt, 47pt, 48pt, 50pt, 51, 52pt, 53pt, 55pt of Venmaniyathoor Village and 1, 2, 3, 4, 5, 6, 10pt, 13pt, 14, 15, 16, 17, 18, 19, 20, 21pt, 22/1, 2, 32, 33, 34, 35, 36, 37, 38pt, 39, 40, 41, 42, 43/1pt, 2, 45, 46, 47, 48/1, 49, 50, 51, 52, 53, 54, 55, 56, 57, 60, 61/1, 2, 3pt, 62, 63, 64, 118, 120, 121, 123, 125, 126, 129 of Pelakuppam Village, PELAKUPPAM Village, Tindivanam Taluk, Villupuram District.

Authorizing occupier to establish or take steps to establish the industry in the site mentioned below:

S.F No. 181pt, 182, 183, 184, 194, 195, 196, 197, 198, 199, 200, 201, 202, 203, 204, 205, 206, 207, 208, 209, 210, 212, 213pt, 214, 237, 244, 245 & 246pt of Kollar Village, 46pt, 47pt, 48pt, 50pt, 51, 52pt, 53pt, 55pt of Venmaniyathoor Village and 1, 2, 3, 4, 5, 6, 10pt, 13pt, 14, 15, 16, 17, 18, 19, 20, 21pt, 22/1, 2, 32, 33, 34, 35, 36, 37, 38pt, 39, 40, 41, 42, 43/1pt, 2, 45, 46, 47, 48/1, 49, 50, 51, 52, 53, 54, 55, 56, 57, 60, 61/1, 2, 3pt, 62, 63, 64, 118, 120, 121, 123, 125, 126, 129 of Pelakuppam Village, PELAKUPPAM Village, Tindivanam Taluk, Villupuram District.

This Consent to establish is valid upto **March 31, 2026**, or till the industry obtains consent to operate under Section 21 of the Air (Prevention and control of Pollution) Act, 1981, as amended in 1987 whichever is earlier subject to special and general conditions enclosed.





## TAMILNADU POLLUTION CONTROL BOARD


G. Gopalakrishnan

For Member Secretary,  
Tamil Nadu Pollution Control Board,  
Chennai

To  
The Managing Director,  
M/s.SIPCOT INDUSTRIAL PARK AT THINDIVANAM,  
State Industries Promotion Corporation of Tamilnadu Limited (SIPCOT),  
No.19-A, Rukmani Lakshmipathy Road,  
Egmore, Chennai.,  
Pin: 600008

**Copy to:**

- 1.The Commissioner, MYLAM-Panchayat Union, Tindivanam Taluk, Villupuram District .
2. The District Environmental Engineer, Tamil Nadu Pollution Control Board, VILLUPURAM.
3. The JCEE-Monitoring, Tamil Nadu Pollution Control Board, Vellore.
4. File

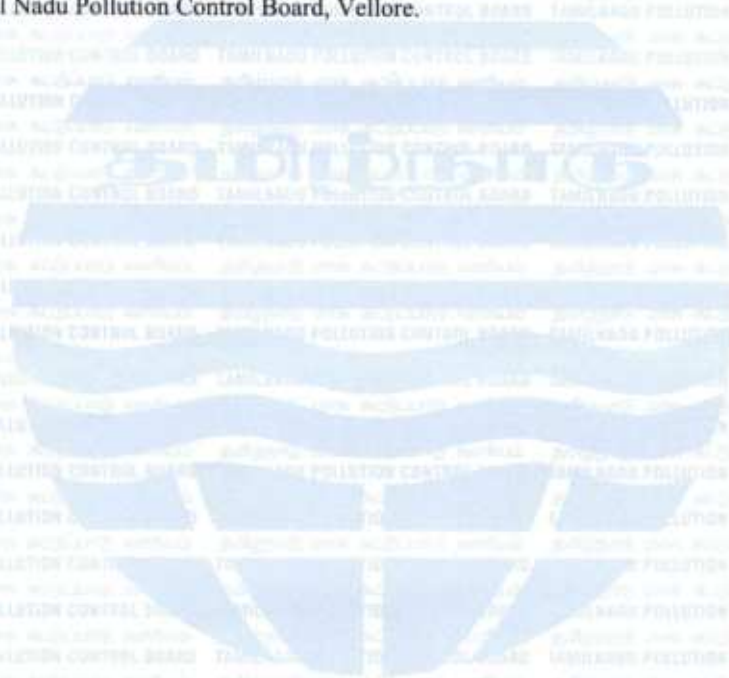





1. This consent to establish is valid for establishing the facility for the manufacture of products/byproducts (Col. 2) at the rate (Col 3) mentioned below. Any change in the product/byproduct and its quantity has to be brought to the notice of the Board and fresh consent has to be obtained.

2. This consent to establish is valid for establishing the facility with the below mentioned emission/noise sources along with the control measures and/or stack. Any change in the emission source/control measures/change in stack height has to be brought to the notice of the Board and fresh consent has to be obtained if necessary.

3. **Special Additional Conditions:**

4. **Additional Conditions:**

1. The unit shall comply with the conditions as stipulated in the Environmental Clearance obtained from SEIAA, TN vide Lr.No.SEIAA-TN/F.6497/EC/8(b)/681/2019 Dated 27.11.2019.
2. The unit shall ensure that no process emission is let out from its activity.
3. The unit shall conduct Ambient Noise level survey report and Ambient Air Quality survey report for base line data to assess the quality of Ambient Air and Ambient Noise level and submit the report within one month's time.
4. The unit shall install Continuous Ambient Air Quality Monitoring System (CAAQMS) stations in the downwind and upwind directions and shall connect the same to CAC, TNPCB, Chennai.
5. The unit shall provide odour control mechanism individually or through the member units for the containment of odour emitting from the industries.
6. The unit shall remit consent fee in case of revision by the Government.

**For Member Secretary,  
Tamil Nadu Pollution Control Board,  
Chennai**





## TAMILNADU POLLUTION CONTROL BOARD

### GENERAL CONDITIONS

1. This consent to establish cannot be construed as consent to operate and the unit shall not commence the operation without obtaining the Consent to operate.
2. The applicant shall make a request for grant of consent to operate at least thirty days, before the commissioning of trial production.
3. Any Change in the details furnished in the conditions has to be brought to the notice of the Board and got approved by the Board, before obtaining consent to operate under the said Act.
4. The unit has to comply with the provisions of Public Liability Insurance Act, 1991 to provide immediate relief in the event of any hazard to human beings, other living creatures/plants and properties while handling and storage of hazardous substances (wherever applicable).
5. Consent to operate will not be issued unless the unit complies with the conditions of consent to establish.
6. The unit shall provide adequate water sprinklers for the control of dust emission during the loading and unloading of construction material so as to minimize the dust emission.
7. The unit shall provide water sprinklers along the temporary roads inside the premises to avoid fugitive dust emission during the vehicle movements.
8. The unit shall develop green belt of adequate width around the premises.
9. In case there is any change in the management, the unit shall inform the change with relevant documents immediately.

G. Gopalakrishnan

For Member Secretary,  
Tamil Nadu Pollution Control Board,  
Chennai





19 MAR 2021

**RED**

**DATED: 16/03/2021**

1





## TAMILNADU POLLUTION CONTROL BOARD

Pin: 600008

### Copy to:

1. The Commissioner, MYLAM-Panchayat Union, Tindivanam Taluk, Villupuram District .
2. The District Environmental Engineer, Tamil Nadu Pollution Control Board, VILLUPURAM.
3. The JCEE-Monitoring, Tamil Nadu Pollution Control Board, Vellore.
4. File







## TAMILNADU POLLUTION CONTROL BOARD

### SPECIAL CONDITIONS

- This consent to establish is valid for establishing the facility for the manufacture of products/byproducts (Col. 2) at the rate (Col 3) mentioned below. Any change in the product/byproduct and its quantity has to be brought to the notice of the Board and fresh consent has to be obtained.

Sl. No.	Description	Quantity	Unit
<b>Product Details</b>			
1.	SIPCOT Industrial Park at Thindivanam is an infrastructure development project which involves development of Industrial plots, development of roads, water supply, storm water drainage, street lights, green belt development and such other amenities.	291.60.5	Hectares

- The unit shall provide Sewage Treatment Plant and /or Effluent Treatment Plant as indicated below.

<b>a Sewage Treatment Plant:</b>			
Treatment status: Septic Tank and SP/DT			
SL. No.	Name of the Treatment Unit	No. of Units	Dimensions in metres
1.	Septic tank	1	4.2 x 2.3 x 1.9
2.	Soak pit	1	1.0 m dia x 2.5 m Ht
<b>b Effluent Treatment Plant:</b>			
Treatment status: No trade effluent and hence does not arise			
SL. No.	Name of the Treatment Unit	No. of Units	Dimensions in metres
1.			

- This consent to establish is valid for establishing the facility with the below mentioned outlets for the discharge of sewage/trade effluent. Any change in the outlets and the quantity has to be brought to the notice of the Board and fresh consent has to be obtained.

Outlet No.	Description of Outlet	Maximum daily discharge in KLD	Point of disposal
<b>Effluent Type : Sewage</b>			
1.	Sewage	0.13	On Industrys own land
<b>Effluent Type : Trade Effluent</b>			

- Additional Conditions:**





## TAMILNADU POLLUTION CONTROL BOARD

1. The unit shall comply with the conditions as stipulated in the Environmental Clearance obtained from SEIAA, TN vide Lr.No.SEIAA-TN/F.6497/EC/8(b)/681/2019 Dated 27.11.2019.
2. The issue of CTE to the project shall not be construed as CTO and shall not commission the project without obtaining CTO from the Board.
3. The unit shall start its establishment activities only after getting the necessary project/building approvals from the competent authorities.
4. This consent order does not absolve from obtaining necessary permission / Clearance from other Authority or under other statutes as applicable.
5. The stability of the entire building/ STP does not falls under the purview of the TNPC Board.
6. The unit shall submit baseline data for ground water to assess the quality of ground water for 1 KM radius outside the boundary of the project and also inside available open wells within a month's time.
7. The unit shall monitor the ground water in and around the unit premises periodically, so as to assess its quality and submit the same to the Board.
8. The unit has to ensure that all the member Industries within the industrial Park shall make their own arrangements to achieve zero discharge of the trade effluents, solid waste & E waste management, gaseous emission and noise control measures to achieve the standards prescribed by the TNPCB.
9. The unit shall obtain the necessary permission / NOC of water supply from the TWAD Board / competent Authority.
10. The unit shall provide septic tank followed by soak pit to treat the sewage generated from SIPCOT administrative building, so as to achieve the standards prescribed by the Board.
11. The SIPCOT shall obtain NOC from competent authority for the withdrawal of 1 MLD of water from 50 Nos of open wells in its premises.
12. The unit shall ensure that the allotted industrial units obtain consent from the TNPCB separately for their establishment & operation in this industrial estate.
13. Compensation is to be paid for land acquisition as fixed by the District Collector and District Magistrate as civil liability.
14. The SIPCOT shall ensure that the allotted units are mandated to implement own sewage treatment system for treating and disposing the sewage and shall ensure that no treated / untreated sewage shall gain access outside the unit premises on land / water source under any circumstances.
15. The SIPCOT shall ensure that the allotted units not dig any well or bore well inside their premises for drawing of ground water.
16. The SIPCOT shall ensure that the allotted units are mandated that the water courses/pathai leading to the Water bodies located in the surroundings will not be disturbed and in this regard a condition shall be imposed in the allotment order to the member units.
17. The SIPCOT shall ensure that the allotted units are mandated that all the member industries to develop green belt in 35% of their allotted area.
18. The proponent shall provide Rain Water Harvesting pits so as to recharge the ground water table.
19. The unit shall allot 5% (10 Hectare) of the total plot area (180.65 Hectare) for Solid Waste Management as reported in the unit's letter dated 26.02.2021.
20. The bio degradable solid waste, non bio degradable solid waste, STP sludge, etc generated from the project activity shall be properly collected, segregated and disposed as per the provision of Solid waste(Management and Handling) Rules,2016.
21. The project generating more than 20 tons of construction and demolition waste or more in one day or 300 tons per project in a month shall segregate the waste into four streams such as concrete, soil, steel, wood and plastics, bricks and mortar and keep the construction and demolition waste within the premise or get the waste deposited at collection centre so made by the local body or handover it to the authorised processing facilities of construction and demolition waste and ensure that there is no littering or deposition of construction and demolition waste so as to prevent obstruction to the traffic or the public or drains.
22. The plastic wastes shall be segregated and disposed as per the provisions of Plastic Waste (Management and Handling) Rules, 2016.
23. The unit shall remit consent fee in case of revision by the Government.

**G. Gopalakrishnan**

**For Member Secretary,  
Tamil Nadu Pollution Control Board,  
Chennai**

Digitally signed by G. Gopalakrishnan  
DN: cn=G. Gopalakrishnan, o=Tamil Nadu Pollution Control Board, ou=Engineering Department,  
email=gopalakrishnan@tnpcb.gov.in, c=IN  
Date: 2023.03.16 16:10:10 +05'30'





## TAMILNADU POLLUTION CONTROL BOARD

### GENERAL CONDITIONS

1. This consent to establish cannot be construed as consent to operate and the unit shall not commence the operation without obtaining the Consent to operate.
2. The applicant shall make a request for grant of consent to operate at least thirty days, before the commissioning of trial production.
3. Any Change in the details furnished in the conditions has to be brought to the notice of the Board and got approved by the Board, before obtaining consent to operate under the said Act.
4. The unit has to comply with the provisions of Public Liability Insurance Act, 1991 to provide immediate relief in the event of any hazard to human beings, other living creatures/plants and properties while handling and storage of hazardous substances (wherever applicable).
5. Consent to operate will not be issued unless the unit complies with the conditions of consent to establish.
6. The unit shall provide adequate water sprinklers for the control of dust emission during the loading and unloading of construction material so as to minimize the dust emission.
7. The unit shall provide water sprinklers along the temporary roads inside the premises to avoid fugitive dust emission during the vehicle movements.
8. The unit shall develop green belt of adequate width around the premises.
9. In case there is any change in the management, the unit shall inform the change with relevant documents immediately.

**G. Gopalakrishnan**

**For Member Secretary,  
Tamil Nadu Pollution Control Board,  
Chennai**

Digitally signed by G. Gopalakrishnan  
DN: cn=G. Gopalakrishnan, o=Tamil Nadu Pollution Control Board, email=gopalakrishnan@tnpcb.gov.in, c=IN  
c=IN, o=Tamil Nadu Pollution Control Board, email=gopalakrishnan@tnpcb.gov.in, c=IN  
c=IN, o=Tamil Nadu Pollution Control Board, email=gopalakrishnan@tnpcb.gov.in, c=IN

## TAMIL NADU WATER SUPPLY AND DRAINAGE BOARD

31, Kamarajar Salai, Chepauk, Chennai-600 005.

Dr.C.N.Mahesvaran,I.A.S.,  
Managing Director.Lr.No.F. 280518/ AE1/PDC/2018-2/Dt.02.09.2020To  
The Managing Director,  
SIPCOT Ltd,  
19-A, Rukmani Lakshmiipatty Road,  
Egmore, Chennai-8.

Sir,

Sub: Setting up Of 60 Mld Capacity Desalination Plant at Koonimedu near Marakanam in Villupuram District and Conveyance of Product Water to Villupuram and Tindivanam Municipalities, Vicravandi, Marakanam Town panchayats and 692 rural habitations in Marakanam, Kanai, Mailam, Vicravandi and Vanur unions in Villupuram Dt - 3 Mld water supply requested to SIPCOT, Tindivanam - Proportionate cost to be borne by SIPCOT - remittance of proportionate project cost - requested - reg.

Ref: 1. Chief Engineer, SIPCOT, Chennai Lr.No. CW/TIP/External Water Supply/2018/Dt.03.01.2019 addressed to CE, TWAD, Vellore.  
2. EE, TWAD, RWS, Kallakurichi Lr.No. F.DSP-CWSS-1/DO/RWS/KKI/2020/Dt.8.8.2020 addressed to Project officer, SIPCOT, Cuddalore

With reference to the letter 1<sup>st</sup> cited, it is pertinent to inform the following.

- ✓ TWAD Board is proposed to install 60 mld capacity Desalination Plant at Koonimedu near Marakanam in Villupuram District for providing water supply to Villupuram and Tindivanam Municipalities, Vicravandi, Marakanam Town panchayats and 692 rural habitations in Marakanam, Kanai, Mailam, Vicravandi and Vanur unions in Villupuram Dt.
- ✓ Originally, the Detailed project report was prepared with Schedule of rates for the year 2019-20 for Rs.1450 Crore (Plant cost - Rs.615 crore & Conveyance cost - Rs.835 Crore) to install and Rs.100.27 Crore to maintain Annually (Plant - Rs.80.81 Crore & Conveyance - Rs.19.46 Crore).
- ✓ Now, the DPR has been revised with the provision for revision with Schedule of rates for the year 2020-21 for Rs.1556.00 Crore (Plant cost - Rs.665.00 crore & Conveyance cost - Rs.891.00 Crore).
- ✓ Administrative approval and fund tie up for this project is being processed by Govt intently.



- ✓ Under this Scheme, provision has been made to provide 3 MLD (30.00 LL) of water supply to SIPCOT, Tindivanam based on the request made vide reference 1<sup>st</sup> cited.
- ✓ It is proposed to supply 3.00 MLD of water to SIPCOT, Tindivanam by pumping through 25.83 Km length of Pumping main (500 mm to 300 mm DI K7 pipe) from the proposed Endur booster station (Transmission Main 2) located at 30.19 Km from Desalination Plant location site. The Flow diagram of the project is appended herewith.
- ✓ The proportionate Project cost towards supply of 3 mld to SIPCOT, Tindivanam is Rs.65.18 Crore
- ✓ Fund tie up for the project is sought for from Govt excluding the proportionate cost of Rs.65.18 Crore towards supply of 3 mld to SIPCOT, Tindivanam.

In this regard, I request you to


- Remit the proportionate Project Cost of Rs. 65.18 Crore to TWAD on receipt of Administrative sanction for the project from the Govt and enter upon MoU with TWAD.
- Give consent to bear excess project cost if any arises during implementation of the Scheme, on receipt of intimation from TWAD Board.

Encl: Flow Diagram of the Project.

Sd/-02.09.2020  
Managing Director,  
TWAD Board, Chennai-5.

*[Signature]*  
for Managing Director,  
TWAD Board, Chennai-05.  
*M/S*  
*2/9/2020*

OWSS TO VILLUPURAM & TINDIVANAM MUNICIPALITY, 2 TOWN PANCHYATS, 892 RURAL HABITATIONS IN 8 PANCHYAT UNIONS, 5-STAR TINDIVANAM AND MEDICAL COLLEGE & HOSPITAL AT MUNDIKAMPAKKAM BY SETTING UP A DESALINATION PLANT IN KODUMEDU AT VILLUPURAM DISTRICT

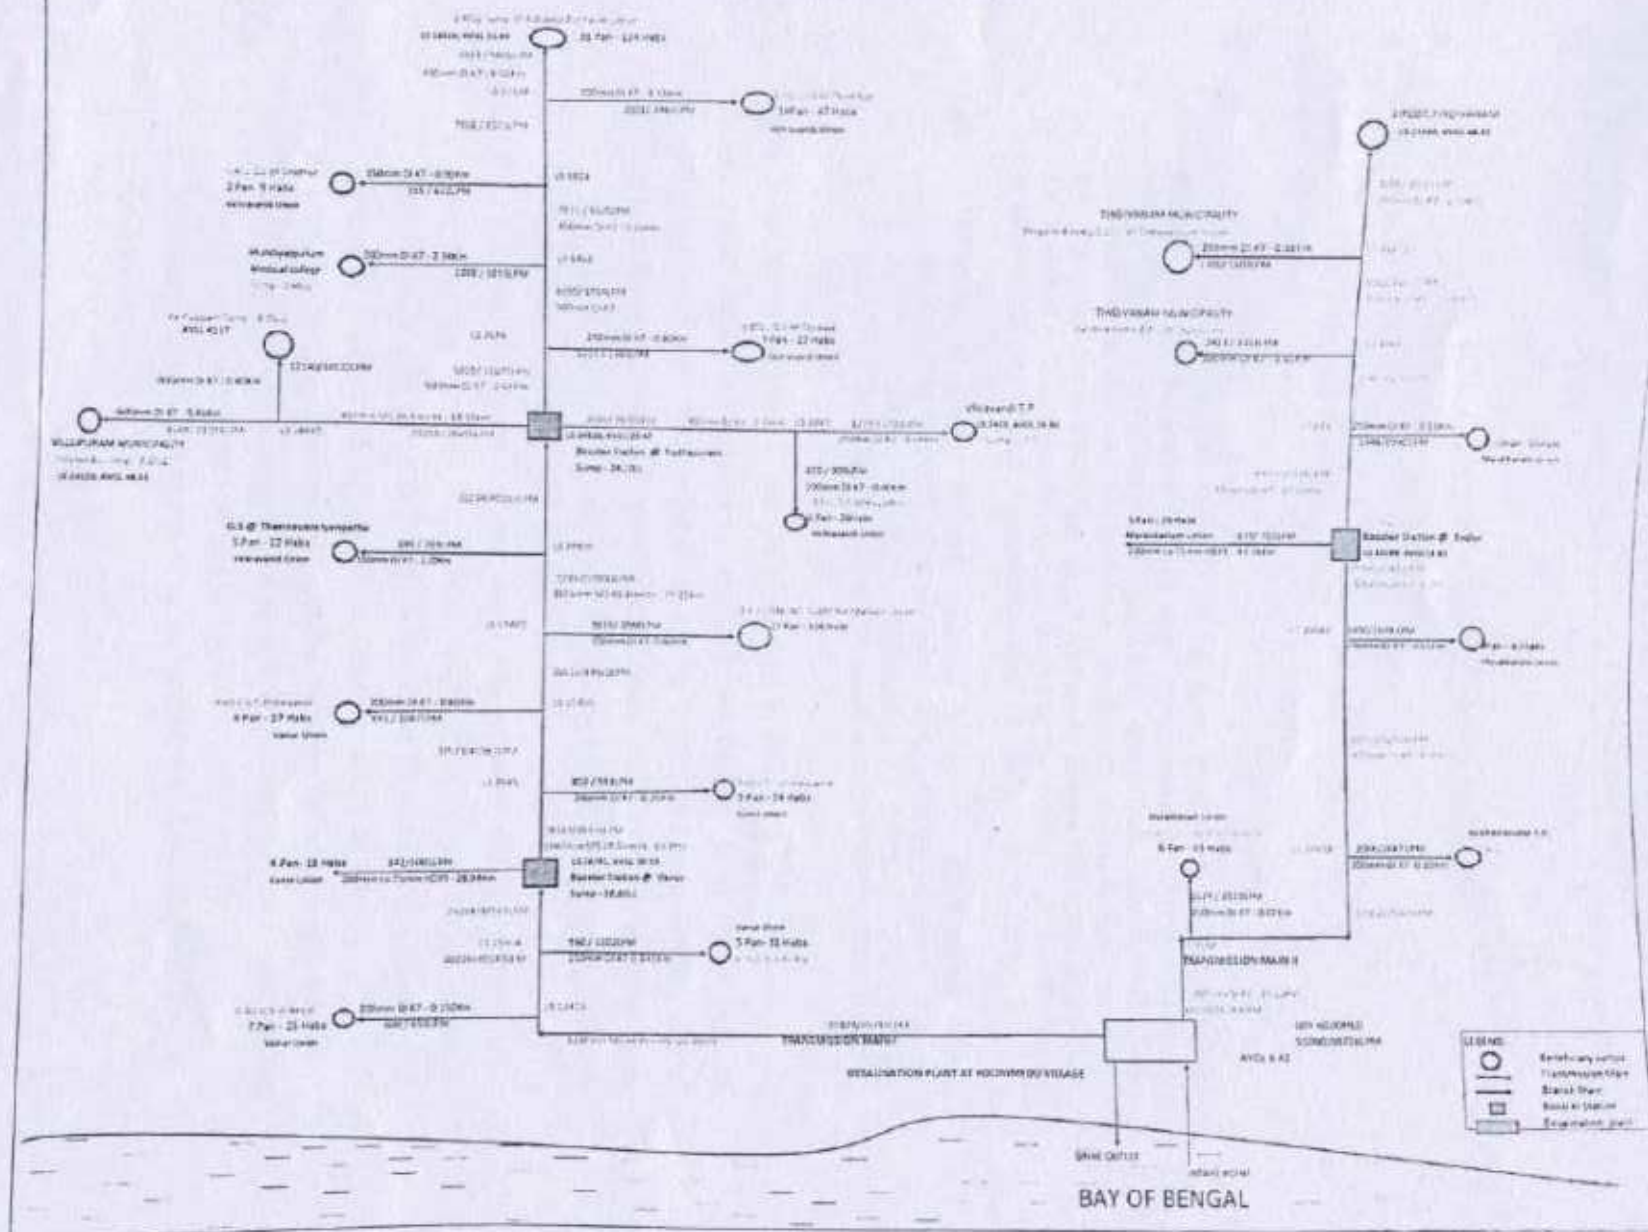

C.A. 11


**TAMILNADU WATER SUPPLY AND DRAINAGE BOARD**

31, Kamarajar Salai, Chempauk, Chennai.5

**Dr.C.N.Mahesvaran., I.A.S.,**

**Managing Director**

Lr No F.280518/ AE1/ PDC/ 2018/ dt. 05.09.2020



To

The Managing Director  
SIPCOT Ltd,  
19-A, Rukmani Lakshmapathy road,  
Egmore, Chennai.

Sir,

Sub: TWAD Board – SIPCOT Industrial park, Tindivanam – 3.00 mld subsurface water supply near SIPCOT Park – finalization of immediate requirement - Online registration and consent requested - reg

Ref: 1. MD, SIPCOT Lr No CW/ TIP/ W.S/2018/ dt14.07.2020.  
2. This office Lr.No. No F.280518/ AE1/ PDC/ 2018/ dt.20.07.2020.  
3. MD, SIPCOT Lr No CW/ IWC /TIP/WS/2020/ dt10.08.2020.

With reference to MD, SIPCOT's request vide reference 1<sup>st</sup> cited to expedite the investigation for supply of 3 mld by sparing from the existing water supply scheme of TWAD Board, MD, SIPCOT was addressed vide reference 2<sup>nd</sup> cited informing that

- ✓ There are no existing WS schemes in Cuddalore and Villupuram Districts from which 3 MLD could be spared to SIPCOT, Tindivanam.
- ✓ Apart from the source identified for supply of 0.5 mld from the **subsurface source nearby park** by constructing 3 or 4 open wells, another 0.50 mld would be possible to tap from the **palakuppam panchayat of Tindivanam taluk** by construction of 3 to 4 open wells for which necessary permission from the Panchayat is to be obtained for industrial supply by SIPCOT.
- ✓ Also, suggested around 30 nos. of open wells from **Veedur dam** assuming yield of 100-110LPM


Now, in the reference 3<sup>rd</sup> cited it has been requested to confirm the feasibility of drawal of 3 mld surface water from Veedur dam.

In this regard, HG, Chennai after carrying out thorough hydrogeological investigation of dam ruled out the Veedur Dam option citing that

- ✓ excavation of open wells outside the Veedur dam is not feasible since there are no spaces
- ✓ it is not possible to excavate wells inside also since the parapet wall of wells to be raised to Dam height of 32 ft to prevent submergence when the reservoir is full.

Further the HG has suggested that an immediate requirement of around 1 MLD is possible for drawal from the existing (50 Nos) of open wells in SIPCOT premises by carrying out suitable rejuvenation works. .

On finalization of immediate requirement by SIPCOT and on completion of online registration , remittance of upfront deposit and furnishing consent for 'ToR' of TWAD Board as already requested vide reference 2<sup>nd</sup> cited , investigation works will be taken up by TWAD.


  
for Managing Director  
TWAD Board - Chennai-5



## **ENVIRONMENTAL MANAGEMENT CELL**

### **1. INTRODUCTION:**

- 1.1. For effective implementation and monitoring of environmental management system, it is necessary to have a permanent organizational set-up as Environmental Management Cell (EMC). This is done by assigning responsibility to the concerned personnel for implementation of environmental control measures.
- 1.2. SIPCOT Environmental Management Cell consist of 7 team members headed by SIPCOT Managing Director, General Manager (Projects), Manager and two Environmental Consultants assisted by two Office Staffs which will enforce and implement the Environmental Plan.
- 1.3. The Organization of Environmental Management Cell (EMC) proposed is given in **Figure - 1**.

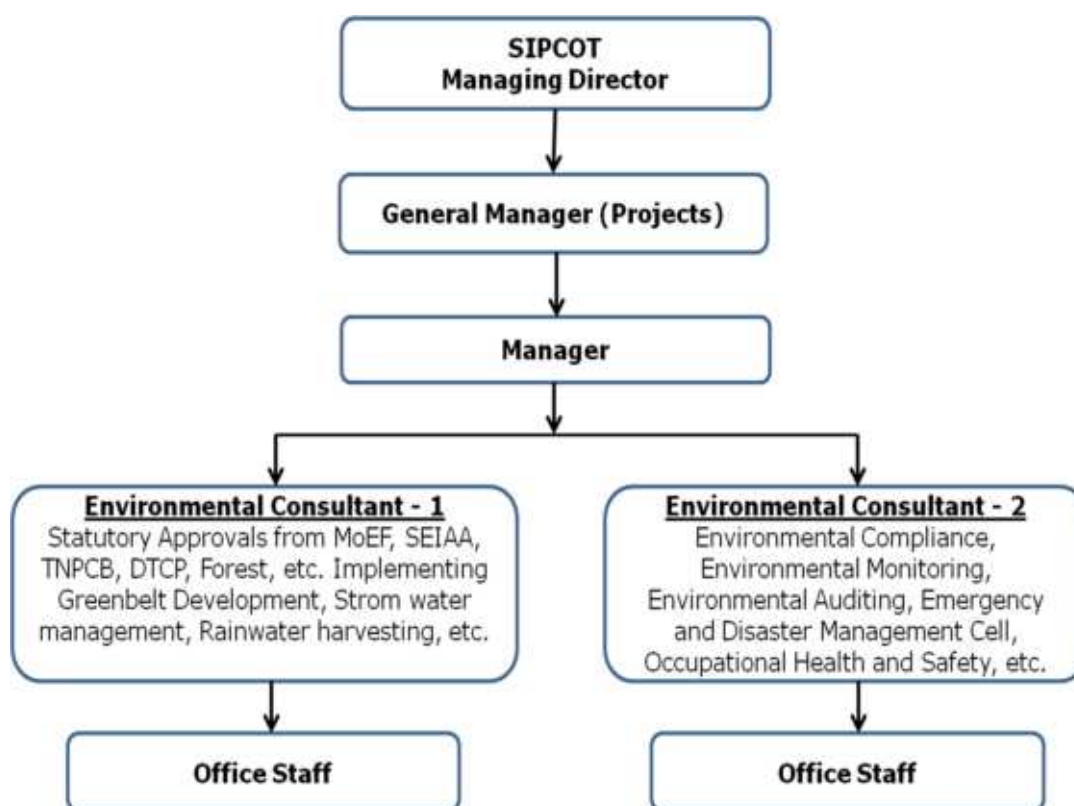

**Figure - 1 Organogram for Environmental Management Cell**

## **2. RESPONSIBILITIES OF ENVIRONMENTAL MANAGEMENT CELL:**

- 2.1. Environmental Management Cell (EMC) shall obtain all applicable statutory clearances and approvals as mandated by the regulatory authorities and maintain the Industrial Parks in compliance with all applicable rules and regulations.
- 2.2. Other responsibilities of the cell will include:
  - a) Review the progress of regulatory compliance of SIPCOT and initiate necessary action for the compliance of the same.
  - b) The EMC will review, implement, update, and comply with the Environment Policy to ensure the effective implementation of environmental safeguard measures.
  - c) Keeping the Board updated on regular basis about the activities carried out under environmental measures and suggests measures to improve environment preservation and protection.
  - d) Encourages allottee units to implement, adopt and use of green and sustainable technologies such as Solar, Wind, Thermal, Biomass, Electric & Hybrid vehicles, etc. to achieve more resource-efficient, clean and resilient growth towards reducing pollution during their process, manufacturing and transportation of goods and encourages energy recovery for self sustainability from their Industrial process.
  - e) Mandate industries to reduce the use of one time use plastics, Styrofoam, and other plastic material during the packing and delivery of goods.

**Table – 1: Roles and responsibilities of EMC**

<b>S.No.</b>	<b>Designation</b>	<b>Responsibilities</b>
1	Managing Director	<ul style="list-style-type: none"> <li>➤ Responsible for overall environmental management.</li> <li>➤ Regularly conduct meeting with EMC and take feedback regarding all the activities performed under Environmental Management and give directions to succeeding component.</li> <li>➤ Approval of funds for carrying out environmental management activities.</li> </ul>
2	GM – Projects	<ul style="list-style-type: none"> <li>➤ Keep aware about all the activities performed under EMC in the industrial parks.</li> <li>➤ Issuing direction to Project officers for implementing Greenbelt development, Storm water management, rain water harvesting, etc.</li> <li>➤ To deal with legal entity pertaining to environmental issues.</li> </ul>
3	Manager	<ul style="list-style-type: none"> <li>➤ To prepare and allocate budget for Environment Management Plan.</li> <li>➤ Ensuring compliance to the conditions prescribed by statutory authority.</li> <li>➤ Mandating member industries to comply with the conditions stipulated in the statutory approvals and non-compliance if any shall be reported to GM and immediately required action will be taken.</li> </ul>
4	Environmental Consultants (Two)	<ul style="list-style-type: none"> <li>➤ Obtaining Statutory Approvals from MoEF&amp;CC / SEIAA / TNPCB, etc.</li> <li>➤ Addressing the various queries received from statutory authorities on environmental front.</li> <li>➤ Submitting Environmental compliance report and coordinating with project officers for Environmental monitoring, audit, etc.</li> <li>➤ Compliance with the environmental laws and implications which dynamically changes from time to time due to the emerging challenges.</li> </ul>



TC-12310

**TEST REPORT**

Page : 1 of 1

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Atmospheric Pollution

Sample Name : Ambient Air

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Project Area

Environmental Condition : Temperature (°C) : 29.8 | Humidity (%) : 53.0

Sampling Method &amp; Plan : IS 5182 Part 5 &amp; Part 14

ULR : TC1231025000016535F

Report No. : HECS/AP/086/240325

Sample ID No : 240325272

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 05/04/2025

Report Date : 05/04/2025

Sample quantity : NA

S.No.	Test Parameters	Units	Results	Test Method	NAAQ Standards : 2009	
Discipline : Chemical						
1	Arsenic	ng/m <sup>3</sup>	BLQ (LOQ: 2.0)	HECS-G/INS/SOP/ 041 Issue No.:01 Issue Date:01.03.2021	6 (Annual)	6 (Annual)
2	Nickel	ng/m <sup>3</sup>	BLQ (LOQ: 2.0)	HECS-G/INS/SOP/ 041 Issue No.:01 Issue Date:01.03.2021	20 (Annual)	20 (Annual)
3	Benzene-AAQ	µg/m <sup>3</sup>	BLQ (LOQ: 0.1)	IS 5182 Part 11: 2006	5 (Annual)	5 (Annual)
4	Benzo (a) pyrene-AAQ	ng/m <sup>3</sup>	BLQ (LOQ: 0.1)	IS : 5182 Part 12: 2004	1 (Annual)	1 (Annual)
5	Ammonia as NH <sub>3</sub>	µg/m <sup>3</sup>	BLQ(LOQ 5)	IS 5182 (Part 25) 2018	400 (24 hours)	100 (Annual)
6	Carbon Monoxide (CO)	mg/ m <sup>3</sup>	BLQ(LOQ 0.05)	IS 5182 (Part 10) Clause 4 1999	4 (1 hours)	2 (8 hours)
7	Nitrogen dioxides as NO <sub>2</sub>	µg/m <sup>3</sup>	15.79	IS 5182 (Part 6) 2006	80 (24 hours)	40 (Annual)
8	Ozone as O <sub>3</sub>	µg/m <sup>3</sup>	BLQ(LOQ 10)	IS 5182 (Part 9) 1974	180 (1 hours)	100 (8 hours)
9	Particulate matter (Size less than 10 µm)	µg/m <sup>3</sup>	80.05	IS 5182 (Part 23) 2006	100 (24 hours)	60 (Annual)
10	Particulate matter (Size less than 2.5 µm)	µg/m <sup>3</sup>	27.82	IS 5182 (Part 24) 2019	60 (24 hours)	40 (Annual)
11	Sulphur dioxide as SO <sub>2</sub>	µg/m <sup>3</sup>	9.21	IS 5182 (Part 2) 2001	80 (24 hours)	50 (Annual)
12	Lead	µg/m <sup>3</sup>	BLQ (LOQ: 0.002)	HECS-G/INS/SOP/ 041 Issue No.:01 Issue Date:01.03.2021	1 (24 hours)	0.5 (Annual)

Note:- BLQ - Below the Limit of Quantification, LOQ- Limit of Quantification, µg/m<sup>3</sup>- Micrograms per cubic meter, mg/m<sup>3</sup>-Milligrams per cubic meter, ng/m<sup>3</sup>-Nanograms per cubic meter.

Remarks: The Tested Parameters as above are within the Limits of NAAQ Standards 2009.

\*\*\*End of Report\*\*\*



D.Anusuya  
Lab Manager  
Authorized Signatory

**Hubert Enviro Care Systems (P) Ltd.**A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax : 42985500

E-mail : labsales@hecs.in

**Laboratory Services Division**

(Chemical &amp; Biological Testing)

Recognized by CPCB (MoEF &amp; CC)

BIS, FSSAI Notified Laboratory

ISO 9001, 14001 &amp; 45001 Certified.

**TEST REPORT**

Page : 1 of 1

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Atmospheric Pollution

Sample Name : Ambient Air

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s.Hubert Enviro care Systems (P) Ltd.

Sample Location : Project Area

Environmental Condition : Temperature (°C) : 29.8 | Humidity (%) : 53.0

Sampling Method &amp; Plan : IS 5182 Part 5 &amp; Part 14

Report No. : HECS/AP/086/240325/N

Sample ID No : 240325272

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 05/04/2025

Report Date : 05/04/2025

Sample quantity : NA

S.No.	Test Parameters	Units	Results	Test Method
Discipline : Chemical				
1	TVOC	ppmv	BLQ(LOQ 0.1)	HECS-G/ENV/AAQ/SOP/005 Issue No.:01 Issue Date:02:07 2020

Note:- BLQ - Below the Limit of Quantification, LOQ- Limit of Quantification, ppmv- Parts per million by Volume.

\*\*\*End of Report\*\*\*

D.Anusuya  
Lab Manager  
Authorized Signatory



# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 1 of 1

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Atmospheric Pollution

Sample Name : Ambient Air

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Botheri

Environmental Condition : Temperature (°C) : 29.8 | Humidity (%) : 53.0

Sampling Method & Plan : IS 5182 Part 5 & Part 14

U/LR : TC1231025000016536F

Report No. : HECS/AP/087/240325

Sample ID No : 240325273

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 05/04/2025

Report Date : 05/04/2025

Sample quantity : NA

S.No.	Test Parameters	Units	Results	Test Method	NAAQ Standards : 2009	
Discipline : Chemical						
1	Arsenic	ng/m <sup>3</sup>	BLQ (LOQ: 2.0)	HECS-G/INS/SOP/ 041 Issue No.:01 Issue Date:01.03.2021	6 (Annual)	6 (Annual)
2	Nickel	ng/m <sup>3</sup>	BLQ (LOQ: 2.0)	HECS-G/INS/SOP/ 041 Issue No.:01 Issue Date:01.03.2021	20 (Annual)	20 (Annual)
3	Benzene-AAQ	µg/m <sup>3</sup>	BLQ (LOQ: 0.1)	IS 5182 Part 11: 2006	5 (Annual)	5 (Annual)
4	Benzo (a) pyrene-AAQ	ng/m <sup>3</sup>	BLQ (LOQ: 0.1)	IS : 5182 Part 12: 2004	1 (Annual)	1 (Annual)
5	Ammonia as NH <sub>3</sub>	µg/m <sup>3</sup>	BLQ(LOQ 5)	IS 5182 (Part 25) 2018	400 (24 hours)	100 (Annual)
6	Carbon Monoxide (CO)	mg/ m <sup>3</sup>	BLQ(LOQ 0.05)	IS 5182 (Part 10) Clause 4 1999	4 (1 hours)	2 (8 hours)
7	Nitrogen dioxides as NO <sub>2</sub>	µg/m <sup>3</sup>	17.07	IS 5182 (Part 6) 2006	80 (24 hours)	40 (Annual)
8	Ozone as O <sub>3</sub>	µg/m <sup>3</sup>	BLQ(LOQ 10)	IS 5182 (Part 9) 1974	180 (1 hours)	100 (8 hours)
9	Particulate matter (Size less than 10 µm)	µg/m <sup>3</sup>	78.11	IS 5182 (Part 23) 2006	100 (24 hours)	60 (Annual)
10	Particulate matter (Size less than 2.5 µm)	µg/m <sup>3</sup>	25.19	IS 5182 (Part 24) 2019	60 (24 hours)	40 (Annual)
11	Sulphur dioxide as SO <sub>2</sub>	µg/m <sup>3</sup>	7.22	IS 5182 (Part 2) 2001	80 (24 hours)	50 (Annual)
12	Lead	µg/m <sup>3</sup>	BLQ (LOQ: 0.002)	HECS-G/INS/SOP/ 041 Issue No.:01 Issue Date:01.03.2021	1 (24 hours)	0.5 (Annual)

Note:- BLQ - Below the Limit of Quantification, LOQ- Limit of Quantification, µg/m<sup>3</sup>- Micrograms per cubic meter, mg/m<sup>3</sup>-Milligrams per cubic meter, ng/m<sup>3</sup>-Nanograms per cubic meter.

Remarks: The Tested Parameters as above are within the Limits of NAAQ Standards 2009.

\*\*\*End of Report\*\*\*



D.Anusuya  
Lab Manager  
Authorized Signatory

**Hubert Enviro Care Systems (P) Ltd.**

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax : 42985500

E-mail : labsales@hecs.in

**Laboratory Services Division**

(Chemical & Biological Testing)

Recognized by CPCB (MoEF & CC)

BIS, FSSAI Notified Laboratory

ISO 9001, 14001 & 45001 Certified.

**TEST REPORT**

Page : 1 of 1

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Atmospheric Pollution

Sample Name : Ambient Air

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s.Hubert Enviro care Systems (P) Ltd.

Sample Location : Botheri

Environmental Condition : Temperature (°C) : 29.8 | Humidity (%) : 53.0

Sampling Method & Plan : IS 5182 Part 5 & Part 14

Report No. : HECS/AP/087/240325/N

Sample ID No : 240325273

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 05/04/2025

Report Date : 05/04/2025

Sample quantity : NA

S.No.	Test Parameters	Units	Results	Test Method
Discipline : Chemical				
1	TVOC	ppmv	BLQ(LOQ 0.1)	HECS-G/ENV/AAQ/SOP/005 Issue No.:01 Issue Date:02:07 2020

Note:- BLQ - Below the Limit of Quantification, LOQ- Limit of Quantification, ppmv- Parts per million by Volume.

\*\*\*End of Report\*\*\*



D.Anusuya

Lab Manager

Authorized Signatory



# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 1 of 1

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Atmospheric Pollution

Sample Name : Ambient Air

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Agoor

Environmental Condition : Temperature (°C) : 29.8 | Humidity (%) : 53.0

Sampling Method & Plan : IS 5182 Part 5 & Part 14

ULR : TC1231025000016537F

Report No. : HECS/AP/088/240325

Sample ID No : 240325274

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 05/04/2025

Report Date : 05/04/2025

Sample quantity : NA

S.No.	Test Parameters	Units	Results	Test Method	NAAQ Standards : 2009	
Discipline : Chemical						
1	Arsenic	ng/m <sup>3</sup>	BLQ (LOQ: 2.0)	HECS-G/INS/SOP/ 041 Issue No.:01 Issue Date:01.03.2021	6 (Annual)	6 (Annual)
2	Nickel	ng/m <sup>3</sup>	BLQ (LOQ: 2.0)	HECS-G/INS/SOP/ 041 Issue No.:01 Issue Date:01.03.2021	20 (Annual)	20 (Annual)
3	Benzene-AAQ	µg/m <sup>3</sup>	BLQ (LOQ: 0.1)	IS 5182 Part 11: 2006	5 (Annual)	5 (Annual)
4	Benzo (a) pyrene-AAQ	ng/m <sup>3</sup>	BLQ (LOQ: 0.1)	IS : 5182 Part 12: 2004	1 (Annual)	1 (Annual)
5	Ammonia as NH3	µg/m <sup>3</sup>	14.58	IS 5182 (Part 25) 2018	400 (24 hours)	100 (Annual)
6	Carbon Monoxide (CO)	mg/ m <sup>3</sup>	BLQ(LOQ 0.05)	IS 5182 (Part 10) Clause 4 1999	4 (1 hours)	2 (8 hours)
7	Nitrogen dioxides as NO2	µg/m <sup>3</sup>	26.31	IS 5182 (Part 6) 2006	80 (24 hours)	40 (Annual)
8	Ozone as O3	µg/m <sup>3</sup>	20.47	IS 5182 (Part 9) 1974	180 (1 hours)	100 (8 hours)
9	Particulate matter (Size less than 10 µm)	µg/m <sup>3</sup>	126.83	IS 5182 (Part 23) 2006	100 (24 hours)	60 (Annual)
10	Particulate matter (Size less than 2.5 µm)	µg/m <sup>3</sup>	31.08	IS 5182 (Part 24) 2019	60 (24 hours)	40 (Annual)
11	Sulphur dioxide as SO2	µg/m <sup>3</sup>	14.64	IS 5182 (Part 2) 2001	80 (24 hours)	50 (Annual)
12	Lead	µg/m <sup>3</sup>	BLQ (LOQ: 0.002)	HECS-G/INS/SOP/ 041 Issue No.:01 Issue Date:01.03.2021	1 (24 hours)	0.5 (Annual)

Note:- BLQ - Below the Limit of Quantification, LOQ- Limit of Quantification, µg/m<sup>3</sup>- Micrograms per cubic meter, mg/m<sup>3</sup>-Milligrams per cubic meter, ng/m<sup>3</sup>-Nanograms per cubic meter.

Remarks: The Tested Parameters as above are within the Limits of NAAQ Standards 2009.

\*\*\*End of Report\*\*\*



D.Anusuya  
Lab Manager  
Authorized Signatory

**Hubert Enviro Care Systems (P) Ltd.**

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax : 42985500

E-mail : labsales@hecs.in

**Laboratory Services Division**

(Chemical &amp; Biological Testing)

Recognized by CPCB (MoEF &amp; CC)

BIS, FSSAI Notified Laboratory

ISO 9001, 14001 &amp; 45001 Certified.

**TEST REPORT**

Page : 1 of 1

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Atmospheric Pollution

Sample Name : Ambient Air

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s.Hubert Enviro care Systems (P) Ltd.

Sample Location : Agoor

Environmental Condition : Temperature (°C) : 29.8 | Humidity (%) : 53.0

Sampling Method &amp; Plan : IS 5182 Part 5 &amp; Part 14

Report No : HECS/AP/088/240325/N

Sample ID No : 240325274

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 05/04/2025

Report Date : 05/04/2025

Sample quantity : NA

S.No.	Test Parameters	Units	Results	Test Method
Discipline : Chemical				
1	TVOC	ppmv	BLQ(LOQ 0.1)	HECS-G/ENV/AAQ/SOP/005 Issue No.:01 Issue Date:02:07 2020

Note:- BLQ - Below the Limit of Quantification, LOQ- Limit of Quantification, ppmv- Parts per million by Volume.

\*\*\*End of Report\*\*\*



D.Anusuya  
Lab Manager  
Authorized Signatory



# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 1 of 1

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Atmospheric Pollution

Sample Name : Ambient Air

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Pelakuppam

Environmental Condition : Temperature (°C) : 29.8 | Humidity (%) : 53.0

Sampling Method & Plan : IS 5182 Part 5 & Part 14

ULR : TC1231025000016538F

Report No. : HECS/AP/089/240325

Sample ID No : 240325275

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 05/04/2025

Report Date : 05/04/2025

Sample quantity : NA

S.No.	Test Parameters	Units	Results	Test Method	NAAQ Standards : 2009	
Discipline : Chemical						
1	Arsenic	ng/m <sup>3</sup>	BLQ (LOQ: 2.0)	HECS-G/INS/SOP/ 041 Issue No.:01 Issue Date:01.03.2021	6 (Annual)	6 (Annual)
2	Nickel	ng/m <sup>3</sup>	BLQ (LOQ: 2.0)	HECS-G/INS/SOP/ 041 Issue No.:01 Issue Date:01.03.2021	20 (Annual)	20 (Annual)
3	Benzene-AAQ	µg/m <sup>3</sup>	BLQ (LOQ: 0.1)	IS 5182 Part 11: 2006	5 (Annual)	5 (Annual)
4	Benzo (a) pyrene-AAQ	ng/m <sup>3</sup>	BLQ (LOQ: 0.1)	IS : 5182 Part 12: 2004	1 (Annual)	1 (Annual)
5	Ammonia as NH <sub>3</sub>	µg/m <sup>3</sup>	7.68	IS 5182 (Part 25) 2018	400 (24 hours)	100 (Annual)
6	Carbon Monoxide (CO)	mg/ m <sup>3</sup>	BLQ(LOQ 0.05)	IS 5182 (Part 10) Clause 4 1999	4 (1 hours)	2 (8 hours)
7	Nitrogen dioxides as NO <sub>2</sub>	µg/m <sup>3</sup>	14.64	IS 5182 (Part 6) 2006	80 (24 hours)	40 (Annual)
8	Ozone as O <sub>3</sub>	µg/m <sup>3</sup>	BLQ(LOQ 10)	IS 5182 (Part 9) 1974	180 (1 hours)	100 (8 hours)
9	Particulate matter (Size less than 10 µm)	µg/m <sup>3</sup>	74.19	IS 5182 (Part 23) 2006	100 (24 hours)	60 (Annual)
10	Particulate matter (Size less than 2.5 µm)	µg/m <sup>3</sup>	23.67	IS 5182 (Part 24) 2019	60 (24 hours)	40 (Annual)
11	Sulphur dioxide as SO <sub>2</sub>	µg/m <sup>3</sup>	10.03	IS 5182 (Part 2) 2001	80 (24 hours)	50 (Annual)
12	Lead	µg/m <sup>3</sup>	BLQ (LOQ: 0.002)	HECS-G/INS/SOP/ 041 Issue No.:01 Issue Date:01.03.2021	1 (24 hours)	0.5 (Annual)

Note:- BLQ - Below the Limit of Quantification, LOQ- Limit of Quantification, µg/m<sup>3</sup>- Micrograms per cubic meter, mg/m<sup>3</sup>-Milligrams per cubic meter, ng/m<sup>3</sup>-Nanograms per cubic meter.

Remarks: The Tested Parameters as above are within the Limits of NAAQ Standards 2009.

\*\*\*End of Report\*\*\*



D.Anusuya  
Lab Manager  
Authorized Signatory

**Hubert Enviro Care Systems (P) Ltd.**

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax : 42985500

E-mail : labsales@hecs.in

**Laboratory Services Division**

(Chemical &amp; Biological Testing)

Recognized by CPCB (MoEF &amp; CC)

BIS, FSSAI Notified Laboratory

ISO 9001, 14001 &amp; 45001 Certified.

**TEST REPORT**

Page : 1 of 1

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Atmospheric Pollution

Sample Name : Ambient Air

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s.Hubert Enviro care Systems (P) Ltd.

Sample Location : Pelakuppam

Environmental Condition : Temperature (°C) : 29.8 | Humidity (%) : 53.0

Sampling Method &amp; Plan : IS 5182 Part 5 &amp; Part 14

Report No. : HECS/AP/089/240325/N

Sample ID No : 240325275

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 05/04/2025

Report Date : 05/04/2025

Sample quantity : NA

S.No.	Test Parameters	Units	Results	Test Method
Discipline : Chemical				
1	TVOC	ppmv	BLQ(LOQ 0.1)	HECS-G/ENV/AAQ/SOP/005 Issue No.:01 Issue Date:02:07 2020

Note:- BLQ - Below the Limit of Quantification, LOQ- Limit of Quantification, ppmv- Parts per million by Volume.

\*\*\*End of Report\*\*\*



D.Anusuya  
Lab Manager  
Authorized Signatory



# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 1 of 1

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Atmospheric Pollution

Sample Name : Ambient Air

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Ural

Environmental Condition : Temperature (°C) : 29.8 | Humidity (%) : 53.0

Sampling Method & Plan : IS 5182 Part 5 & Part 14

ULR : TC1231025000016539F

Report No. : HECS/AP/090/240325

Sample ID No : 240325276

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 05/04/2025

Report Date : 05/04/2025

Sample quantity : NA

S.No.	Test Parameters	Units	Results	Test Method	NAAQ Standards : 2009	
Discipline : Chemical						
1	Arsenic	ng/m <sup>3</sup>	BLQ (LOQ: 2.0)	HECS-G/INS/SOP/ 041 Issue No.:01 Issue Date:01.03.2021	6 (Annual)	6 (Annual)
2	Nickel	ng/m <sup>3</sup>	BLQ (LOQ: 2.0)	HECS-G/INS/SOP/ 041 Issue No.:01 Issue Date:01.03.2021	20 (Annual)	20 (Annual)
3	Benzene-AAQ	µg/m <sup>3</sup>	BLQ (LOQ: 0.1)	IS 5182 Part 11: 2006	5 (Annual)	5 (Annual)
4	Benzo (a) pyrene-AAQ	ng/m <sup>3</sup>	BLQ (LOQ: 0.1)	IS : 5182 Part 12: 2004	1 (Annual)	1 (Annual)
5	Ammonia as NH3	µg/m <sup>3</sup>	11.61	IS 5182 (Part 25) 2018	400 (24 hours)	100 (Annual)
6	Carbon Monoxide (CO)	mg/ m <sup>3</sup>	BLQ(LOQ 0.05)	IS 5182 (Part 10) Clause 4 1999	4 (1 hours)	2 (8 hours)
7	Nitrogen dioxides as NO2	µg/m <sup>3</sup>	19.29	IS 5182 (Part 6) 2006	80 (24 hours)	40 (Annual)
8	Ozone as O3	µg/m <sup>3</sup>	16.36	IS 5182 (Part 9) 1974	180 (1 hours)	100 (8 hours)
9	Particulate matter (Size less than 10 µm)	µg/m <sup>3</sup>	106.61	IS 5182 (Part 23) 2006	100 (24 hours)	60 (Annual)
10	Particulate matter (Size less than 2.5 µm)	µg/m <sup>3</sup>	29.35	IS 5182 (Part 24) 2019	60 (24 hours)	40 (Annual)
11	Sulphur dioxide as SO2	µg/m <sup>3</sup>	12.70	IS 5182 (Part 2) 2001	80 (24 hours)	50 (Annual)
12	Lead	µg/m <sup>3</sup>	BLQ (LOQ: 0.002)	HECS-G/INS/SOP/ 041 Issue No.:01 Issue Date:01.03.2021	1 (24 hours)	0.5 (Annual)

Note:- BLQ - Below the Limit of Quantification, LOQ- Limit of Quantification, µg/m<sup>3</sup>- Micrograms per cubic meter, mg/m<sup>3</sup>-Milligrams per cubic meter, ng/m<sup>3</sup>-Nanograms per cubic meter.

Remarks: The Tested Parameters as above are within the Limits of NAAQ Standards 2009.

\*\*\*End of Report\*\*\*



D.Anusuya  
Lab Manager  
Authorized Signatory

**Hubert Enviro Care Systems (P) Ltd.**

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax : 42985500

E-mail : labsales@hecs.in

**Laboratory Services Division**

(Chemical &amp; Biological Testing)

Recognized by CPCB (MoEF &amp; CC)

BIS, FSSAI Notified Laboratory

ISO 9001, 14001 &amp; 45001 Certified.

**TEST REPORT**

Page : 1 of 1

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Atmospheric Pollution

Sample Name : Ambient Air

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Ural

Environmental Condition : Temperature (°C) : 29.8 | Humidity (%) : 53.0

Sampling Method &amp; Plan : IS 5182 Part 5 &amp; Part 14

ULR : TC1231025000016539F

Report No. : HECS/AP/090/240325

Sample ID No : 240325276

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 05/04/2025

Report Date : 05/04/2025

Sample quantity : NA

S.No.	Test Parameters	Units	Results	Test Method
Discipline : Chemical				
I	TVOC	ppmv	BLQ(LOQ 0.1)	HECS-G/ENV/AAQ/SOP/005 Issue No.:01 Issue Date:02:07 2020

Note:- BLQ - Below the Limit of Quantification, LOQ- Limit of Quantification, ppmv- Parts per million by Volume.

\*\*\*End of Report\*\*\*



D.Anusuya  
Lab Manager  
Authorized Signatory

# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 1 of 4

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Water

Sample Name : Ground Water

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Near Agoor

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method & Plan : IS 17614(Part-1):2021

ULR : TC1231025000017011F

Report No. : HECSL/WT/139/240325

Sample ID No : 240325278

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 2 Litres

S.No.	Test Parameters	Units	Results	Test Method	IS 10500 : 2012	
					Acceptable Limits (Max)	Acceptable Limits (Max)
Discipline : Chemical						
1	Bi carbonate	mg/l	463.6	IS 3025 Part 51: 2001	NA	NA
2	Boron as B	mg/l	BLQ(LOQ:0.1)	IS 3025 Part 57 -Curcumin Method: 2021	0.5	2.4
3	Calcium as Ca	mg/l	76.15	IS 3025 Part 40: 1991(EDTA Titrimetric Method)	75	200
4	Carbonate	mg/l	BLQ(LOQ:1.0)	IS 3025 Part 51: 2001	NA	NA
5	Chloride as Cl	mg/l	108.87	IS 3025 Part 32: 1988 ( Argentometric Method)	250	1000
6	Cyanide as CN	mg/l	BLQ(LOQ:0.01)	IS 3025 Part 27 Sec 1: 2021	0.05	No relaxation
7	Electrical Conductivity at 25°C	µS/cm	1042.0	IS 3025 Part-14: 2013	NA	NA
8	Fluoride as F	mg/l	0.37	APHA 23rd edition (Method 4500F-B , D): 2017	1.0	1.5
9	Iron as Fe	mg/l	0.085	IS 3025 (Part 53): 2003	1.0	No relaxation
10	Magnesium as Mg	mg/l	34.02	IS 3025 Part 46: 1994 ( Valumetric Method using EDTA)	30	100
11	Nitrate as NO3	mg/l	2.75	APHA 23rd edition (Method 4500 NO3B): 2017	45	No relaxation
12	Colour	Hazen units	BLQ(LOQ:1.0)	IS 3025 (Part4): 2021	5	15
13	pH at 25°C	-	7.73	IS 3025(Part 11) : 2022 (Electrometric method)	6.5-8.5	No relaxation



D.Anusuya  
Lab Manager  
Authorized Signatory



# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 2 of 4

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Water

Sample Name : Ground Water

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Near Agoor

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method & Plan : IS 17614(Part-1):2021

ULR : TC1231025000017011F

Report No. : HECSL/WT/139/240325

Sample ID No : 240325278

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 2 Litres

S.No.	Test Parameters	Units	Results	Test Method	IS 10500 : 2012	
					Acceptable Limits (Max)	Acceptable Limits (Max)
14	Potassium as K	mg/l	9.0	IS 3025 Part 45: 1993 ( Flame emission Photometric Method)	NA	NA
15	Sodium as Na	mg/l	86.0	IS 3025 Part 45: 1993 ( Flame emission Photometric Method)	NA	NA
16	Sulphate as SO <sub>4</sub>	mg/l	10.9	IS 3025 Part 24 Sec 1: 2022( Turbidity Method)( Turbidity Method)	200	400
17	Total dissolved solids	mg/l	574.0	IS 3025 (Part 16): 1984	500	2000
18	Total Suspended Solids	mg/l	4.0	IS 3025 (Part 17): 1984	NA	NA
19	Phosphorous as P	mg/l	0.420	IS 3025 Part 31 Sec 1: 2022 ( Stannous Chloride method)	NA	NA
20	Total hardness as CaCO <sub>3</sub>	mg/l	330.0	IS 3025 (Part 21): 2009	200	600
21	Turbidity, NTU	NTU	1.7	IS 3025 (Part 10): 1984	1	5
22	Arsenic	mg/l	BLQ (LOQ: 0.005)	USEPA 200.8 : 1994	0.01	No relaxation
23	Cadmium	mg/l	BLQ (LOQ: 0.001)	USEPA 200.8 : 1994	0.003	No relaxation
24	Chromium	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	0.05	No relaxation
25	Copper	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	0.05	1.5



D. Anusuya  
Lab Manager  
Authorized Signatory

# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 3 of 4

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Water

Sample Name : Ground Water

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Near Agoor

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method & Plan : IS 17614(Part-1):2021

ULR : TC1231025000017011F

Report No. : HECSL/WT/139/240325

Sample ID No : 240325278

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 2 Litres

S.No.	Test Parameters	Units	Results	Test Method	IS 10500 : 2012	
					Acceptable Limits (Max)	Acceptable Limits (Max)
26	Lead	mg/l	BLQ (LOQ: 0.005)	USEPA 200.8 : 1994	0.01	No relaxation
27	Mercury	mg/l	BLQ (LOQ: 0.0005)	USEPA 200.8 : 1994	0.001	No relaxation
28	Nickel	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	0.02	No relaxation
29	Zinc	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	5	15
30	Phenolic compounds as C <sub>6</sub> H <sub>5</sub> OH	mg/l	BLQ(LOQ:0.001)	IS 3025 Part 43 Sec 1: 2022	0.001	0.002
31	Anionic Surface Active agents as MBAS	mg/l	BLQ(LOQ:0.05)	APHA 23rd edition (Method 5540 B, C): 2017	0.2	1
32	Percent Sodium	%	35.23	HECS /WT/SOP/002:: 2019	NA	NA
33	Barium	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	0.7	No relaxation
34	Residual Sodium Carbonate	meq/l	BLQ(LOQ:1.0)	IS 11624: 2019	0.2	1.0
35	Ammonia as NH <sub>3</sub>	mg/l	BLQ(LOQ:0.02)	IS 3025 Part 34:Sec 2: 2021 (Nesslerization Method)	0.5	No relaxation
36	Sodium Adsorption Ratio(SAR)	Square root of (millimole/lit)	2.1	IS 11624 : 2019	NA	NA
37	Dissolved oxygen	mg/l	6.6	IS 3025 (Part 38): 1989 ( Titrimetric Method)	NA	NA



D.Anusuya  
Lab Manager  
Authorized Signatory



# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 4 of 4

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Water

Sample Name : Ground Water

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Near Agoor

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method & Plan : IS 17614(Part-1):2021

ULR : TC1231025000017011F

Report No. : HECSL/WT/139/240325

Sample ID No : 240325278

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 2 Litres

S.No.	Test Parameters	Units	Results	Test Method	IS 10500 : 2012	
					Acceptable Limits (Max)	Acceptable Limits (Max)
38	Biological Oxygen Demand (BOD)@ 27°C For 3 days	mg/l	BLQ(LOQ:2.0)	IS 3025 Part 44: 1993	NA	NA
39	Chemical Oxygen Demand (COD)	mg/l	BLQ(LOQ:4.0)	IS 3025 Part 58: 2006	NA	NA
40	Seelenium	mg/l	BLQ (LOQ: 0.005)	USEPA 200.8 : 1994	0.01	No relaxation
41	Manganese	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	0.1	0.3
42	Total alkalinity as CaCO3	mg/l	380.0	IS 3025 (Part 23): 1986	200	600
43	Phosphate as PO4	mg/l	0.420	IS 3025 Part 31 Sec 1: 2022	NA	NA

Note :- BLQ - Below the Limit of Quantification, LOQ- Limit of Quantification, NTU- Nephelometric Turbidity Unit, mg/l- Milligrams per litre, NA - Not Applicable.

\*\*\*End of Report\*\*\*



D. Anusuya  
Lab Manager  
Authorized Signatory

**Hubert Enviro Care Systems (P) Ltd.**

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax : 42985500

E-mail : labsales@hecs.in

**Laboratory Services Division**

(Chemical &amp; Biological Testing)

Recognized by CPCB (MoEF &amp; CC)

BIS, FSSAI Notified Laboratory

ISO 9001, 14001 &amp; 45001 Certified.

**TEST REPORT**

Page : 1 of 1

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Water

Sample Name : Ground Water

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s.Hubert Enviro care Systems (P) Ltd.

Sample Location : Near Agoor

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method &amp; Plan : IS 17614(Part-1):2021

Report No. : HECSL/WT/139/240325N

Sample ID No : 240325278

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 2 Litres

S.No.	Test Parameters	Units	Results	Test Method
Discipline : Chemical				
1	Hexavalent Chromium as Cr6+	mg/l	BLQ(LOQ:0.01)	IS 3025 Part 52 Clause 6: 2003

Note:- BLQ : Below Limit of Quantification, LOQ: Limit of Quantification, mg/l: milligram per Litre.

\*\*\*End of Report\*\*\*



D.Anusuya  
Lab Manager  
Authorized Signatory

# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 1 of 4

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Water

Sample Name : Ground Water

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Botheri

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method & Plan : IS 17614(Part-1):2021

ULR : TC1231025000017012F

Report No. : HECSL/WT/140/240325

Sample ID No : 240325279

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 2 Litres

S.No.	Test Parameters	Units	Results	Test Method	IS 10500 : 2012	
					Acceptable Limits (Max)	Acceptable Limits (Max)
Discipline : Chemical						
1	Bi carbonate	mg/l	353.8	IS 3025 Part 51: 2001	NA	NA
2	Boron as B	mg/l	BLQ(LOQ:0.1)	IS 3025 Part 57 -Curcumin Method: 2021	0.5	2.4
3	Calcium as Ca	mg/l	100.20	IS 3025 Part 40: 1991(EDTA Titrimetric Method)	75	200
4	Carbonate	mg/l	BLQ(LOQ:1.0)	IS 3025 Part 51: 2001	NA	NA
5	Chloride as Cl	mg/l	123.72	IS 3025 Part 32: 1988 ( Argentometric Method)	250	1000
6	Cyanide as CN	mg/l	BLQ(LOQ:0.01)	IS 3025 Part 27 Sec 1: 2021	0.05	No relaxation
7	Electrical Conductivity at 25°C	µS/cm	1184.0	IS 3025 Part-14: 2013	NA	NA
8	Fluoride as F	mg/l	0.39	APHA 23rd edition (Method 4500F-B , D): 2017	1.0	1.5
9	Iron as Fe	mg/l	0.032	IS 3025 (Part 53): 2003	1.0	No relaxation
10	Magnesium as Mg	mg/l	43.74	IS 3025 Part 46: 1994 ( Valumetric Method using EDTA)	30	100
11	Nitrate as NO3	mg/l	17.88	APHA 23rd edition (Method 4500 NO3B): 2017	45	No relaxation
12	Colour	Hazen units	BLQ(LOQ:1.0)	IS 3025 (Part4): 2021	5	15
13	pH at 25°C	-	7.39	IS 3025(Part 11) : 2022 (Electrometric method)	6.5-8.5	No relaxation



D.Anusuya  
Lab Manager  
Authorized Signatory



# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 2 of 4

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Water

Sample Name : Ground Water

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Botheri

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method & Plan : IS 17614(Part-1):2021

ULR : TC1231025000017012F

Report No. : HECSL/WT/140/240325

Sample ID No : 240325279

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 2 Litres

S.No.	Test Parameters	Units	Results	Test Method	IS 10500 : 2012	
					Acceptable Limits (Max)	Acceptable Limits (Max)
14	Potassium as K	mg/l	7.0	IS 3025 Part 45: 1993 ( Flame emission Photometric Method)	NA	NA
15	Sodium as Na	mg/l	68.0	IS 3025 Part 45: 1993 ( Flame emission Photometric Method)	NA	NA
16	Sulphate as SO <sub>4</sub>	mg/l	89.85	IS 3025 Part 24 Sec 1: 2022( Turbidity Method)( Turbidity Method)	200	400
17	Total dissolved solids	mg/l	626.0	IS 3025 (Part 16): 1984	500	2000
18	Total Suspended Solids	mg/l	BLQ(LOQ:2.0)	IS 3025 (Part 17): 1984	NA	NA
19	Phosphorous as P	mg/l	0.450	IS 3025 Part 31 Sec 1: 2022 ( Stannous Chloride method)	NA	NA
20	Total hardness as CaCO <sub>3</sub>	mg/l	430.0	IS 3025 (Part 21): 2009	200	600
21	Turbidity, NTU	NTU	BLQ(LOQ:0.1)	IS 3025 (Part 10): 1984	1	5
22	Arsenic	mg/l	BLQ (LOQ: 0.005)	USEPA 200.8 : 1994	0.01	No relaxation
23	Cadmium	mg/l	BLQ (LOQ: 0.001)	USEPA 200.8 : 1994	0.003	No relaxation
24	Chromium	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	0.05	No relaxation
25	Copper	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	0.05	1.5



D. Anusuya  
Lab Manager  
Authorized Signatory

# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 3 of 4

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Water

Sample Name : Ground Water

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Botheri

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method & Plan : IS 17614(Part-1):2021

ULR : TC1231025000017012F

Report No. : HECSL/WT/140/240325

Sample ID No : 240325279

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 2 Litres

S.No.	Test Parameters	Units	Results	Test Method	IS 10500 : 2012	
					Acceptable Limits (Max)	Acceptable Limits (Max)
26	Lead	mg/l	BLQ (LOQ: 0.005)	USEPA 200.8 : 1994	0.01	No relaxation
27	Mercury	mg/l	BLQ (LOQ: 0.0005)	USEPA 200.8 : 1994	0.001	No relaxation
28	Nickel	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	0.02	No relaxation
29	Zinc	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	5	15
30	Phenolic compounds as C <sub>6</sub> H <sub>5</sub> OH	mg/l	BLQ(LOQ:0.001)	IS 3025 Part 43 Sec 1: 2022	0.001	0.002
31	Anionic Surface Active agents as MBAS	mg/l	BLQ(LOQ:0.05)	APHA 23rd edition (Method 5540 B, C): 2017	0.2	1
32	Percent Sodium	%	25.07	HECS /WT/SOP/002:: 2019	NA	NA
33	Barium	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	0.7	No relaxation
34	Residual Sodium Carbonate	meq/l	BLQ(LOQ:1.0)	IS 11624: 2019	0.2	1.0
35	Ammonia as NH <sub>3</sub>	mg/l	BLQ(LOQ:0.02)	IS 3025 Part 34:Sec 2: 2021 (Nesslerization Method)	0.5	No relaxation
36	Sodium Adsorption Ratio(SAR)	Square root of (millimole/lit)	1.4	IS 11624 : 2019	NA	NA
37	Dissolved oxygen	mg/l	6.4	IS 3025 (Part 38): 1989 ( Titrimetric Method)	NA	NA



D. Anusuya  
Lab Manager  
Authorized Signatory



# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax : 42985500

E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 4 of 4

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Water

Sample Name : Ground Water

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Botheri

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method & Plan : IS 17614(Part-1):2021

ULR : TC1231025000017012F

Report No. : HECSL/WT/140/240325

Sample ID No : 240325279

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 2 Litres

S.No.	Test Parameters	Units	Results	Test Method	IS 10500 : 2012	
					Acceptable Limits (Max)	Acceptable Limits (Max)
38	Biological Oxygen Demand (BOD)@ 27°C For 3 days	mg/l	BLQ(LOQ:2.0)	IS 3025 Part 44: 1993	NA	NA
39	Chemical Oxygen Demand (COD)	mg/l	BLQ(LOQ:4.0)	IS 3025 Part 58: 2006	NA	NA
40	Selenium	mg/l	BLQ (LOQ: 0.005)	USEPA 200.8 : 1994	0.01	No relaxation
41	Manganese	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	0.1	0.3
42	Total alkalinity as CaCO <sub>3</sub>	mg/l	290.0	IS 3025 (Part 23): 1986	200	600
43	Phosphate as P	mg/l	0.450	IS 3025 Part 31 Sec 1: 2022	NA	NA

Note :- BLQ - Below the Limit of Quantification, LOQ- Limit of Quantification, NTU- Nephelometric Turbidity Unit, mg/l- Milligrams per litre, NA - Not Applicable.

\*\*\*End of Report\*\*\*



D. Anusuya  
Lab Manager  
Authorized Signatory

**Hubert Enviro Care Systems (P) Ltd.**

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax : 42985500

E-mail : labsales@hecs.in

**Laboratory Services Division**

(Chemical &amp; Biological Testing)

Recognized by CPCB (MoEF &amp; CC)

BIS, FSSAI Notified Laboratory

ISO 9001, 14001 &amp; 45001 Certified.

**TEST REPORT**

Page : 1 of 1

Name of the Client : M/s. SIPCOT  
Address of the Client : Tindivanam  
Group : Water  
Sample Name : Ground Water  
Sample Mark : NA  
Sample Reference : NA  
Sample Drawn By : M/s.Hubert Enviro care Systems (P) Ltd.  
Sample Location : Botheri  
Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0  
Sampling Method & Plan : IS 17614(Part-I):2021

Report No. : HECSL/WT/140/240325N  
Sample ID No : 240325279  
Sampling Date : 24/03/2025  
Received Date : 24/03/2025  
Commenced Date : 24/03/2025  
Completed On : 07/04/2025  
Report Date : 07/04/2025  
Sample quantity : 2 Litres

S.No.	Test Parameters	Units	Results	Test Method
Discipline : Chemical				
1	Hexavalent Chromium as Cr6+	mg/l	BLQ(LOQ:0.01)	IS 3025 Part 52 Clause 6: 2003

Note:- BLQ : Below Limit of Quantification, LOQ: Limit of Quantification, mg/l: milligram per Litre.

\*\*\*End of Report\*\*\*



D.Anusuya  
Lab Manager  
Authorized Signatory



# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



TC-12310

## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 1 of 4

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Water

Sample Name : Ground Water

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Near Project Site

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method & Plan : IS 17614(Part-1):2021

U.L.R : TC1231025000017013F

Report No. : HECSL/WT/141/240325

Sample ID No : 240325280

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 2 Litres

S.No.	Test Parameters	Units	Results	Test Method	IS 10500 : 2012	
					Acceptable Limits (Max)	Acceptable Limits (Max)
Discipline : Chemical						
1	Bi carbonate	mg/l	414.8	IS 3025 Part 51: 2001	NA	NA
2	Boron as B	mg/l	BLQ(LOQ:0.1)	IS 3025 Part 57 -Curcumin Method: 2021	0.5	2.4
3	Calcium as Ca	mg/l	80.16	IS 3025 Part 40: 1991(EDTA Titrimetric Method)	75	200
4	Carbonate	mg/l	BLQ(LOQ:1.0)	IS 3025 Part 51: 2001	NA	NA
5	Chloride as Cl	mg/l	59.38	IS 3025 Part 32: 1988 ( Argentometric Method)	250	1000
6	Cyanide as CN	mg/l	BLQ(LOQ:0.01)	IS 3025 Part 27 Sec 1: 2021	0.05	No relaxation
7	Electrical Conductivity at 25°C	µS/cm	913.0	IS 3025 Part-14: 2013	NA	NA
8	Fluoride as F	mg/l	0.35	APHA 23rd edition (Method 4500F-B , D): 2017	1.0	1.5
9	Iron as Fe	mg/l	0.063	IS 3025 (Part 53): 2003	1.0	No relaxation
10	Magnesium as Mg	mg/l	41.31	IS 3025 Part 46: 1994 ( Valumetric Method using EDTA)	30	100
11	Nitrate as NO3	mg/l	3.9	APHA 23rd edition (Method 4500 NO3B): 2017	45	No relaxation
12	Colour	Hazen units	BLQ(LOQ:1.0)	IS 3025 (Part4): 2021	5	15
13	pH at 25°C	-	7.81	IS 3025(Part 11) : 2022 (Electrometric method)	6.5-8.5	No relaxation



D.Anusuya  
Lab Manager  
Authorized Signatory

# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 2 of 4

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Water

Sample Name : Ground Water

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Near Project Site

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method & Plan : IS 17614(Part-1):2021

U.L.R : TC1231025000017013F

Report No. : HECSL/WT/141/240325

Sample ID No : 240325280

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 2 Litres

S.No.	Test Parameters	Units	Results	Test Method	IS 10500 : 2012	
					Acceptable Limits (Max)	Acceptable Limits (Max)
14	Potassium as K	mg/l	5.0	IS 3025 Part 45: 1993 ( Flame emission Photometric Method)	NA	NA
15	Sodium as Na	mg/l	48.0	IS 3025 Part 45: 1993 ( Flame emission Photometric Method)	NA	NA
16	Sulphate as SO <sub>4</sub>	mg/l	71.27	IS 3025 Part 24 Sec 1: 2022( Turbidity Method)( Turbidity Method)	200	400
17	Total dissolved solids	mg/l	531.0	IS 3025 (Part 16): 1984	500	2000
18	Total Suspended Solids	mg/l	5.0	IS 3025 (Part 17): 1984	NA	NA
19	Phosphorous as P	mg/l	0.091	IS 3025 Part 31 Sec 1: 2022 ( Stannous Chloride method)	NA	NA
20	Total hardness as CaCO <sub>3</sub>	mg/l	370.0	IS 3025 (Part 21): 2009	200	600
21	Turbidity, NTU	NTU	2.4	IS 3025 (Part 10): 1984	1	5
22	Arsenic	mg/l	BLQ (LOQ: 0.005)	USEPA 200.8 : 1994	0.01	No relaxation
23	Cadmium	mg/l	BLQ (LOQ: 0.001)	USEPA 200.8 : 1994	0.003	No relaxation
24	Chromium	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	0.05	No relaxation
25	Copper	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	0.05	1.5



D. Anusuya  
Lab Manager  
Authorized Signatory



# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 3 of 4

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Water

Sample Name : Ground Water

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Near Project Site

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method & Plan : IS 17614(Part-1):2021

ULR : TC1231025000017013F

Report No. : HECSL/WT/141/240325

Sample ID No : 240325280

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 2 Litres

S.No.	Test Parameters	Units	Results	Test Method	IS 10500 : 2012	
					Acceptable Limits (Max)	Acceptable Limits (Max)
26	Lead	mg/l	BLQ (LOQ: 0.005)	USEPA 200.8 : 1994	0.01	No relaxation
27	Mercury	mg/l	BLQ (LOQ: 0.0005)	USEPA 200.8 : 1994	0.001	No relaxation
28	Nickel	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	0.02	No relaxation
29	Zinc	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	5	15
30	Phenolic compounds as C6H5OH	mg/l	BLQ(LOQ:0.001)	IS 3025 Part 43 Sec 1: 2022	0.001	0.002
31	Anionic Surface Active agents as MBAS	mg/l	BLQ(LOQ:0.05)	APHA 23rd edition (Method 5540 B, C): 2017	0.2	1
32	Percent Sodium	%	21.59	HECS /WT/SOP/002:: 2019	NA	NA
33	Barium	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	0.7	No relaxation
34	Residual Sodium Carbonate	meq/l	BLQ(LOQ:1.0)	IS 11624: 2019	0.2	1.0
35	Ammonia as NH3	mg/l	BLQ(LOQ:0.02)	IS 3025 Part 34:Sec 2: 2021 (Nesslerization Method)	0.5	No relaxation
36	Sodium Adsorption Ratio(SAR)	Square root of (millimole/lit)	1.1	IS 11624 : 2019	NA	NA
37	Dissolved oxygen	mg/l	6.5	IS 3025 (Part 38): 1989 ( Titrimetric Method)	NA	NA



D.Anusuya  
Lab Manager  
Authorized Signatory

# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 4 of 4

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Water

Sample Name : Ground Water

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Near Project Site

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method & Plan : IS 17614(Part-1):2021

ULR : TC1231025000017013F

Report No. : HECSL/WT/141/240325

Sample ID No : 240325280

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 2 Litres

S.No.	Test Parameters	Units	Results	Test Method	IS 10500 : 2012	
					Acceptable Limits (Max)	Acceptable Limits (Max)
38	Biological Oxygen Demand (BOD)@ 27°C For 3 days	mg/l	BLQ(LOQ:2.0)	IS 3025 Part 44: 1993	NA	NA
39	Chemical Oxygen Demand (COD)	mg/l	BLQ(LOQ:4.0)	IS 3025 Part 58: 2006	NA	NA
40	Scienium	mg/l	BLQ (LOQ: 0.005)	USEPA 200.8 : 1994	0.01	No relaxation
41	Manganese	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	0.1	0.3
42	Total alkalinity as CaCO3	mg/l	340.0	IS 3025 (Part 23): 1986	200	600
43	Phosphate as PO4	mg/l	0.091	IS 3025 Part 31 Sec 1: 2022	NA	NA

Note :- BLQ - Below the Limit of Quantification, LOQ- Limit of Quantification, NTU- Nephelometric Turbidity Unit, mg/l- Milligrams per litre, NA - Not Applicable.

\*\*\*End of Report\*\*\*



D. Anusuya  
Lab Manager  
Authorized Signatory



**Hubert Enviro Care Systems (P) Ltd.**

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax : 42985500

E-mail : labsales@hecs.in

**Laboratory Services Division**

(Chemical &amp; Biological Testing)

Recognized by CPCB (MoEF &amp; CC)

BIS, FSSAI Notified Laboratory

ISO 9001, 14001 &amp; 45001 Certified.

**TEST REPORT**

Page : 1 of 1

Name of the Client : M/s. SIPCOT  
Address of the Client : Tindivanam  
Group : Water  
Sample Name : Ground Water  
Sample Mark : NA  
Sample Reference : NA  
Sample Drawn By : M/s.Hubert Enviro care Systems (P) Ltd.  
Sample Location : Near Project Site  
Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0  
Sampling Method & Plan : IS 17614(Part-1):2021

Report No. : HECSL/WT/141/240325N  
Sample ID No : 240325280  
Sampling Date : 24/03/2025  
Received Date : 24/03/2025  
Commenced Date : 24/03/2025  
Completed On : 07/04/2025  
Report Date : 07/04/2025  
Sample quantity : 2 Litres

S.No.	Test Parameters	Units	Results	Test Method
Discipline : Chemical				
1	Hexavalent Chromium as Cr6+	mg/l	BLQ(LOQ:0.01)	IS 3025 Part 52 Clause 6: 2003

Note:- BLQ : Below Limit of Quantification, LOQ: Limit of Quantification, mg/l: milligram per Litre.

\*\*\*End of Report\*\*\*



D.Anusuya  
Lab Manager  
Authorized Signatory

# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 1 of 4

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Water

Sample Name : Surface Water

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Lake Near Vizhukkuam

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method & Plan : IS 17614(Part-1):2021

ULR : TC1231025000017027F

Report No. : HECSL/WT/143/240325

Sample ID No : 240325282

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 2 Litres

S.No.	Test Parameters	Units	Results	Test Method	Inland Surface water Standards (Schedule -VI)
Discipline : Chemical					
1	Total alkalinity as CaCO <sub>3</sub>	mg/l	135.0	IS 3025 Part 23: 1986	NA
2	Bi carbonate	mg/l	164.7	IS 3025 Part 51: 2001	NA
3	Biological Oxygen Demand (BOD) <sub>5</sub> @ 27°C For 3 days	mg/l	2.0	IS 3025 Part 44: 1993	30
4	Boron as B	mg/l	BLQ(LOQ:0.1)	IS 3025 Part 57: 2021 ( Curcumin Method)	NA
5	Calcium as Ca	mg/l	22.04	IS 3025 Part 40: 1991(EDTA Titrimetric Method)	NA
6	Chemical Oxygen Demand (COD)	mg/l	24.0	IS 3025 Part 58: 2006	250
7	Chloride as Cl	mg/l	44.53	IS 3025 Part 32: 1988 ( Argentometric Method)	NA
8	Colour	Hazen units	BLQ(LOQ:1.0)	IS 3025 Part 4: 2021	NA
9	Dissolved oxygen	mg/l	5.9	IS 3025 Part 38: 1989	NA
10	Electrical Conductivity at 25°C	µS/cm	450.0	IS:3025 Part 14: 2013	NA
11	Fluoride as F	mg/l	0.27	APHA 23rd edition Method 4500 F -B,D: 2017	2.0
12	Iron as Fe	mg/l	0.17	IS 3025 Part 53: 2003	3.0
13	Nitrate as NO <sub>3</sub>	mg/l	5.18	APHA 23rd edition Method 4500 NO <sub>3</sub> B: 2017	NA



D.Anusuya  
Lab Manager  
Authorized Signatory

# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 2 of 4

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Water

Sample Name : Surface Water

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Lake Near Vizhukkuam

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method & Plan : IS 17614(Part-1):2021

ULR : TC1231025000017027F

Report No. : HECSL/WT/143/240325

Sample ID No : 240325282

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 2 Litres

S.No.	Test Parameters	Units	Results	Test Method	Inland Surface water Standards (Schedule -VI)
14	Manganese	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	2.0
15	Selenium	mg/l	BLQ (LOQ: 0.005)	USEPA 200.8 : 1994	0.05
16	Phosphate as PO4	mg/l	BLQ(LOQ:0.02)	APHA 23rd edition Method 4500-P B,D: 2017	NA
17	pH at 25°C		8.21	IS 3025 Part 11: 2022 ( Electrometric Method)	5.5 – 9.0
18	Total dissolved solids	mg/l	233.0	IS 3025 Part 16: 1984	NA
19	Carbonate	mg/l	BLQ(LOQ:1.0)	IS 3025 Part 51: 2001	NA
20	Cyanide as CN	mg/l	BLQ(LOQ:0.01)	IS 3025 Part 27 sec 1: 2021	0.2
21	Magnesium as Mg	mg/l	17.01	IS 3025 Part 46: 1994 ( Valumetric Method using EDTA)	NA
22	Potassium as K	mg/l	4.0	IS 3025 Part 45: 1993	NA
23	Sodium as Na	mg/l	35.0	IS 3025 Part 45: 1983	NA
24	Sulphate as SO4	mg/l	10.6	IS 3025 Part 24 Sec 1: 2022	NA
25	Phenolic compounds as C6H5OH	mg/l	BLQ(LOQ:0.001)	IS 3025 Part 43:Sec 1: 2022	1.0
26	Anionic Surface Active agents as MBAS	mg/l	BLQ(LOQ:0.05)	APHA 23rd edition Method 5540 B , C: 2017	NA



D.Anusuya  
Lab Manager  
Authorized Signatory



# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 3 of 4

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Water

Sample Name : Surface Water

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Lake Near Vizhukkuam

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method & Plan : IS 17614(Part-1):2021

ULR : TC1231025000017027F

Report No. : HECSL/WT/143/240325

Sample ID No : 240325282

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 2 Litres

S.No.	Test Parameters	Units	Results	Test Method	Inland Surface water Standards (Schedule - VI)
27	Percent Sodium	%	36.72	HECSG /WT/SOP/002 Issue No:01, Issue date 18.12: 2021	NA
28	Barium	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	NA
29	Residual Sodium Carbonate	mg/l	BLQ(LOQ:1.0)	IS 11624: 2019	NA
30	Ammonia as NH3	mg/l	0.35	IS 3025 Part 34 Sec 2: 2021	5.0
31	Sodium Adsorption Ratio(SAR)	Square root of (millimole/liter)	1.36	IS 11624: 2019	NA
32	Total Hardness as CaCO3	mg/l	125.0	IS 3025 Part 21: 2009	NA
33	Total Phosphorous as P	mg/l	BLQ(LOQ:0.02)	IS 3025 Part 31 Sec 1: 2022	NA
34	Total Suspended Solids	mg/l	4.0	IS 3025 Part 17: 1984	100
35	Turbidity	NTU	1.4	IS 3025 Part 10: 1984	NA
36	Arsenic	mg/l	BLQ (LOQ: 0.005)	USEPA 200.8 : 1994	0.2
37	Cadmium	mg/l	BLQ (LOQ: 0.001)	USEPA 200.8 : 1994	2.0
38	Chromium	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	2.0
39	Copper	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	3.0



D.Anusuya  
Lab Manager  
Authorized Signatory



# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 4 of 4

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Water

Sample Name : Surface Water

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Lake Near Vizhukkuam

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method & Plan : IS 17614(Part-1):2021

ULR : TC1231025000017027F

Report No. : HECSL/WT/143/240325

Sample ID No : 240325282

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 2 Litres

S.No.	Test Parameters	Units	Results	Test Method	Inland Surface water Standards (Schedule -VI)
40	Lead	mg/l	BLQ (LOQ: 0.005)	USEPA 200.8 : 1994	0.1
41	Mercury	mg/l	BLQ (LOQ: 0.0005)	USEPA 200.8 : 1994	0.01
42	Nickel	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	3.0
43	Zinc	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	5.0

Note : BLQ : Below Limit of Quantification, LOQ: Limit of Quantification, mg/l: milligram per Litre,

NTU- Nephelometric Turbidity Unit, NA - Not Applicable.

\*\*\*End of Report\*\*\*



D.Anusuya  
Lab Manager  
Authorized Signatory

**Hubert Enviro Care Systems (P) Ltd.**

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax : 42985500

E-mail : labsales@hecs.in

**Laboratory Services Division**

(Chemical &amp; Biological Testing)

Recognized by CPCB (MoEF &amp; CC)

BIS, FSSAI Notified Laboratory

ISO 9001, 14001 &amp; 45001 Certified.

**TEST REPORT**

Page : 1 of 1

Name of the Client : M/s. SIPCOT  
Address of the Client : Tindivanam  
Group : Water  
Sample Name : Surface Water  
Sample Mark : NA  
Sample Reference : NA  
Sample Drawn By : M/s.Hubert Enviro care Systems (P) Ltd.  
Sample Location : Lake Near Vizhukkuam  
Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0  
Sampling Method & Plan : IS 17614(Part-1):2021

Report No. : HECSL/WT/143/240325N  
Sample ID No : 240325282  
Sampling Date : 24/03/2025  
Received Date : 24/03/2025  
Commenced Date : 24/03/2025  
Completed On : 07/04/2025  
Report Date : 07/04/2025  
Sample quantity : 2 Litres

S.No.	Test Parameters	Units	Results	Test Method	Inland Surface water Standards (Schedule -VI)
Discipline : Chemical					
1	Hexavalent Chromium as Cr6+	mg/l	BLQ(LOQ:0.01)	IS 3025 Part 52 Clause 6: 2003	0.1

Note:- BLQ : Below the Limit of Quantification, LOQ: Limit of Quantification, mg/l: milligram per Litre.

\*\*\*End of Report\*\*\*



D.Anusuya

Lab Manager

Authorized Signatory

# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 1 of 4

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Water

Sample Name : Surface Water

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Lake Near Botheri

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method & Plan : IS 17614(Part-1):2021

ULR : TC1231025000017028F

Report No. : HECSL/WT/144/240325

Sample ID No : 240325283

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 2 Litres

S.No.	Test Parameters	Units	Results	Test Method	Inland Surface water Standards (Schedule -VI)
Discipline : Chemical					
1	Total alkalinity as CaCO <sub>3</sub>	mg/l	240.0	IS 3025 Part 23: 1986	NA
2	Bi carbonate	mg/l	292.8	IS 3025 Part 51: 2001	NA
3	Biological Oxygen Demand (BOD) <sub>5</sub> at 27°C For 3 days	mg/l	2.0	IS 3025 Part 44: 1993	30
4	Boron as B	mg/l	BLQ(LOQ:0.1)	IS 3025 Part 57: 2021 ( Curcumin Method)	NA
5	Calcium as Ca	mg/l	52.10	IS 3025 Part 40: 1991(EDTA Titrimetric Method)	NA
6	Chemical Oxygen Demand (COD)	mg/l	16.0	IS 3025 Part 58: 2006	250
7	Chloride as Cl	mg/l	133.61	IS 3025 Part 32: 1988 ( Argentometric Method)	NA
8	Colour	Hazen units	BLQ(LOQ:1.0)	IS 3025 Part 4: 2021	NA
9	Dissolved oxygen	mg/l	5.8	IS 3025 Part 38: 1989	NA
10	Electrical Conductivity at 25°C	µS/cm	910.0	IS:3025 Part 14: 2013	NA
11	Fluoride as F	mg/l	0.38	APHA 23rd edition Method 4500 F -B,D: 2017	2.0
12	Iron as Fe	mg/l	0.13	IS 3025 Part 53: 2003	3.0
13	Nitrate as NO <sub>3</sub>	mg/l	6.63	APHA 23rd edition Method 4500 NO <sub>3</sub> B: 2017	NA



D.Anusuya  
Lab Manager  
Authorized Signatory



# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 2 of 4

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Water

Sample Name : Surface Water

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Lake Near Botheri

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method & Plan : IS 17614(Part-1):2021

ULR : TC1231025000017028F

Report No. : HECSL/WT/144/240325

Sample ID No : 240325283

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 2 Litres

S.No.	Test Parameters	Units	Results	Test Method	Inland Surface water Standards (Schedule -VI)
14	Manganese	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	2.0
15	Selenium	mg/l	BLQ (LOQ: 0.005)	USEPA 200.8 : 1994	0.05
16	Phosphate as PO <sub>4</sub>	mg/l	0.086	APHA 23rd edition Method 4500-P B,D: 2017	NA
17	pH at 25°C		7.66	IS 3025 Part 11: 2022 ( Electrometric Method)	5.5 - 9.0
18	Total dissolved solids	mg/l	480.0	IS 3025 Part 16: 1984	NA
19	Carbonate	mg/l	BLQ(LOQ:1.0)	IS 3025 Part 51: 2001	NA
20	Cyanide as CN	mg/l	BLQ(LOQ:0.01)	IS 3025 Part 27 sec 1: 2021	0.2
21	Magnesium as Mg	mg/l	41.31	IS 3025 Part 46: 1994 ( Valumetric Method using EDTA)	NA
22	Potassium as K	mg/l	8.0	IS 3025 Part 45: 1993	NA
23	Sodium as Na	mg/l	68.0	IS 3025 Part 45: 1983	NA
24	Sulphate as SO <sub>4</sub>	mg/l	12.17	IS 3025 Part 24 Sec 1: 2022	NA
25	Phenolic compounds as C <sub>6</sub> H <sub>5</sub> OH	mg/l	BLQ(LOQ:0.001)	IS 3025 Part 43:Sec 1: 2022	1.0
26	Anionic Surface Active agents as MBAS	mg/l	BLQ(LOQ:0.05)	APHA 23rd edition Method 5540 B , C: 2017	NA



D.Anusuya  
Lab Manager  
Authorized Signatory



# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax : 42985500

E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 3 of 4

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Water

Sample Name : Surface Water

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Lake Near Botheri

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method & Plan : IS 17614(Part-1):2021

ULR : TC1231025000017028F

Report No. : HECSL/WT/144/240325

Sample ID No : 240325283

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 2 Litres

S.No.	Test Parameters	Units	Results	Test Method	Inland Surface water Standards (Schedule -VI)
27	Percent Sodium	%	32.10	HECSG /WT/SOP/002 Issue No:01, Issue date 18.12: 2021	NA
28	Barium	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	NA
29	Residual Sodium Carbonate	mg/l	BLQ(LOQ:1.0)	IS 11624: 2019	NA
30	Ammonia as NH3	mg/l	0.42	IS 3025 Part 34 Sec 2: 2021	5.0
31	Sodium Adsorption Ratio(SAR)	Square root of (millimole/lit r	1.70	IS 11624: 2019	NA
32	Total Hardness as CaCO3	mg/l	300.0	IS 3025 Part 21: 2009	NA
33	Total Phosphorous as P	mg/l	0.026	IS 3025 Part 31 Sec 1: 2022	NA
34	Total Suspended Solids	mg/l	3.0	IS 3025 Part 17: 1984	100
35	Turbidity	NTU	0.8	IS 3025 Part 10: 1984	NA
36	Arsenic	mg/l	BLQ (LOQ: 0.005)	USEPA 200.8 : 1994	0.2
37	Cadmium	mg/l	BLQ (LOQ: 0.001)	USEPA 200.8 : 1994	2.0
38	Chromium	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	2.0
39	Copper	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	3.0



D. Anusuya  
Lab Manager  
Authorized Signatory

## Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax : 42985500

E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 4 of 4

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Water

Sample Name : Surface Water

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Lake Near Botheri

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method & Plan : IS 17614(Part-1):2021

ULR : TC1231025000017028F

Report No. : HECSL/WT/144/240325

Sample ID No : 240325283

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 2 Litres

S.No.	Test Parameters	Units	Results	Test Method	Inland Surface water Standards (Schedule -VI)
40	Lead	mg/l	BLQ (LOQ: 0.005)	USEPA 200.8 : 1994	0.1
41	Mercury	mg/l	BLQ (LOQ: 0.0005)	USEPA 200.8 : 1994	0.01
42	Nickel	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	1.0
43	Zinc	mg/l	BLQ (LOQ: 0.01)	USEPA 200.8 : 1994	5.0

Note : BLQ : Below Limit of Quantification, LOQ: Limit of Quantification, mg/l: milligram per Litre,

NTU- Nephelometric Turbidity Unit, NA - Not Applicable.

\*\*\*End of Report\*\*\*



D. Anusuya  
Lab Manager  
Authorized Signatory

**TEST REPORT**

Page : 2 of 1

Name of the Client : M/s. SIPCOT  
Address of the Client : Tindivanam  
Group : Water  
Sample Name : Surface Water  
Sample Mark : NA  
Sample Reference : NA  
Sample Drawn By : M/s.Hubert Enviro care Systems (P) Ltd.  
Sample Location : Lake Near Botheri  
Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0  
Sampling Method & Plan : IS 17614(Part-1):2021

Report No. : HECSL/WT/144/240325 N  
Sample ID No : 240325283  
Sampling Date : 24/03/2025  
Received Date : 24/03/2025  
Commenced Date : 24/03/2025  
Completed On : 07/04/2025  
Report Date : 07/04/2025  
Sample quantity : 2 Litres

S.No.	Test Parameters	Units	Results	Test Method	Inland Surface water Standards (Schedule -VI)
<b>Discipline : Chemical</b>					
1	Hexavalent Chromium as Cr6+	mg/l	BLQ(LOQ:0.01)	IS 3025 Part 52 Clause 6: 2003	0.1

Note:- BLQ : Below the Limit of Quantification, LOQ: Limit of Quantification, mg/l: milligram per Litre.

\*\*\*End of Report\*\*\*



D.Anusuya  
Lab Manager  
Authorized Signatory



# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 1 of 2

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Pollution & Environment

Sample Name : Soil

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Near Project Area

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method & Plan : ICARDA :2013

ULR : TC1231025000017085F

Report No. : HECS/PE/022/240325

Sample ID No : 240325284

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 1 Kg

S.No.	Test Parameters	Units	Results	Test Method
Discipline : Chemical				
1	Cadmium	mg/Kg	BLQ (LOQ: 0.1)	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021
2	Chromium	mg/Kg	12.57	HECS-G/INS/SOP/042 Issue No.:01 Issue Date:01.03.2021
3	Copper	mg/Kg	24.32	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021
4	Zinc	mg/kg	13.58	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021
5	Soil Texture	-	Clay loam	FAO of United Nations, Rome Chapter - III 2008
6	Soil Texture i) Sand	%	40.5	FAO of United Nations, Rome Chapter - III 2008
7	Soil Texture ii) Silt	%	29.3	FAO of United Nations, Rome Chapter - III 2008
8	Soil Texture iii) Clay	%	30.2	FAO of United Nations, Rome Chapter - III 2008
9	pH Value @ 25 ° C (1 : 2.5)	-	8.68	IS 2720 (Part 26) 1987
10	Electrical conductivity @ 25 ° C (1 : 2)	µS/cm	354.0	IS 14767: 2000



D. Anusuya

Lab Manager

Authorized Signatory



# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 2 of 2

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Pollution & Environment

Sample Name : Soil

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Near Project Area

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method & Plan : ICARDA :2013

ULR : TC1231025000017085F

Report No. : HECS/PE/022/240325

Sample ID No : 240325284

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 1 Kg

S.No.	Test Parameters	Units	Results	Test Method
11	Bulk Density	gm/cm <sup>3</sup>	0.99	FAO of United Nations Rome 2007
12	Organic Carbon	%	0.30	IS 2720 (Part 22) Section I 1972
13	Organic Matter	%	0.52	IS 2720 (Part 22) Section I 1972
14	Available Phosphorous as P	µg/g	BLQ(LOQ 5.0)	FAO of United Nations, Rome Chapter - III 2008
15	Available Potassium	mEq/100g	40.29	FAO of United Nations, Rome Chapter - III 2008
16	Boron as B	mg/kg	BLQ(LOQ 0.1)	HECS-G/ENV/SSW/SOP/018 Issue No.:01 Issue Date:02/07/2020
17	Total Nitrogen as N	%	0.0092	IS 14684 Clause 4 1999
18	Exchangable Calcium as Ca	mEq/L	11.71	FAO of United Nations, Rome Chapter - III 2008
19	Exchangable Magnesium as Mg	mEq/L	3.90	FAO of United Nations, Rome Chapter - III 2008
20	Cation Exchange Capacity	mEq/100g	2.1	IS 2720 (Part 24) Clause 5 1976
21	Water Holding capacity	%	18.0	IS 14765: 2000
22	Colour	-	Brown	HECS-G/ENV/SSW/SOP/011 Issue No.:01 Issue Date:02/07/2020

Note:- BLQ : Below the Limit of Quantification, LOQ: Limit of Quantification, mg/kg: milligram per kilogram, % - Percentage..

\*\*\*End of Report\*\*\*



D. Anusuya  
Lab Manager  
Authorized Signatory

**Hubert Enviro Care Systems (P) Ltd.**A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax : 42985500

E-mail : labsales@hecs.in

**Laboratory Services Division**(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS, FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.**TEST REPORT**

Page : 1 of 1

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Pollution &amp; Environment

Sample Name : Soil

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s.Hubert Enviro care Systems (P) Ltd.

Sample Location : Near Project Area

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method &amp; Plan : ICARDA :2013

Report No. : HECS/PE/022/240325/N

Sample ID No : 240325284

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 1 Kg

S.No.	Test Parameters	Units	Results	Test Method
Discipline : Chemical				
1	Moisture	%	3.98	HECS-G/ENV/SSW/SOP/003 Issue No.:01 Issue Date:02:07: 2020
2	Manganese	mg/kg	101.6	HECS-G/INS/SOP/ 042
3	Iron	mg/kg	4.59	Inhouse method
4	Infiltration Rate	-	0.8	Inhouse method

Note:- mg/kg: milligram per kilogram, % - Percentage.

\*\*\*End of Report\*\*\*

D.Anusuya  
Lab Manager  
Authorized Signatory

# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax : 42985500

E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 1 of 2

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Pollution & Environment

Sample Name : Soil

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Near Botheri

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method & Plan : ICARDA :2013

ULR : TC1231025000017086F

Report No. : HECS/PE/023/240325

Sample ID No : 240325285

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 1 Kg

S.No.	Test Parameters	Units	Results	Test Method
Discipline : Chemical				
1	Cadmium	mg/Kg	BLQ (LOQ: 0.1)	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021
2	Chromium	mg/Kg	11.79	HECS-G/INS/SOP/042 Issue No.:01 Issue Date:01.03.2021
3	Copper	mg/Kg	22.78	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021
4	Zinc	mg/kg	20.30	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021
5	Soil Texture	-	Sandy clay loam	FAO of United Nations, Rome Chapter - III 2008
6	Soil Texture i) Sand	%	46.8	FAO of United Nations, Rome Chapter - III 2008
7	Soil Texture ii) Silt	%	28.2	FAO of United Nations, Rome Chapter - III 2008
8	Soil Texture iii) Clay	%	25.0	FAO of United Nations, Rome Chapter - III 2008
9	pH Value @ 25 ° C (1 : 2.5)	-	8.72	IS 2720 (Part 26) 1987
10	Electrical conductivity @ 25 ° C (1 : 2)	µS/cm	240.0	IS 14767: 2000



D. Anusuya  
Lab Manager  
Authorized Signatory



# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 2 of 2

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Pollution & Environment

Sample Name : Soil

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Near Botheri

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method & Plan : ICARDA :2013

ULR : TC1231025000017086F

Report No. : HECS/PE/023/240325

Sample ID No : 240325285

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 1 Kg

S.No.	Test Parameters	Units	Results	Test Method
11	Bulk Density	gm/cm3	1.00	FAO of United Nations Rome 2007
12	Organic Carbon	%	0.31	IS 2720 (Part 22) Section I 1972
13	Organic Matter	%	0.53	IS 2720 (Part 22) Section I 1972
14	Available Phosphorous as P	µg/g	7.64	FAO of United Nations, Rome Chapter - III 2008
15	Available Potassium	mEq/100g	18.84	FAO of United Nations, Rome Chapter - III 2008
16	Boron as B	mg/kg	BLQ(LOQ 0.1)	HECS-G/ENV/SSW/SOP/018 Issue No.:01 Issue Date:02:07 2020
17	Total Nitrogen as N	%	0.0116	IS 14684 Clause 4 1999
18	Exchangable Calcium as Ca	mEq/L	7.97	FAO of United Nations, Rome Chapter - III 2008
19	Exchangable Magnesium as Mg	mEq/L	3.98	FAO of United Nations, Rome Chapter - III 2008
20	Cation Exchange Capacity	mEq/100g	1.4	IS 2720 (Part 24) Clause 5 1976
21	Water Holding capacity	%	16.4	IS 14765: 2000
22	Colour	-	Brown	HECS-G/ENV/SSW/SOP/011 Issue No.:01 Issue Date:02:07 2020

Note:- BLQ : Below the Limit of Quantification, LOQ: Limit of Quantification, mg/kg: milligram per kilogram, % - Percentage..

\*\*\*End of Report\*\*\*



D.Anusuya  
Lab Manager  
Authorized Signatory



**Hubert Enviro Care Systems (P) Ltd.**

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax : 42985500

E-mail : labsales@hecs.in

**Laboratory Services Division**

(Chemical &amp; Biological Testing)

Recognized by CPCB (MoEF &amp; CC)

BIS, FSSAI Notified Laboratory

ISO 9001, 14001 &amp; 45001 Certified.

**TEST REPORT**

Page : 1 of 1

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Pollution &amp; Environment

Sample Name : Soil

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s.Hubert Enviro care Systems (P) Ltd.

Sample Location : Near Botheri

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method &amp; Plan : ICARDA :2013

Report No. : HECS/PE/023/240325/N

Sample ID No : 240325285

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 1 Kg

S.No.	Test Parameters	Units	Results	Test Method
Discipline : Chemical				
1	Moisture	%	5.35	HECS-G/ENV/SSW/SOP/003 Issue No.:01 Issue Date:02-07-2020
2	Manganese	mg/kg	118.0	HECS-G/INS/SOP/ 042
3	Iron	mg/kg	BLQ(LOQ 0.02)	Inhouse method
4	Infiltration Rate	-	1.5	Inhouse method

Note:- mg/kg: milligram per kilogram, % - Percentage.

\*\*\*End of Report\*\*\*



D.Anusuya  
Lab Manager  
Authorized Signatory

# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 1 of 2

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Pollution & Environment

Sample Name : Soil

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Near Agoor

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method & Plan : ICARDA :2013

ULR : TC1231025000017087F

Report No. : HECS/PE/024/240325

Sample ID No : 240325286

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 1 Kg

S.No.	Test Parameters	Units	Results	Test Method
Discipline : Chemical				
1	Cadmium	mg/Kg	BLQ (LOQ: 0.1)	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021
2	Chromium	mg/Kg	13.21	HECS-G/INS/SOP/042 Issue No.:01 Issue Date:01.03.2021
3	Copper	mg/Kg	18.45	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021
4	Zinc	mg/kg	18.95	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021
5	Soil Texture	-	Clay loam	FAO of United Nations, Rome Chapter - III 2008
6	Soil Texture i)Sand	%	22.0	FAO of United Nations, Rome Chapter - III 2008
7	Soil Texture ii)Silt	%	41.6	FAO of United Nations, Rome Chapter - III 2008
8	Soil Texture iii)Clay	%	36.4	FAO of United Nations, Rome Chapter - III 2008
9	pH Value @ 25 ° C (1 : 2.5)	-	7.08	IS 2720 (Part 26) 1987
10	Electrical conductivity @ 25 ° C (1 : 2)	µS/cm	47.9	IS 14767: 2000



D.Anusuya  
Lab Manager  
Authorized Signatory

# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 2 of 2

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Pollution & Environment

Sample Name : Soil

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Near Agoor

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method & Plan : ICARDA :2013

ULR : TC1231025000017087F

Report No. : HECS/PE/024/240325

Sample ID No : 240325286

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 1 Kg

S.No.	Test Parameters	Units	Results	Test Method
11	Bulk Density	gm/cm <sup>3</sup>	0.96	FAO of United Nations Rome 2007
12	Organic Carbon	%	0.48	IS 2720 (Part 22) Section I 1972
13	Organic Matter	%	0.83	IS 2720 (Part 22) Section I 1972
14	Available Phosphorous as P	µg/g	BLQ(LOQ 5.0)	FAO of United Nations, Rome Chapter - III 2008
15	Available Potassium	mEq/100g	26.13	FAO of United Nations, Rome Chapter - III 2008
16	Boron as B	mg/kg	BLQ(LOQ 0.1)	HECS-G/ENV/SSW/SOP/018 Issue No.:01 Issue Date:02:07 2020
17	Total Nitrogen as N	%	0.0127	IS 14684 Clause 4 1999
18	Exchangable Calcium as Ca	mEq/L	11.80	FAO of United Nations, Rome Chapter - III 2008
19	Exchangable Magnesium as Mg	mEq/L	7.86	FAO of United Nations, Rome Chapter - III 2008
20	Cation Exchange Capacity	mEq/100g	2.2	IS 2720 (Part 24) Clause 5 1976
21	Water Holding capacity	%	18.8	IS 14765: 2000
22	Colour	-	Black	HECS-G/ENV/SSW/SOP/011 Issue No.:01 Issue Date:02:07: 2020

Note:- BLQ : Below the Limit of Quantification, LOQ: Limit of Quantification, mg/kg: milligram per kilogram, % - Percentage..

\*\*\*End of Report\*\*\*



D.Anusuya  
Lab Manager  
Authorized Signatory



**Hubert Enviro Care Systems (P) Ltd.**

A-21, III Phase, Thiru Vi Ka Industrial Estate,

Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax : 42985500

E-mail : labsales@hecs.in

**Laboratory Services Division**

(Chemical &amp; Biological Testing)

Recognized by CPCB (MoEF &amp; CC)

BIS, FSSAI Notified Laboratory

ISO 9001, 14001 &amp; 45001 Certified.

**TEST REPORT**

Page : 1 of 1

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Pollution &amp; Environment

Sample Name : Soil

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s.Hubert Enviro care Systems (P) Ltd.

Sample Location : Near Agoor

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method &amp; Plan : ICARDA :2013

Report No. : HECS/PE/024/240325/N

Sample ID No : 240325286

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 1 Kg

S.No.	Test Parameters	Units	Results	Test Method
Discipline : Chemical				
1	Moisture	%	4.23	HECS-G/ENV/SSW/SOP/003 Issue No.:01 Issue Date:02-07-2020
2	Manganese	mg/kg	133.9	HECS-G/INS/SOP/ 042
3	Iron	mg/kg	3.24	Inhouse method
4	Infiltration Rate	-	0.8	Inhouse method

Note:- mg/kg; milligram per kilogram, % - Percentage.

\*\*\*End of Report\*\*\*



D.Anusuya  
Lab Manager  
Authorized Signatory



# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 1 of 2

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Pollution & Environment

Sample Name : Soil

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Near Pelakuppam

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method & Plan : ICARDA :2013

ULR : TC1231025000017088F

Report No. : HECS/PE/025/240325

Sample ID No : 240325287

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 1 Kg

S.No.	Test Parameters	Units	Results	Test Method
Discipline : Chemical				
1	Cadmium	mg/Kg	BLQ (LOQ: 0.1)	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021
2	Chromium	mg/Kg	10.61	HECS-G/INS/SOP/042 Issue No.:01 Issue Date:01.03.2021
3	Copper	mg/Kg	18.45	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021
4	Zinc	mg/kg	15.49	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021
5	Soil Texture	-	Clay	FAO of United Nations, Rome Chapter - III 2008
6	Soil Texture i)Sand	%	20.6	FAO of United Nations, Rome Chapter - III 2008
7	Soil Texture ii)Silt	%	36.8	FAO of United Nations, Rome Chapter - III 2008
8	Soil Texture iii)Clay	%	42.6	FAO of United Nations, Rome Chapter - III 2008
9	pH Value @ 25 ° C (1 : 2.5)	-	6.98	IS 2720 (Part 26) 1987
10	Electrical conductivity @ 25 ° C (1 : 2)	µS/cm	127.3	IS 14767: 2000



D.Anusuya  
Lab Manager  
Authorized Signatory

# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 2 of 2

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Pollution & Environment

Sample Name : Soil

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Near Pelakuppam

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method & Plan : ICARDA :2013

ULR : TC1231025000017088F

Report No. : HECS/PE/025/240325

Sample ID No : 240325287

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 1 Kg

S.No.	Test Parameters	Units	Results	Test Method
11	Bulk Density	gm/cm <sup>3</sup>	0.98	FAO of United Nations Rome 2007
12	Organic Carbon	%	0.38	IS 2720 (Part 22) Section I 1972
13	Organic Matter	%	0.65	IS 2720 (Part 22) Section I 1972
14	Available Phosphorous as P	µg/g	BLQ(LOQ 5.0)	FAO of United Nations, Rome Chapter - III 2008
15	Available Potassium	mEq/100g	24.13	FAO of United Nations, Rome Chapter - III 2008
16	Boron as B	mg/kg	BLQ(LOQ 0.1)	HECS-G/ENV/SSW/SOP/018 Issue No.:01 Issue Date:02:07 2020
17	Total Nitrogen as N	%	0.0103	IS 14684 Clause 4 1999
18	Exchangable Calcium as Ca	mEq/L	3.87	FAO of United Nations, Rome Chapter - III 2008
19	Exchangable Magnesium as Mg	mEq/L	11.62	FAO of United Nations, Rome Chapter - III 2008
20	Cation Exchange Capacity	mEq/100g	1.8	IS 2720 (Part 24) Clause 5 1976
21	Water Holding capacity	%	20.8	IS 14765: 2000
22	Colour	-	Brown	HECS-G/ENV/SSW/SOP/011 Issue No.:01 Issue Date:02:07: 2020

Note:- BLQ : Below the Limit of Quantification, LOQ: Limit of Quantification, mg/kg: milligram per kilogram, % - Percentage..

\*\*\*End of Report\*\*\*



D.Anusuya  
Lab Manager  
Authorized Signatory

**Hubert Enviro Care Systems (P) Ltd.**A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax : 42985500

E-mail : labsales@hecs.in

**Laboratory Services Division**

(Chemical &amp; Biological Testing)

Recognized by CPCB (MoEF &amp; CC)

BIS, FSSAI Notified Laboratory

ISO 9001, 14001 &amp; 45001 Certified.

**TEST REPORT**

Page : 1 of 1

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Pollution &amp; Environment

Sample Name : Soil

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s.Hubert Enviro care Systems (P) Ltd.

Sample Location : Near Pelakuppam

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method &amp; Plan : ICARDA :2013

Report No. : HECS/PE/025/240325/N

Sample ID No : 240325287

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 1 Kg

S.No.	Test Parameters	Units	Results	Test Method
Discipline : Chemical				
1	Moisture	%	3.92	HECS-G/ENV/SSW/SOP/003 Issue No.:01 Issue Date:02:07: 2020
2	Manganese	mg/kg	53.98	HECS-G/INS/SOP/ 042
3	Iron	mg/kg	4.93	Inhouse method
4	Infiltration Rate		0.9	Inhouse method

Note:- mg/kg: milligram per kilogram, % - Percentage.

\*\*\*End of Report\*\*\*



D.Anusuya

Lab Manager

Authorized Signatory



# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 1 of 2

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Pollution & Environment

Sample Name : Soil

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : Near Ural

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method & Plan : ICARDA :2013

ULR : TC1231025000017089F

Report No. : HECS/PE/026/240325

Sample ID No : 240325288

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 1 Kg

S.No.	Test Parameters	Units	Results	Test Method
Discipline : Chemical				
1	Cadmium	mg/Kg	BLQ (LOQ: 0.1)	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021
2	Chromium	mg/Kg	12.72	HECS-G/INS/SOP/042 Issue No.:01 Issue Date:01.03.2021
3	Copper	mg/Kg	8.28	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021
4	Zinc	mg/kg	21.60	HECS-G/INS/SOP/ 042 Issue No.:01 Issue Date:01.03.2021
5	Soil Texture	-	Silty clay loam	FAO of United Nations, Rome Chapter - III 2008
6	Soil Texture i) Sand	%	19.6	FAO of United Nations, Rome Chapter - III 2008
7	Soil Texture ii) Silt	%	52.8	FAO of United Nations, Rome Chapter - III 2008
8	Soil Texture iii) Clay	%	27.6	FAO of United Nations, Rome Chapter - III 2008
9	pH Value @ 25 ° C (1 : 2.5)	-	6.48	IS 2720 (Part 26) 1987
10	Electrical conductivity @ 25 ° C (1 : 2)	µS/cm	189.7	IS 14767: 2000



D. Anusuya  
Lab Manager  
Authorized Signatory



# Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 2 of 2

ULR : TC1231025000017089F  
Report No. : HECS/PE/026/240325  
Sample ID No : 240325288  
Sampling Date : 24/03/2025

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Pollution & Environment

Sample Name : Soil

Sample Mark : NA

Sample Reference : NA

Sample Drawn By : M/s.Hubert Enviro care Systems (P) Ltd.

Sample Location : Near Ural

Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0

Sampling Method & Plan : ICARDA :2013

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 07/04/2025

Report Date : 07/04/2025

Sample quantity : 1 Kg

S.No.	Test Parameters	Units	Results	Test Method
11	Bulk Density	gm/cm <sup>3</sup>	1.00	FAO of United Nations Rome 2007
12	Organic Carbon	%	0.46	IS 2720 (Part 22) Section I 1972
13	Organic Matter	%	0.80	IS 2720 (Part 22) Section I 1972
14	Available Phosphorous as P	µg/g	5.72	FAO of United Nations, Rome Chapter - III 2008
15	Available Potassium	mEq/100g	28.44	FAO of United Nations, Rome Chapter - III 2008
16	Boron as B	mg/kg	BLQ(LOQ 0.1)	HECS-G/ENV/SSW/SOP/018 Issue No.:01 Issue Date:02:07: 2020
17	Total Nitrogen as N	%	0.0153	IS 14684 Clause 4 1999
18	Exchangable Calcium as Ca	mEq/L	11.77	FAO of United Nations, Rome Chapter - III 2008
19	Exchangable Magnesium as Mg	mEq/L	7.84	FAO of United Nations, Rome Chapter - III 2008
20	Cation Exchange Capacity	mEq/100g	2.2	IS 2720 (Part 24) Clause 5 1976
21	Water Holding capacity	%	20.2	IS 14765: 2000
22	Colour	-	Brown	HECS-G/ENV/SSW/SOP/011 Issue No.:01 Issue Date:02:07: 2020

Note:- BLQ - Below the Limit of Quantification, LOQ- Limit of Quantification, mg/kg- Milligrams per kilogram ,  
%- Percentage.

\*\*\*End of Report\*\*\*



D.Anusuya  
Lab Manager  
Authorized Signatory

**Hubert Enviro Care Systems (P) Ltd.**A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.

Ph: 42985555 / 43635555 Fax : 42985500

E-mail : labsales@hecs.in

**Laboratory Services Division**

(Chemical &amp; Biological Testing)

Recognized by CPCB (MoEF &amp; CC)

BIS, FSSAI Notified Laboratory

ISO 9001, 14001 &amp; 45001 Certified.

**TEST REPORT**

Page : 1 of 1

Name of the Client : M/s. SIPCOT  
Address of the Client : Tindivanam  
Group : Pollution & Environment  
Sample Name : Soil  
Sample Mark : NA  
Sample Reference : NA  
Sample Drawn By : M/s.Hubert Enviro care Systems (P) Ltd.  
Sample Location : Near Ural  
Environmental Condition : Temperature (°C) : 28.4 | Humidity (%) : 55.0  
Sampling Method & Plan : ICARDA :2013

Report No. : HECS/PE/026/240325N  
Sample ID No : 240325288  
Sampling Date : 24/03/2025  
Received Date : 24/03/2025  
Commenced Date : 24/03/2025  
Completed On : 07/04/2025  
Report Date : 07/04/2025  
Sample quantity : 1 Kg

S.No.	Test Parameters	Units	Results	Test Method
Discipline : Chemical				
1	Moisture	%	6.34	HECS-G/ENV/SSW/SOP/003 Issue No.:01 Issue Date:02:07: 2020
2	Manganese	mg/kg	117.6	HECS-G/INS/SOP/ 042
3	Iron	mg/kg	6.76	Inhouse method
4	Infiltration Rate	-	1.5	Inhouse method

Note:- mg/kg: milligram per kilogram, % - Percentage.

\*\*\*End of Report\*\*\*



D.Anusuya  
Lab Manager  
Authorized Signatory

## Hubert Enviro Care Systems (P) Ltd.

A-21, III Phase, Thiru Vi Ka Industrial Estate,  
Guindy, Chennai - 600 032.  
Ph: 42985555 / 43635555 Fax : 42985500  
E-mail : labsales@hecs.in



## Laboratory Services Division

(Chemical & Biological Testing)  
Recognized by CPCB (MoEF & CC)  
BIS FSSAI Notified Laboratory  
ISO 9001, 14001 & 45001 Certified.



### TEST REPORT

Page : 1 of 1

Name of the Client : M/s. SIPCOT

Address of the Client : Tindivanam

Group : Atmospheric Pollution

Sample Name : Ambient Noise Levels (Excluding vibration)

Sample Mark : Noise

Sample Reference : NA

Sample Drawn By : M/s. Hubert Enviro care Systems (P) Ltd.

Sample Location : NA

Environmental Condition : Temperature (°C) : 31.8 | Humidity (%) : 55.0

Sampling Method & Plan : IS 9989:1981

ULR : TC1231025000016540F

Report No. : HECS/AP/091/240325

Sample ID No : 240325277

Sampling Date : 24/03/2025

Received Date : 24/03/2025

Commenced Date : 24/03/2025

Completed On : 04/04/2025

Report Date : 05/04/2025

Sample quantity : NA

S.No	Sampling Location	Day Noise level in dB (A)	Night Noise level in dB (A)
1	Project Site	54.6	43.2
2	Botheri	55.8	44.9
3	Agoor	54.7	45.3
4	Pelakuppam	53.6	44.5
5	Ural	49.5	40.6

#### Noise Standards - CPCB:

- |      |                  |                       |                       |
|------|------------------|-----------------------|-----------------------|
| i.   | Industrial Area  | : Day Time-75 dB (A); | Night Time-70 dB (A). |
| ii.  | Commercial Area  | : Day Time-65 dB (A); | Night Time-55 dB (A). |
| iii. | Residential Area | : Day Time-55 dB (A); | Night Time-45 dB (A). |
| iv.  | Silence Zone     | : Day Time-50 dB (A); | Night Time-40 dB (A). |

**Note:** 1. Day Time shall mean from 6.00 am to 10.00 pm.

2. Night Time shall mean from 10.00 pm to 6.00 am.

Remarks:- The noise level meets the requirement of CPCB Limit

\*\*\*End of Report\*\*\*



D.Anusuya  
Lab Manager  
Authorized Signatory



## SIPCOT- THINDIVANAM MONITORING PHOTOGRAPHS

### AMBIENT AIR QUALITY MONITORING PHOTOGRAPH

PROJECT AREA



URAL



BUDERI





## PELLAKUPPAM



## AGOOR





## NOISE MONITORING PHOTOGRAPH

### PROJECT AREA






### BUDERI



URAL	PELLAKUPPAM
 <p>Ural, Tamil Nadu, India 79°41'51" Long, Tamil Nadu 604001, India Lat 12.242788° Long 78.697889° 24/03/2025 03:19 PM GMT +05:30</p>	 <p>Palakuppam, Tamil Nadu, I... 89°45', Palakuppam, Tamil Nadu 604001, India Lat 12.241019° Long 79.622617° 24/03/2025 04:14 PM GMT +05:30</p>
AGOOR	
 <p>Agar, Tamil Nadu, India 79°42', Velmanku Patti - Madan Road, Agar, Tamil Nadu 604001, India Lat 12.277800° Long 78.698817° 24/03/2025 11:53 AM GMT +05:30</p>	

## SOIL SAMPLING PHOTOGRAPH

PROJECT AREA	BUDERI
 <p>Tindivanam, Tamil Nadu, ... 22, Gingee Rd, Rocharai, Tindivanam, Tamil Nadu 604001, India Lat 12.250008° Long 79.62687° 24/03/2025 10:31 AM GMT +05:30 2848</p>	 <p>Tindivanam, Tamil Nadu, ... 3/2, Tindivanam, Tamil Nadu 604307, India Lat 12.225736° Long 79.63461° 24/03/2025 06:30 PM GMT +05:30 2849</p>

URAL	PELLAKUPPAM
 <p>GPS Map Camera Ural, Tamil Nadu, India Tahsil, Ural, Tamil Nadu 604001, India Lat 12.262124° Long 79.628022° 24/03/2025 03:12 PM GMT +05:30</p>	 <p>GPS Map Camera Palakuppam, Tamil Nadu, I... Rajagopal, Palakuppam, Tamil Nadu 604001, India Lat 12.241244° Long 79.628042° 24/03/2025 04:18 PM GMT +05:30</p>
AGOOR	
 <p>GPS Map Camera Agar, Tamil Nadu, India Thiruvazhi, Mahanadu Panna - Mahan Road, Agar, Tamil Nadu 604001, India Lat 12.277782° Long 79.658861° 24/03/2025 11:54 AM GMT +05:30</p>	

## GROUND WATER SAMPLING PHOTOGRAPH

PROJECT AREA	PELLAKUPPAM
 <p>GPS Map Camera Viluppuram, Tamil Nadu, ... Tamil Nadu 604001, India, Viluppuram, Tamil Nadu 604001, India Lat 12.246948° Long 79.625939° 24/03/2025 10:58 AM GMT +05:30 2667</p>	 <p>GPS Map Camera Palakuppam, Tamil Nadu, I... Rajagopal, Palakuppam, Tamil Nadu 604001, India Lat 12.241202° Long 79.628192° 24/03/2025 04:07 PM GMT +05:30</p>



## BUDERI



## SURFACE WATER SAMPLING PHOTOGRAPH

### BOTHERI LAKE



### LAKE NEAR VIZHUKKAM





**Environmental Clearance for SIPCOT Thindivanam**  
**Published in "Deccan Chronicle" Chennai Edition dated 05.01.2020 in**  
**English Language**

● **Blogger Pradeep John, also called the 'Tamil Nadu weatherman', wrote on his Facebook post that the fog in the city was not due to pollution. "It's not like the smog that happened in November." He said the fog will continue for the next 2-3 days.**

Chennai airport authorities pointed out on its Twitter handle that, "due to adverse weather conditions/poor visibility, flights are diverted/delayed. The inconvenience caused to passengers is sincerely regretted. Passengers are requested to check with the concerned airline (s) for further updates." The airlines also updated the passengers about the flight delays and apologised to the passengers.

A blanket of fog covered most parts of the city till 8.30 am on Saturday disrupting vehicular movement.

Ooty, Jan 4: The district court here on Saturday granted a three-day parole to Valayar Manoj, one of the accused in the Kodanadu estate, murder and heist cases, to perform the last rites of his father who expired two days ago in Kerala.

As the petition for parole came up for hearing, district judge P. Vadamalai gave the parole to Valayar Manoj and directed that be produced

before court on January 7.

Manoj is one of the 10 accused in the murder of a security guard and heist in the bungalow in Kodanadu belonging to late Tamil Nadu chief minister Jayalalithaa and lodged in the Central jail here.

His counsel had filed a petition seeking parole to Manoj to perform the last rites of his father who died two days ago in Thrissur, Kerala. —PTI



**STATE INDUSTRIES PROMOTION CORPORATION OF TAMILNADU LIMITED**  
**SIPCOT INDUSTRIAL PARK, THINDIVANAM**  
**THINDIVANAM TALUK, VILLUPURAM DISTRICT**

**ENVIRONMENTAL CLEARANCE**

Environmental Clearance has been obtained for the proposed SIPCOT Industrial Park at Thindivanam, Villupuram District from State Level Environment Impact Assessment Authority (SEIAA), Tamil Nadu vide their Lr.No.SEIAA-TN/F.6497/EC/8(b)/681/2019 dt.27.11.2019.

The contents of the Environmental Clearance can be downloaded from SIPCOT website [www.sipcot.in](http://www.sipcot.in) and also in the SEIAA website [www.seiaa.tn.gov.in](http://www.seiaa.tn.gov.in). Further the copies of the Environmental clearance could be obtained from the Head office of SIPCOT.

**MANAGING DIRECTOR**  
**SIPCOT**

19-A, RUKMANI LAKSHMIPATHY ROAD,  
 EGMORE, CHENNAI-8

DIPR/24/DISPLAY/2020



**TAMIL NADU COMMON ENTRANCE TEST (TANCET) 2020**

**FOR M.B.A., M.C.A., & M.E./M.Tech./M.Arch./M.Plan. DEGREE PROGRAMMES**

**ANNA UNIVERSITY, CHENNAI - 600 025**



Applications for Tamil Nadu Common Entrance Test (TANCET) 2020 conducted by Anna University, Chennai on behalf of the Government of Tamil Nadu from candidates who seek admission to 1. M.B.A., 2. M.C.A. and 3. M.E. / M.Tech. / M.Arch. / M.Plan. Degree Programmes for the academic year 2020 – 2021 offered at University Departments,

**Environmental Clearance for SIPCOT Tindivanam**  
**Published in "Dinamani" Villupuram Edition dated 05.01.2020**  
**in Tamil Language**

யாழ்ப்பாணம்  
 ல் உள்ள தனி  
 விசை பெற்று  
 சனிக்கிழமை  
 அவருக்கு அர

ணாநகரில் உள்ள அவரின் இல்லத்தில்  
 இருந்து பிற்பகல் 3 மணிளவில் உடல்  
 எடுத்துச் செல்லப்பட்டு, கீழ்ப்பாக்கம் கல்  
 லறை தோட்டத்தில் நல்லடக்கம் செய்யப்  
 பட்டவுள்ளது.

வும் பணியாற்றி அவர் வரலாற்றின் பக்கங்க  
 ளில் இடம்பெறுவார். அவரதுமறைவு அதி  
 முகவுக்கு ஈடுசெய்ய முடியாத இழப்பு என  
 அறிக்கையில் தெரிவிக்கப்பட்டுள்ளது.

**இந்தியா (இலா) லிமிடெட்**  
**IREL (INDIA) LIMITED**  
 ரூபி ல் (இலா) லிமிடெட்  
**INDIAN RARE EARTHS LIMITED**  
 காரைக்கல் 605 008 / A Govt. of India Undertaking  
 காரைக்கல் / MANAVALLAKURU (C.B.) - 605 252  
 Kanyakumari District, கன்னியாகுமரி, Tamil Nadu  
 (049551) 227255-257, 258 / Fax : (049551) 227220  
 eil : indianrareearths@irel.in Website : http://irel.co.in  
 (ISO 9001, ISO 14001, OHSAS 18001 Certified Unit)

04-01-2020

reliable and capable contractor firms for the following work  
 against the numbers mentioned below:

**அவ் பிராண்டர் லா கிரைவர்**  
**Hiring of Front End Loader**

[enquiries@irel.co.in](mailto:enquiries@irel.co.in), [www.irel.co.in](http://www.irel.co.in) (CP)  
 if any will be hosted in the above websites only

Sd/-  
 Chief Manager (Purchase)

**STATE INDUSTRIES PROMOTION CORPORATION OF TAMILNADU LIMITED**  
 19-A, RUKMANI LAKSHMI PATHY ROAD, EGMORE, CHENNAI - 600 008.  
 CIN U74999TN19735GC005967

**Tender Cancellation Notice**

The Tenders called for, in this office Tender Notice No. NIT.No. 32/CW/  
 DO/T.No.48 & 49/2019-20, Dt.28.11.2019 for the following works are  
 hereby **Cancelled** due to Administrative reasons.

"1. Interior fitout work for Industrial Innovation Centre for SIPCOT at  
 Hosur in Krishnagiri District.  
 "2. Interior fitout work for Industrial Innovation Centre for SIPCOT at  
 Sriperumbudur in Kancheepuram District."

DI/PR/24/TENDER/2020 SUPERINTENDING ENGINEER

**பு பல்கலைக்கழகம்**

**நதயுள்ள அறிவிப்பு**

கல்வியில் மேம்பாட்டும் கிராமப்புறங்கள் கணிதத்  
 தேவையுடனும் மற்றும் தரமான வளங்களுக்கிட  
 மற்கொள்வதற்கான லாப முத்திரைகளைப் பட்ட  
 லுப்பற்ற விரைவில் பங்கு கிடைக்கப்பட்டுள்ள  
 து விரைவில் பங்கு கிடைக்கப்பட்டு பதிவாளர்  
 கிடைக்க (இரு கிடைக்கப்பட்டு)

: 05.01.2020  
 : 09.01.2020 மாலை 3.00 மணி

கலை  
 உடல் நடை: 21.01.2020 மாலை 3.00 மணி வரை  
 கலை  
 : 21.01.2020 மாலை 4.00 மணி

0

விலை: 4724 / பிடிப்புகள் / 2019 பதிவாளர்

**தமிழ்நாடு தொழில் முன்னேற்ற நிறுவனம்**  
**சிப்காட் தொழிற் பூங்கா, திண்டிவனம்**  
 திண்டிவனம் தாலுகா, விழுப்புரம் மாவட்டம்.

**சுற்றுச்சூழல் இசைவாணை**

மாநில சுற்றுச்சூழல் தாக்க மதிப்பீட்டு ஆணையம், தமிழ்நாடு சமூக  
 ள் Lr.No.SEIAA-TN/F.6497/EC/8(b)/681/2019 தேதி 27.11.2019  
 மூலம் விழுப்புரம் மாவட்டம், மேல்குப்பம், பெண்ணையத்தூர் மற்றும்  
 செல்வம் கிராமங்களில் அமைக்கப்பட்டுள்ள தொழிற் பூங்காவிற்கு  
 சுற்றுச்சூழல் இசைவாணை வழங்கியுள்ளது.

சுற்றுச்சூழல் இயல்பிசைவாணையின் முடிவின்படி களை  
 சிப்காட் இணையதளமான [www.sipcot.com](http://www.sipcot.com) மற்றும் மாநில  
 சுற்றுச்சூழல் தாக்க மதிப்பீட்டு ஆணையத்தின் இணையதளமான  
[www.seiaa.tn.gov.in](http://www.seiaa.tn.gov.in) ஆகியவற்றில் பதிவிறக்கம் செய்து கொள்ளலாம்.  
 மேலும் இயல்பிசைவாணையின் நகலினை இயல்பிசைவாணைத் தி  
 பெற்றுக்கொள்ளலாம்.

மேலாண்மை இயக்குநர்  
 சிப்காட்

19- அ. ருத்மணி இலட்சுமிபதி ளைவ,  
 எழுப்பூர், சென்னை-600 008.

செ.பி.டி.டி/சுற்றுச்சூழல்/0020

**இந்தியன் ஓவர்சீஸ் வங்கி, மண்டல அலுவலகம், திருச்சி.**

**அசையும் / அசையா சொத்துக்கள் விற்பனை செய்வதற்கான விற்பனை அறிவிப்பு**

(இணைய தளம் (அணைக்கம்) விதிகளை விதி 8 (6) நிபந்தனையின் கீழ்) உடனிட சொத்துக்கள் விற்பனைக்குரிய வதும்  
 நிதி சொத்துக்களை விற்பனைக்குரிய உடனிட சொத்துக்கள் விற்பனை உடனிட அணைக்கம் உடனிட, 2002, இணைய தளம் (அணைக்கம்) விதிக்  
 2002-ல் விதி 6(2) மற்றும் 8(6) உடனிட கீழ், அசையும் / அசையா சொத்துக்களின் விற்பனைக்கான பின்புறம் லா விற்பனை அறிவிப்பு  
 இவ் லாப லாபம் உடனிட மற்றும் உத்தரவாதமற்றவர்கள் மற்றும் மேலாண்மைக்குத் தெரிவித்து என்னவென்றால், உடனிட  
 வதற்கு வங்கியால் விற்பனைத்திற்ப்புள்ள / அடமைய வங்கியுடனிட / லாபவங்கியுடனிட கீழ் வங்கியுடனிட ஆணையர் சொத்தானது.  
 இந்தியன் ஓவர்சீஸ் வங்கியின் (உடனிட வங்கியின்) அங்கீகரிக்கப்பட்ட அதிகாரியால் ஆக்கழிவ வங்கியை செய்து வங்கியுடனிட.  
 கீழ் குறிப்பிடப்பட்டுள்ள உத்தரவாதம் / உத்தரவாதமற்றவர்கள் ஆகியவர்களுக்கு உடனிட வங்கியை வங்கியுடனிட கீழ்



Projects/Thindivanam/2019

Date:05.02.2020

The Deputy Director General of Forests (C),  
Ministry of Environment, Forest and Climate Change,  
Regional Office (SEZ), Ist and IInd Floor,  
Handloom Export Promotion Council, 34, Cathedral Garden Road,  
Nungambakkam, Chennai - 600 034

/RPAD/

Sir,

Sub: SIPCOT Industrial Park, Thindivanam - Submission of copy of the  
press release for issue of Environmental Clearance from SEIAA -  
Forwarded - Reg.


Ref: SEIAA EC Letter No. SEIAA-TN/F. 6497/EC/8(b)/681/2019 dated  
27.11.2019.

\*\*\*\*\*

With reference to the above, we have obtained Environmental Clearance  
(EC) from SEIAA. As per EC condition, the advertisement regarding issue of  
Environment Clearance for SIPCOT Industrial Park at Thindivanam has been  
released in 'Deccan Chronicle' Chennai edition dated 05.01.2020 in English  
language and 'Dinamani' Villupuram edition dated 05.01.2020 in Tamil  
Language.

The copy of both the press release has been enclosed here with for your  
kind perusal.

Yours Faithfully,

  
GENERAL MANAGER (P-II)i/c

Encl.: as above



Projects/Thindivanam/2019

Date:05.02.2020

The Member Secretary,  
State Level Environmental Impact Assessment Authority,  
3rd Floor, Panagal Maligai,  
No.1. Jeenis Road,  
Saidapet, Chennai - 600 015.

/RPAD/

Sir,

Sub: SIPCOT Industrial Park, Thindivanam - Submission of copy of the  
press release for issue of Environmental Clearance from SEIAA -  
Forwarded - Reg.


Ref: SEIAA EC Letter No. SEIAA-TN/F. 6497/EC/8(b)/681/2019 dated  
27.11.2019.

\*\*\*\*\*

With reference to the above, we have obtained Environmental Clearance  
(EC) from SEIAA. As per EC condition, the advertisement regarding issue of  
Environment Clearance for SIPCOT Industrial Park at Thindivanam has been  
released in 'Deccan Chronicle' Chennai edition dated 05.01.2020 in English  
language and 'Dinamani' Villupuram edition dated 05.01.2020 in Tamil  
Language.

The copy of both the press release has been enclosed here with for your  
kind perusal.

Yours Faithfully,

  
GENERAL MANAGER (P-II)i/c

Encl.: as above





**Environmental Clearance for SIPCOT Thindivanam**  
**Published in "Deccan Chronicle" Chennai Edition dated 05.01.2020 in**  
**English Language**

● **Blogger Pradeep John, also called the 'Tamil Nadu weatherman', wrote on his Facebook post that the fog in the city was not due to pollution. "It's not like the smog that happened in November." He said the fog will continue for the next 2-3 days.**

Chennai airport authorities pointed out on its Twitter handle that, "due to adverse weather conditions/poor visibility, flights are diverted/delayed. The inconvenience caused to passengers is sincerely regretted. Passengers are requested to check with the concerned airline (s) for further updates." The airlines also updated the passengers about the flight delays and apologised to the passengers.

A blanket of fog covered most parts of the city till 8.30 am on Saturday disrupting vehicular movement.

Ooty, Jan 4: The district court here on Saturday granted a three-day parole to Valayar Manoj, one of the accused in the Kodanadu estate, murder and heist cases, to perform the last rites of his father who expired two days ago in Kerala.

As the petition for parole came up for hearing, district judge P. Vadimalai gave the parole to Valayar Manoj and directed that be produced

before court on January 7.

Manoj is one of the 10 accused in the murder of a security guard and heist in the bungalow in Kodanadu belonging to late Tamil Nadu chief minister Jayalalithaa and lodged in the Central jail here.

His counsel had filed a petition seeking parole to Manoj to perform the last rites of his father who died two days ago in Thrissur, Kerala. —PTI



**STATE INDUSTRIES PROMOTION CORPORATION OF TAMILNADU LIMITED**  
**SIPCOT INDUSTRIAL PARK, THINDIVANAM**  
**THINDIVANAM TALUK, VILLUPURAM DISTRICT**

**ENVIRONMENTAL CLEARANCE**

Environmental Clearance has been obtained for the proposed SIPCOT Industrial Park at Thindivanam, Villupuram District from State Level Environment Impact Assessment Authority (SEIAA), Tamil Nadu vide their Lr.No.SEIAA-TN/F.6497/EC/8(b)/681/2019 dt.27.11.2019.

The contents of the Environmental Clearance can be downloaded from SIPCOT website [www.sipcot.in](http://www.sipcot.in) and also in the SEIAA website [www.seiaa.tn.gov.in](http://www.seiaa.tn.gov.in). Further the copies of the Environmental clearance could be obtained from the Head office of SIPCOT.

**MANAGING DIRECTOR**  
**SIPCOT**

19-A, RUKMANI LAKSHMIPATHY ROAD,  
 EGMORE, CHENNAI-8

DIPR/24/DISPLAY/2020



**TAMIL NADU COMMON ENTRANCE TEST (TANCET) 2020**

**FOR M.B.A., M.C.A., & M.E./M.Tech./M.Arch./M.Plan. DEGREE PROGRAMMES**

**ANNA UNIVERSITY, CHENNAI - 600 025**



Applications for Tamil Nadu Common Entrance Test (TANCET) 2020 conducted by Anna University, Chennai on behalf of the Government of Tamil Nadu from candidates who seek admission to **1. M.B.A., 2. M.C.A. and 3. M.E. / M.Tech. / M.Arch. / M.Plan. Degree Programmes** for the academic year 2020 – 2021 offered at University Departments,

**Environmental Clearance for SIPCOT Tindivanam**  
**Published in "Dinamani" Villupuram Edition dated 05.01.2020**  
**in Tamil Language**

யாவதென்பதில் உள்ள தனி விசை பெற்று சமீக்கிழமை அவருக்கு அர

ணாநகரில் உள்ள அவரின் இல்லத்தில் இருந்து பிற்பகல் 3 மணிபளவில் உடல் எடுத்துச் செல்லப்பட்டு, கீழ்ப்பாக்கம் கல்வறை தோட்டத்தில் நல்லடக்கம் செய்யப் படவுள்ளது.

வும் பணியாற்றி அவர் வரலாற்றின் பக்கங்களில் இடம்பெறுவார். அவரது மறைவு அதிமுகவுக்கு ஈடுசெய்ய முடியாத இழப்பு என அறிக்கையில் தெரிவிக்கப்பட்டுள்ளது.

**இந்தியா லிமிடெட்**  
**IREL (INDIA) LIMITED**  
 (புதிதான இந்தியா லிமிடெட்)  
**INDIAN RARE EARTHS LIMITED**  
 100, 101, 102, 103, 104, 105, 106, 107, 108, 109, 110, 111, 112, 113, 114, 115, 116, 117, 118, 119, 120, 121, 122, 123, 124, 125, 126, 127, 128, 129, 130, 131, 132, 133, 134, 135, 136, 137, 138, 139, 140, 141, 142, 143, 144, 145, 146, 147, 148, 149, 150, 151, 152, 153, 154, 155, 156, 157, 158, 159, 160, 161, 162, 163, 164, 165, 166, 167, 168, 169, 170, 171, 172, 173, 174, 175, 176, 177, 178, 179, 180, 181, 182, 183, 184, 185, 186, 187, 188, 189, 190, 191, 192, 193, 194, 195, 196, 197, 198, 199, 200, 201, 202, 203, 204, 205, 206, 207, 208, 209, 210, 211, 212, 213, 214, 215, 216, 217, 218, 219, 220, 221, 222, 223, 224, 225, 226, 227, 228, 229, 230, 231, 232, 233, 234, 235, 236, 237, 238, 239, 240, 241, 242, 243, 244, 245, 246, 247, 248, 249, 250, 251, 252, 253, 254, 255, 256, 257, 258, 259, 260, 261, 262, 263, 264, 265, 266, 267, 268, 269, 270, 271, 272, 273, 274, 275, 276, 277, 278, 279, 280, 281, 282, 283, 284, 285, 286, 287, 288, 289, 290, 291, 292, 293, 294, 295, 296, 297, 298, 299, 300, 301, 302, 303, 304, 305, 306, 307, 308, 309, 310, 311, 312, 313, 314, 315, 316, 317, 318, 319, 320, 321, 322, 323, 324, 325, 326, 327, 328, 329, 330, 331, 332, 333, 334, 335, 336, 337, 338, 339, 340, 341, 342, 343, 344, 345, 346, 347, 348, 349, 350, 351, 352, 353, 354, 355, 356, 357, 358, 359, 360, 361, 362, 363, 364, 365, 366, 367, 368, 369, 370, 371, 372, 373, 374, 375, 376, 377, 378, 379, 380, 381, 382, 383, 384, 385, 386, 387, 388, 389, 390, 391, 392, 393, 394, 395, 396, 397, 398, 399, 400, 401, 402, 403, 404, 405, 406, 407, 408, 409, 410, 411, 412, 413, 414, 415, 416, 417, 418, 419, 420, 421, 422, 423, 424, 425, 426, 427, 428, 429, 430, 431, 432, 433, 434, 435, 436, 437, 438, 439, 440, 441, 442, 443, 444, 445, 446, 447, 448, 449, 450, 451, 452, 453, 454, 455, 456, 457, 458, 459, 460, 461, 462, 463, 464, 465, 466, 467, 468, 469, 470, 471, 472, 473, 474, 475, 476, 477, 478, 479, 480, 481, 482, 483, 484, 485, 486, 487, 488, 489, 490, 491, 492, 493, 494, 495, 496, 497, 498, 499, 500, 501, 502, 503, 504, 505, 506, 507, 508, 509, 510, 511, 512, 513, 514, 515, 516, 517, 518, 519, 520, 521, 522, 523, 524, 525, 526, 527, 528, 529, 530, 531, 532, 533, 534, 535, 536, 537, 538, 539, 540, 541, 542, 543, 544, 545, 546, 547, 548, 549, 550, 551, 552, 553, 554, 555, 556, 557, 558, 559, 560, 561, 562, 563, 564, 565, 566, 567, 568, 569, 570, 571, 572, 573, 574, 575, 576, 577, 578, 579, 580, 581, 582, 583, 584, 585, 586, 587, 588, 589, 590, 591, 592, 593, 594, 595, 596, 597, 598, 599, 600, 601, 602, 603, 604, 605, 606, 607, 608, 609, 610, 611, 612, 613, 614, 615, 616, 617, 618, 619, 620, 621, 622, 623, 624, 625, 626, 627, 628, 629, 630, 631, 632, 633, 634, 635, 636, 637, 638, 639, 640, 641, 642, 643, 644, 645, 646, 647, 648, 649, 650, 651, 652, 653, 654, 655, 656, 657, 658, 659, 660, 661, 662, 663, 664, 665, 666, 667, 668, 669, 670, 671, 672, 673, 674, 675, 676, 677, 678, 679, 680, 681, 682, 683, 684, 685, 686, 687, 688, 689, 690, 691, 692, 693, 694, 695, 696, 697, 698, 699, 700, 701, 702, 703, 704, 705, 706, 707, 708, 709, 710, 711, 712, 713, 714, 715, 716, 717, 718, 719, 720, 721, 722, 723, 724, 725, 726, 727, 728, 729, 730, 731, 732, 733, 734, 735, 736, 737, 738, 739, 740, 741, 742, 743, 744, 745, 746, 747, 748, 749, 750, 751, 752, 753, 754, 755, 756, 757, 758, 759, 760, 761, 762, 763, 764, 765, 766, 767, 768, 769, 770, 771, 772, 773, 774, 775, 776, 777, 778, 779, 780, 781, 782, 783, 784, 785, 786, 787, 788, 789, 790, 791, 792, 793, 794, 795, 796, 797, 798, 799, 800, 801, 802, 803, 804, 805, 806, 807, 808, 809, 810, 811, 812, 813, 814, 815, 816, 817, 818, 819, 820, 821, 822, 823, 824, 825, 826, 827, 828, 829, 830, 831, 832, 833, 834, 835, 836, 837, 838, 839, 840, 841, 842, 843, 844, 845, 846, 847, 848, 849, 850, 851, 852, 853, 854, 855, 856, 857, 858, 859, 860, 861, 862, 863, 864, 865, 866, 867, 868, 869, 870, 871, 872, 873, 874, 875, 876, 877, 878, 879, 880, 881, 882, 883, 884, 885, 886, 887, 888, 889, 890, 891, 892, 893, 894, 895, 896, 897, 898, 899, 900, 901, 902, 903, 904, 905, 906, 907, 908, 909, 910, 911, 912, 913, 914, 915, 916, 917, 918, 919, 920, 921, 922, 923, 924, 925, 926, 927, 928, 929, 930, 931, 932, 933, 934, 935, 936, 937, 938, 939, 940, 941, 942, 943, 944, 945, 946, 947, 948, 949, 950, 951, 952, 953, 954, 955, 956, 957, 958, 959, 960, 961, 962, 963, 964, 965, 966, 967, 968, 969, 970, 971, 972, 973, 974, 975, 976, 977, 978, 979, 980, 981, 982, 983, 984, 985, 986, 987, 988, 989, 990, 991, 992, 993, 994, 995, 996, 997, 998, 999, 1000.

**STATE INDUSTRIES PROMOTION CORPORATION OF TAMILNADU LIMITED**  
 19-A, RUKMANI LAKSHMI PATHY ROAD, EGMORE, CHENNAI - 600 008.  
 CIN U74999TN1971SGC005967

**Tender Cancellation Notice**  
 The Tenders called for, in this office Tender Notice No. NIT.No. 32/CW/DO/T.No.48 & 49/2019-20, Dt.28.11.2019 for the following works are hereby Cancelled due to Administrative reasons.

"1. Interior fitout work for Industrial Innovation Centre for SIPCOT at Hosur in Krishnagiri District.  
 "2. Interior fitout work for Industrial Innovation Centre for SIPCOT at Sriperumbudur in Kancheepuram District."

DI/PR/24/TENDER/2020 **SUPERINTENDING ENGINEER**

## புதுப்பலகைக்கழகம்

### நதப்பள்ளி அறிவிப்பு

கழகத்தில் வேலாக்கம், கிராமத்துகள் கணத்தினை சேர்த்துப் பற்றும் தரமான வளங்களைக் கண்டறிவதற்கான பணியை மேற்கொண்டு வருகிறது. மேலும், கிராமத்துகள் கணத்தினை சேர்த்துப் பற்றும் தரமான வளங்களைக் கண்டறிவதற்கான பணியை மேற்கொண்டு வருகிறது. மேலும், கிராமத்துகள் கணத்தினை சேர்த்துப் பற்றும் தரமான வளங்களைக் கண்டறிவதற்கான பணியை மேற்கொண்டு வருகிறது.

: 05.01.2020

: 09.01.2020 மாலை 3.00 மணி

கலை

உச்சி நடை: 21.01.2020 மாலை 3.00 மணி வரை

கள்

: 21.01.2020 மாலை 4.00 மணி

0

வழி: 4724 புதுப்பலகை/2020

புதுப்பலகை

வழி: 4724

வழி: 4724



வழி: 4724

## இந்தியன் ஒவார்சீஸ் வாங்கி, மண்டல அலுவலகம், திருச்சி.

### அசையும் / அசையா சொத்துக்கள் விற்பனை செய்வதற்கான விற்பனை அறிவிப்பு

(மேலேயுள்ள அசையும் / அசையா சொத்துக்கள் விற்பனை செய்வதற்கான விற்பனை அறிவிப்பு) உடனடி சொத்துக்கள் விற்பனைக்குரிய பற்றும் தரமான வளங்களைக் கண்டறிவதற்கான பணியை மேற்கொண்டு வருகிறது. மேலும், கிராமத்துகள் கணத்தினை சேர்த்துப் பற்றும் தரமான வளங்களைக் கண்டறிவதற்கான பணியை மேற்கொண்டு வருகிறது. மேலும், கிராமத்துகள் கணத்தினை சேர்த்துப் பற்றும் தரமான வளங்களைக் கண்டறிவதற்கான பணியை மேற்கொண்டு வருகிறது.



1261

**Annexure 8 A**

Projects/Thindivanam/2019

Date: 05.02.2020

The President,  
Venmaniyathur Village Panchayat,  
Thindivanam Taluka,  
Villupuram District,  
Tamil Nadu

Sir,

Sub: SIPCOT Industrial Park, Thindivanam – Submission of copy of the press release for issue of Environmental Clearance from SEIAA – Forwarded - Reg.

Ref: SEIAA EC Letter No. SEIAA-TN/F. 6497/EC/8(b)/681/2019 dated 27.11.2019.

\*\*\*\*\*

With reference to the above, we have obtained Environmental Clearance (EC) for SIPCOT Industrial Park at Pelakuppam, Venmaniyathur, Kollar Village, Thindivanam Taluka, Villupuram District, Tamil Nadu from SEIAA. The copy of Environmental Clearance has been enclosed here with for your kind perusal.

Yours Faithfully,

  
GENERAL MANAGER (P-II)i/c

Encl.: as above

Copy to:

Project Officer, SIP - Cuddalore

- To hand over a copy of the Environmental Clearance to the above panchayat with due acknowledgement and send a report to H.O.





Projects/Thindivanam/2019

Date: 05.02.2020

The President,  
Pelakuppam Village Panchayat,  
Thindivanam Taluka,  
Villupuram District,  
Tamil Nadu

Sir,


Sub: SIPCOT Industrial Park, Thindivanam - Submission of copy of the press release for issue of Environmental Clearance from SEIAA - Forwarded - Reg.

Ref: SEIAA EC Letter No. SEIAA-TN/F. 6497/EC/8(b)/681/2019 dated 27.11.2019.

\*\*\*\*\*

With reference to the above, we have obtained Environmental Clearance (EC) for SIPCOT Industrial Park at Pelakuppam, Venmaniyathur, Kollar Village, Thindivanam Taluka, Villupuram District, Tamil Nadu from SEIAA. The copy of Environmental Clearance has been enclosed here with for your kind perusal.

Yours Faithfully,

  
GENERAL MANAGER (P-II)i/c

Encl.: as above

Copy to:

Project Officer, SIP - Cuddalore

- To hand over a copy of the Environmental Clearance to the above panchayat with due acknowledgement and send a report to H.O.



Projects/Thindivanam/2019

Date: 05.02.2020

The President,  
Kollar Village Panchayat,  
Thindivanam Taluka,  
Villupuram District,  
Tamil Nadu

Sir,


Sub: SIPCOT Industrial Park, Thindivanam - Submission of copy of the press release for issue of Environmental Clearance from SEIAA - Forwarded - Reg.

Ref: SEIAA EC Letter No. SEIAA-TN/F. 6497/EC/8(b)/681/2019 dated 27.11.2019.

\*\*\*\*\*

With reference to the above, we have obtained Environmental Clearance (EC) for SIPCOT Industrial Park at Pelakuppam, Venmaniyathur, Kollar Village, Thindivanam Taluka, Villupuram District, Tamil Nadu from SEIAA. The copy of Environmental Clearance has been enclosed here with for your kind perusal.

Yours Faithfully,

  
GENERAL MANAGER (P-II)i/c

Encl.: as above

Copy to:

Project Officer, SIP - Cuddalore -

To hand over a copy of the Environmental Clearance to the above panchayat with due acknowledgement and send a report to H.O.



WhatsApp

SIPCOT

Annexure - 8 B

←

→

↻

🔍 sipcotweb.tn.gov.in/Environment\_clearance

☆

👤

⋮

Home

About Us

Why SIPCOT ?

Land Information

Industrial Parks

Resources

Tenders


Logins

Contact Us

ENVIRONMENTAL CLEARANCE

S.NO.	NAME OF THE COMPLEX/ PARK / GROWTH CENTRE	NAME OF THE DISTRICT	ENVIRONMENTAL CLEARANCE
22	Pillaipakkam	Kancheepuram	📄 Download
23	Vallam Vadagal – I	Kancheepuram	📄 Download
24	Aerospace Park	Kancheepuram	📄 Download
25	Vallam Vadagal – II	Kancheepuram	📄 Download
26	Manaparai	Tiruchirappalli	📄 Download
27	Tindivanam	Villupuram	📄 Download
28	Manallur	Thiruvallur	📄 Download

ENQUIRE NOW



SIPCOT

Govt. of Tamilnadu

Newsletter

Mandatories

Map

📄 Public Food Shelter

🔍 Search

📖

📧

📁

🌐

📷

🎨

📄

🔍

🖼️

ENG

IN

📶

🔊

🔋

16:17

23-04-2024

🔔

PRE



Inbox (3) - consent@hecs.in - HT X WhatsApp SIPCOT - State Industries Promo X

sipcotweb.tn.gov.in/Compliance\_Report

Home About Us Why SIPCOT ? Land Information Industrial Parks Special Projects Tenders Resources Logins Contact Us

## COMPLIANCE REPORTS

S.NO.	TITLE	DOWNLOAD
1	Compliance Report - Thervoy Kandigai for Dec 2024	Download
2	Compliance Report - Pillaipakkam for Dec 2024	Download
3	Compliance Report - Vallam Vadagal I for Dec 2024	Download
4	Compliance Report - Vaipur Mathur for Dec 2024	Download
5	Compliance Report - Aerospace Park for December 2024	Download
6	Compliance Report - Cheyyar for December 2024	Download
7	Compliance Report - Manaparai for December 2024	Download
8	Compliance Report - Tindivanam for December 2024	Download
9	Compliance Report - Manallur for December 2024	Download
10	Compliance Report - Vallam Vadagal II for Dec 2024	Download
11	Compliance Report - Thoothukudi for December 2024	Download
12	Compliance Report - Nemili for Dec 2024	Download
13	Compliance Report - Mambakkam for Dec 2024	Download
14	Compliance Report - Marudhandapalli for Dec 2024	Download
15	Compliance Report - Theni for Dec 2024	Download

ENQUIRE NOW

17:06 07-04-2025

**SIPCOT**

I/173639/2024

Date: 26-09-2024

To,  
The Member Secretary,  
Tamil Nadu Pollution Control Board,  
No.76, Mount Salai, Guindy,  
Chennai - 600 032.

Sir,

Sub: SIPCOT Industrial Park, Tindivanam - Environmental Statement for the  
Financial Year ending 31<sup>st</sup> March 2024 - Submitted - Reg.

Ref: SEIAA Lr. No. SEIAA-TN/F.6497/EC/8(b)/681/2019 dated 27.11.2019

\*\*\*\*\*

With reference to the above, we hereby submit the Environmental Statement in Form-V as prescribed under the Environmental (Protection) Rules, 1986 and its subsequent amendment in respect of SIPCOT Industrial Park at Pelakuppam, Venmaniyathoor and Kollar Villages in Tindivanam Taluk, Villupuram District, Tamil Nadu for the Financial Year ending 31<sup>st</sup> March 2024.

Yours faithfully,

DEPUTY GENERAL MANAGER (P-II)

Encl: As above.

**State Industries Promotion Corporation of Tamil Nadu Limited**

(A Government of Tamil Nadu Undertaking)

CIN : U74999TN1971SGC005967

Regd. Office : 19-A, Rukmani Lakshminipathy Road, Post Box No.7223, Egmore, Chennai - 600 008.

Phone : 45261777, Fax : 45261796 Website : www.sipcot.tn.gov.in

## GREENBELT PHOTOGRAPHS







Tindivanam, Tamil Nadu, India  
22, Gingee Rd, Roshanai, Tindivanam, Tamil Nadu  
604001, India  
Lat 12.25017° Long 79.627062°  
24/03/25 10:53 AM GMT +05:30

## STORM DRAIN PHOTOGRAPHS





Venmaniyathur, Tamil Nadu, India  
6jx8+gf, Venmaniyathur, Tamil Nadu 604001, India  
Lat 12.248904° Long 79.61669°  
24/03/25 09:19 AM GMT +05:30



## LED LIGHT PHOTOGRAPHS

